CAPITAL PLANNING PROJECT OVERVIEW REPORT

September 9, 2015

TABLE OF CONTENTS


Capital Pipeline Overview				
Statements of Interest (S	OIs)	3		
Core Program		4-10		
Eligibility P	eriod	4		
Consultant	Selection	5		
Feasibility S	Study	6		
Schematic	Design	7		
Commissio	ning	8		
Design Dev	elopment	9		
Summary c	of Bid Data	9		
Constructio	on	10		
Accelerated Repair Progra	am	11-13		
Project Variances		14-15		
Appendix				
(

(A) Project Status List
(B) 2015 & 2016 Estimated Bid Dates
(C) Construction Status Report

CAPITAL PIPELINE OVERVIEW

Current Projects Status

A total of 306 projects that have received invitations from the Board of Directors ("Board") to collaborate with the MSBA are currently in the MSBA's Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. For a detailed look at the Capital Pipeline projects, please go to <u>www.massschoolbuildings.org/building</u> and select "Capital Pipeline Status Chart".

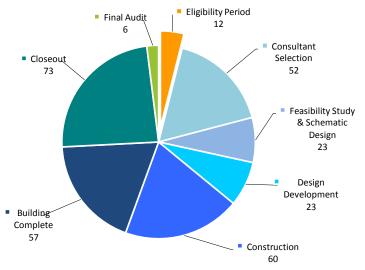

2015 Progress Report

- SOI 2015
 - o 97 Core Program SOIs were received; due diligence is underway.
 - 2015 ARP SOIs were finalized with recommendations for invitation issued for 24 districts representing 44 projects at the June 3, 2015 Board meeting.
- Eligibility Period
 - Collaboration with the remaining 12 districts invited into Eligibility Period is underway.
 Invitations to Feasibility Study are anticipated at the upcoming September, November and January Board meetings.
- Feasibility Study/Schematic Design
 - One district received MSBA approval for selection of an OPM.
 - Two districts completed designer selection.
- Accelerated Repair Program
 - From the 2014 SOI opening, one district with two projects remains for recommendation for a Project Funding Agreement.
 - From the 2015 SOI opening, districts are underway with preliminary requirements. Consultant assignments are anticipated in August/September and Project Funding Agreement recommendations are anticipated in the fall/winter.
- Construction Costs
 - Of the 13 bids and/or executions of a GMP in 2015, eight have been reported to date.
 - Of the eight, six came in within their estimated budget.
- Substantial Completion
 - Of the 24 districts anticipating substantial completion in 2015, 20 have declared substantial completion as of this report.

STATEMENTS OF INTEREST (SOIs)

2015 SOI Process

The 2015 Statement of Interest ("SOI") process opened on Friday, January 9, 2015. The deadline to file a SOI for consideration in the Accelerated Repair Program ("ARP") was Friday, February 13, 2015. Due to inclement weather, the MSBA extended the deadline for ARP printed SOI material and related vote information to Friday, February 17, 2015. As of the deadline, the MSBA received 61 SOIs, submitted by 24 districts for consideration into the Program. Invites into the ARP were concluded at the June 3, 2015 Board of Directors meeting; and 24 districts, representing 44 projects, were invited into the Program.

The deadline to file a SOI for consideration in the Core Program, which is primarily for projects beyond the scope of Accelerated Repair, including extensive repairs, renovations, additions/renovations and new school construction, was Friday, April 10, 2015. As of the deadline, the MSBA received 97 Core Program SOIs. The review process for these SOIs continues with invites into Eligibility Period anticipated at the winter of 2016 Board of Directors meetings.

CORE PROGRAM

Eligibility Period

There are 12 districts in Eligibility Period. Of the 12, four districts have secured funding, while the remaining eight districts have yet to confirm their dates for action.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. All 12 districts have completed their online enrollment projection information. Of the 12 districts, three districts have received their enrollment certifications.

Based upon the schedules anticipated by the districts for completion of Eligibility Period requirements, staff anticipates recommending the districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

	istrict School Date of Invitation to Eligibility Period		30 days	60 days	90 c	lays	180	days	270 days	Date of
District			ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	Invitation to Feasibility Study (Estimated)
Attleboro	Attleboro HS	01/14/15	х	х	х	х	х	х		11/18/15
Bristol County Agricultural RSD	Bristol County Agricultural HS	01/14/15	x	x	x	х	х			11/18/15
Cape Cod RVTSD	Cape Cod RTHS	01/14/15	х	х	х	х	х			10/26/15
Clarksburg	Clarksburg ES	01/14/15	х	х	х	х	х			11/18/15
Fall River	B.M.C. Durfee HS	01/14/15	х		х	х	х			10/26/15
Middleborough	Middleborough HS	01/14/15	х	х	х	х	х			11/18/15
Taunton	James L. Mulcahey ES	01/14/15	х	х	х	х	х	х		9/30/15
Waltham	Waltham HS	01/14/15	х	х	x	х	х	х		9/30/15
Worcester	South High Community School	01/14/15	x	х	x	х	х		x	9/30/15
Easthampton	Maple ES	3/25/15	x	х	х	х	х		x	01/04/16
Everett	George Keverian School	3/25/15	x	х	x	х			x	01/04/16
Lowell	Lowell HS	3/25/15	х	х	x	х	х		x	01/04/16

Consultant Selection

OPM Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). Since the last report, one district has completed its OPM selection as shown shaded in the table below. Currently, there are six districts in the Capital Pipeline that are in the process of procuring an OPM.

District	School	Anticipated Selection
Millis	Clyde F. Brown ES	August 2015
Ipswich	Winthrop ES	September 2015
Saugus	Saugus High School	December 2015
Holyoke	Lt. Elmer J. McMahon ES	TBD
Boston	Boston Arts Academy	TBD
Lynn	Pickering Middle School	TBD
Westport	Westport Middle School	TBD

Designer Selection

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. Since the last report, two districts have completed their Designer selections as shown shaded in the table below. There are currently two districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Amherst	Wildwood ES	July 2015
Somerville	Somerville HS	July 2015
Bourne	James F. Peebles ES	September 2015
Millis	Clyde F. Brown ES	November 2015

For additional information on the selected consultant teams, see Appendix A.

Feasibility Study

Once a district has procured an OPM and Designer, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that seven districts will present their preferred schematic designs to the Board at the upcoming September, November and January Board meetings.

District	School	Anticipated PS Board Date
Dedham	Early Childhood Center	September 30, 2015
Mount Greylock RSD	Mount Greylock RHS	September 30, 2015
Quincy	Sterling MS	November 18, 2015
Braintree	East MS	January 27, 2016
Hanover	Sylvester ES	January 27, 2016
Needham	Hillside ES	January 27, 2016
Stoughton	Stoughton HS	January 27, 2016

Schematic Design

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that 11 districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming September, November and January Board meetings.

District	School	Anticipated PS&B Board Date
Beverly	Briscoe MS	September 30, 2015
Hopkinton	Center School	September 30, 2015
Provincetown	Provincetown Schools (K-8)	September 30, 2015
Carver	Carver ES	November 18, 2015
Narragansett RSD	Templeton Center ES	November 18, 2015
Newton	Cabot ES	November 18, 2015
Billerica	Memorial HS	January 27, 2016
Dedham	Early Childhood Center	January 27, 2016
Granby	West Street ES	January 27, 2016
Minuteman RVTSD	Minuteman Career and Technical HS	January 27, 2016
Mount Greylock RSD	Mount Greylock RHS	January 27, 2016

Commissioning

The MSBA assigns a Commissioning Consultant once a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned additional Commissioning Consultants to four projects presented in the table below. To date, the MSBA has executed 328 Commissioning Consultant contracts, totaling \$23.6 million. To date, 167 contracts have been completed.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Pittsfield	Taconic HS	Core	\$97.76	Strategic Building Solutions	\$192,271
Brookline	Edward Devotion School	Core	\$73.00	Consulting Engineering Services	\$177,128
Woburn	Wyman-Hurld ES	Core	\$30.00	Fitzemeyer & Tocci Associates	\$82,014
New Bedford	Taylor School at Sea Lab	Waitlist	\$7.16	WSP USA	\$79,376

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced	Percent Complete
FY10	31	\$4,231,376	\$4,273,277	100%
FY11	95	\$6,132,890	\$6,034,447	98%
FY12	52	\$4,450,761	\$4,103,243	92%
FY13	55	\$3,364,697	\$2,585,084	77%
FY14	47	\$2,604,062	\$1,348,347	52%
FY15	44	\$2,277,711	\$407,049	18%
FY16	4	\$530,789	\$0	0%

Design Development

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters into the Design Development phase. Currently, there are 23 projects in the Design Development phase with a total estimated construction cost of approximately \$568.9 million: 14 Accelerated Repair projects, one waitlist project, and eight Core Program projects. The eight Core Program projects in Design Development have a total estimated construction cost of approximately \$537.4 million and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
	Middle School Districts	Pittsfield	Brookline (K-8)
	Scituate		Holbrook (PK-12)
	Westborough		Worcester (PK-6)
	Middle/High School Districts		
	Abington		
	Boston (Dearborn MS)		

Summary of Bid Data

Based on the most recent data and schedules provided by the districts, the MSBA anticipates 13 projects will bid in 2015.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget
2015	13	10,370	\$875.4 M	\$692.1 M
2016	5	3,310	\$346.3 M	\$284.2 M
Totals	18	13,680	\$1.22 B	\$976.3 M

Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation.

Anticipated Bids in 2015:

- October Abington (DBB), Chelsea (CMR)
- November Boston (CMR), Holbrook (CMR)
- December Scituate (DBB)

For additional information on each of these projects, see Appendix B.

Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction phase. Currently, there are 60 projects in the Construction phase with a total estimated construction cost of \$988.5 million: 40 Accelerated Repair projects and 20 Core Program projects. This does not include the 57 projects that have reached substantial completion and are currently in the Building Complete phase. The 20 Core Program projects have a total estimated construction cost of \$928.2 million and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Athol-Royalston Regional	Middle School Districts	North Middlesex Regional	Haverhill (K-8)
Gloucester	Chelsea	Plymouth	North Adams (K-7)
Milford	Lynn	Winchester	
Newton	Peabody		
Northborough	Wachusett Regional		
South Hadley			
Westfield*	Middle/High School Districts		
	Georgetown		
	Greenfield		
	Lunenburg		
	Winthrop		

*Note: Westfield, Abner Gibbs Elementary School, stopped construction in December of 2012 due to a preliminary injunction based upon project site status as Article 97 "Protected Land".

For additional information on the construction status for each of these projects, see Appendix C.

ACCELERATED REPAIR PROGRAM

Currently there are a total of 83 districts, representing 172 projects, either active or completed in the Accelerated Repair Program.

Repair Program	Number of Districts	Number of Projects	Total Project Costs	Maximum Facility Grants	Number of Projects Final Audit Approved
2015 Accelerated*	24	44	-	-	0
2014 Accelerated**	34	47	\$108,410,084	\$65,388,035	0
2013 Accelerated	25	45	\$94,349,037	\$54,509,127	5
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	22
Green	93	189	\$366,647,226	\$222,889,214	177

*Totals reflect projects invited into the Accelerated Repair Program as of the August 6, 2015 Board of Directors' Meeting.


**Totals reflect projects approved for Project Funding Agreements as of the August 6, 2015 Board of Directors' Meeting.

2015 Accelerated Repair Program

- Invitations 24 districts, representing 44 projects
 - Scope includes 22 roofs, 26 windows/doors and nine boilers
- · Consultants assigned following submission of pre-requisite documents

2014 Accelerated Repair Program

- Invitations 36 districts, representing 51 projects
- SOI Removal two districts, representing four projects
- Current 2014 ARP projects 34 districts, representing 47 projects
 - Scope includes 20 roofs, 25 windows/doors and 13 boilers
- Approved for Project Funding Agreements 33 districts, representing 45 projects
- The remaining 2014 district, representing two projects, is anticipated for PFA Approval at the September 30, 2015 Board of Directors meeting
- Four districts, representing five projects, required schedule extensions following PFA approval
- 96% of reporting projects bid within estimated budget



2014 ARP Status Chart

2013 Accelerated Repair Program


- Invitations 28 districts, representing 50 projects
- SOI Removals four districts, representing five projects
- Approved for Project Funding Agreements 26 districts, representing 47 projects
- Active Projects 25 districts, representing 45 projects
 - Scope includes 30 roofs, 13 windows/doors and seven boilers
- Total Project Budgets \$94,349,037
- MSBA Total Facilities Grants \$54,509,127
- Four districts, representing seven projects, required schedule extensions following PFA approval
- 82% of projects bid within estimated budget
- Since the last report, projects that have reached substantial completion have increased from 76.6% to 80.8%

2012 Accelerated Repair Program


- Invitations 27 districts, representing 39 projects
- SOI Removals three districts, representing three projects
- Approved Project Funding Agreements 24 districts, representing 36 projects
 - Scope includes 21 roofs, 11 windows/doors and seven boilers
- Total Project Budgets \$63,009,653
- MSBA Total Facilities Grants \$38,267,952
- Five districts, representing nine projects, required schedule extensions following PFA approval
- 86% of projects bid within estimated budget
- Since the last report, projects that have completed Final Audit have increased from 47.2% to 61.1%



The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,214 in MSBA grants. Of the 189 projects, 177 have been approved for final grant payments. All projects that have not been previously approved for final grant payments (12) are substantially complete and require Final Audit.







2012 ARP Status Chart

2014 Accelerated Repair Projects – Construction Estimate vs. 2015-2016 Bid Amount

- Staff has reported previously on the shaded projects. As of this report, staff notes one new project has been out to bid.
- 96% of the 26 reported projects came within the estimated budget
- 11 additional projects are scheduled to be reported prior to the November 18, 2015 Board of Directors meeting
- After the November 18, 2015 Board of Directors meeting, six of the final 10 projects will be bid in 2015.

				Total	\$45,390,060	\$32,513,336	\$12,876,724	-	\$7,892,050
District	School	Scope	Project Type	Bid Date	Construction Estimate **	Bid Amount **	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance *
Quincy	Francis W. Parker MS	Windows/Doors	DBB	Jan-15	\$1,077,920	\$987,000	\$90,920	71.16%	\$64,699
Quincy	Lincoln-Hancock Community School	Windows/Doors	DBB	Jan-15	\$2,075,113	\$1,479,000	\$596,113	71.16%	\$424,194
Sudbury	General Nixon ES	Partial Roof/ Partial Windows / Doors	DBB	Feb-15	\$915,204	\$817,466	\$97,738	36.89%	\$36,056
Lynn	William P. Connery ES	Roof	DBB	Feb-15	\$859,532	\$604,000	\$255,532	78.95%	\$201,743
Lynn	E. J. Harrington ES	Roof	DBB	Feb-15	\$1,505,681	\$1,217,700	\$287,981	78.95%	\$227,361
Worcester	Goodard School of Science and Technology	Windows/Doors	DBB	Feb-15	\$4,634,609	\$3,053,000	\$1,581,609	78.95%	\$1,248,680
Worcester	West Tatnuck School	Windows/Doors	DBB	Feb-15	\$1,997,979	\$1,162,019	\$835,960	78.95%	\$659,990
Worcester	Clark Street Community	Windows/Doors	DBB	Feb-15	\$2,095,791	\$1,465,163	\$630,628	78.95%	\$497,881
Worcester	Union Hill School	Windows/Doors	DBB	Feb-15	\$2,096,895	\$1,618,818	\$478,077	78.95%	\$377,442
Dartmouth	George H. Potter ES	Roof	DBB	Feb-15	\$1,548,538	\$1,283,000	\$265,538	51.84%	\$137,655
Medway	John D. McGovern ES	Windows/Doors	DBB	Feb-15	\$894,675	\$561,886	\$332,789	50.16%	\$166,927
Norwood	Cornelius M. Callahan ES	Boiler	DBB	Mar-15	\$356,939	\$224,171	\$132,768	50.58%	\$67,154
Greenfield	Green River	Roof, Windows, Doors	DBB	Mar-15	\$1,739,286	\$1,005,890	\$733,396	77.47%	\$568,162
Springfield	Kensington Avenue	Windows/Doors	DBB	Mar-15	\$779,500	\$832,500	-\$53,000	80.00%	\$0
Wellesley	Wellesley MS	Windows/Doors	DBB	Mar-15	\$3,827,871	\$2,752,500	\$1,075,371	31.00%	\$333,365
Tyngsborough	Tyngsborough HS	Roof, Boiler	DBB	Mar-15	\$3,282,118	\$1,964,300	\$1,317,818	52.89%	\$696,994
Middleton	Fuller Meadow ES	Partial Roof	DBB	Apr-15	\$1,257,849	\$906,800	\$351,049	46.37%	\$162,781
Northampton	Leeds ES	Partial Roof	DBB	Apr-15	\$540,900	\$401,550	\$139,350	56.26%	\$78,398
Northampton	R. K. Finn Ryan Road School	Partial Roof	DBB	Apr-15	\$851,639	\$501,520	\$350,119	56.26%	\$196,977
North Attleborough	Roosevelt Avenue ES	Boiler	DBB	Apr-15	\$303,623	\$265,667	\$37,956	53.53%	\$20,318
Southern Berkshire RSD	Mount Everett RHS	Roof, Boiler	DBB	Apr-15	\$6,376,974	\$4,806,662	\$1,570,312	39.21%	\$615,719
Leominster	Northwest ES	Roof	DBB	May-15	\$2,693,028	\$1,805,000	\$888,028	71.96%	\$639,025
Tri-County Regional	Tri-County RVTHS	Boiler	DBB	Jun-15	\$729,259	\$494,131	\$235,128	51.42%	\$120,903
Auburn	Auburn MS	Roof, Partial Boiler	DBB	Jun-15	\$1,757,394	\$1,371,393	\$386,001	54.16%	\$209,058
Auburn	Bryn Mawr ES	Roof	DBB	Jun-15	\$671,935	\$578,000	\$93,935	54.16%	\$50,875
South Shore Voc-Tech Regional	South Shore Voc-Tech Regional HS	Boiler	DBB	Aug-15	\$519,808	\$354,200	\$165,608	54.16%	\$89,693

*These numbers are based on preliminary information received from the district and are subject to further review and calculation.

**The construction estimate and bid amount do not include pre-construction services and alternatives.

PROJECT VARIANCES

Core Program – Total Project Budget Update

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 11 projects shaded below at previous Board meetings. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

			Project Fundin	g Agreement	PFA Bid Amen Auc		
District	School	Scop e	Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	Reason for Increase to Total Project Budget
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,374,837	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Burlington	Marshall Simonds MS	Add/ Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical High School	New	\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Lexington	Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
North Reading	North Reading MS/HS	Add/ Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Somerville	East Somerville Community School	Add/ Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District Ioan.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/ Reno	\$28,552,385	\$15,369,712	30,589,078	13.867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Sutton	Sutton MS	Add/ Reno	\$59,945,474	\$29,843,511	TBD*	TBD*	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Weston	Field ES	New	\$31,504,146	\$8,310,510	TBD*	TBD*	District-approved Construction Change Orders exceeded available contingency amount.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	TBD*	TBD*	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Woburn**	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	TBD*	TBD*	The District had completed a project review with its Conservation Commission and an Order of conditions was issued on June 12, 2015. A neighborhood group has appealed this Order and it is now under review by DEP. The District has experienced delays in completing its City Council vote for its appropriation and incurred additional costs.

As of this report, staff notes that two projects have increased their Total Project Budget.

*PFA Bid Amendment has not been developed to calculate a revised Total Facilities Grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but, upon review, may decrease.

**Pending an executed Project Funding Agreement.

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their Project Funding Agreements pending compliance with the following stipulations:

- The district needed to submit a detailed, revised construction timeline showing how the work will be completed at each school; and
- Any costs that may result from the district's requested extension of the construction schedule will be the sole responsibility of the district and are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for windows, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board.

Seven of the 45 2013 Accelerated Repair Projects did not meet their anticipated construction completion dates in 2014. These projects have revised construction schedules and are scheduled to be completed by the beginning of the 2015-2016 school year.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Hamilton-Wenham RSD	Winthrop ES	Windows	9/15/2014	8/13/2015	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2015.
Pathfinder RVTSD	Pathfinder RVTHS	Roof	9/22/2014	8/28/2015	The District fell behind schedule due to local funding issues.
Quincy	Merrymount ES	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Quincy	North Quincy HS	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Quincy	Wollaston ES	Windows	9/22/2014	8/28/2015	The District and its consultants have elected to re-bid the project and complete construction in 2015.
Dighton-Rehoboth RSD	Dighton ES	Roof	8/29/2014	7/31/2015	The District requested that spray-foam insulation be applied during Summer 2015. The spray-foam created an odor that was disruptive to students and staff.
Dighton-Rehoboth RSD	Dighton MS	Roof	8/29/2014	7/31/2015	The District requested that spray-foam insulation be applied during Summer 2015. The spray-foam created an odor that was disruptive to students and staff.

As of this report, staff notes that there is no new activity.

Five of the 47 2014 Accelerated Repair Projects will not meet their anticipated construction completion dates in 2015. These projects have revised construction schedules and are scheduled to be completed by the beginning of the 2015-2016 school year.

Staff has reported previously on the shaded projects. As of this report, staff notes one project has extended its Construction Completion date.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Orleans	Orleans ES	Partial Window/Door	8/25/2015	8/29/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Springfield	John F. Kennedy MS	Window/Door	12/22/2015	10/28/2016	The District and its consultants have determined that the estimated lead time for windows requires construction to be scheduled for 2016.
Brockton	Ashfield MS	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Brockton	Gilmore School	Roof/Boiler	8/31/2015	7/11/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facilities.
Medfield	Ralph Wheelock School	Boiler	1/6/2016	8/31/2016	The District and its consultants have determined that the bidding for construction in 2016 would better serve the project budget and existing facility.

APPENDIX A PROJECT STATUS LIST



Date of Report: 9/9/2015

Total Projects: 306

MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	ОРМ	Designer	CM\GC	Commissioning Consultant
200800010405	Abington	Frolio Middle School	Design Development	Core Program	New Construction	DBB	Knight, Bagge & Anderson Inc.	Ai3 Architects LLC	-	Horizon Engineering Associates, LLP
201300080050	Amherst	Wildwood Elementary	Feasibility Study	Core Program			Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	-
200800090003	Andover	Bancroft Elementary School	Closeout	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.		Skanska USA Building, Inc.	Sebesta Blomberg & Associates, Inc.
201300140405	Ashland	Ashland Middle	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Raymond Design Associates, Inc.	Gibson Roofs, Inc.	Gale Associates, Inc.
201300140010	Ashland	Henry E Warren Elem Assabet Valley Regional	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc. Strategic Building	Raymond Design Associates, Inc. Design Partnership of	MDM Engineering	Gale Associates, Inc. Symmes, Maini & McKee
200908010605	Assabet Valley	Technical High School	Building Complete	Core Program	Repair	DBB	Solutions, LLC Symmes Maini & McKee	Cambridge, Inc. Mount Vernon Group	CTA Construction Co., Inc.	Associates Strategic Building
200906150020	Athol-Royalston	Riverbend School	Construction	Core Program	New Construction	DBB	Associates	Architects, Inc.	Fontaine Brothers, Inc.	Solutions, LLC
201400160505	Attleboro	Attleboro High	Eligibility Period	Core Program			-	- Lamoureux Pagano &	-	-
200800170305	Auburn	Auburn Middle	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc		Fontaine Brothers, Inc.	WSP USA
201400170305	Auburn	Auburn Middle	Construction	Accelerated Repair	Roof, Boiler		Skanska USA Building, Inc		-	Horizon Engineering Associates, LLP Thompson & Lichtner Co., Inc.
201400170010	Auburn	Bryn Mawr	Construction	Accelerated Repair	Roof		Skanska USA Building, Inc		-	Thompson & Lichtner Co., Inc.
200806160505	Ayer-Shirley	Ayer-Shirley Regional Middle/High School	Building Complete	Core Program	Addition / Renovation		Dore and Whittier Architects, Inc.	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	WSP USA
201106160002G	Ayer-Shirley	Page Hilltop School		Green Repair		DBB	-	-	•	-
201300200010	Barnstable	Barnstable United Elementary School	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
201100200005G	Barnstable	West Barnstable Elem	Closeout	Green Repair	Windows / Doors	DBB	PMA Construction Services	-	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201200250009	Bellingham	Clara Macy Elementary		Core Program			-	-	-	- Duildian Englanda
201400250020	Bellingham	South Elem	Design Development		Roof		Atlantic Construction and Management, Inc.	-	-	Building Enclosure Associates, LLC
201100260015G	Belmont	Daniel Butler		Green Repair		DBB	-	-	-	-
200800260035	Belmont	Roger Wellington Elementary School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	Jonathan Levi Architects LLC	Skanska USA Building, Inc.	
200806200505	Berlin-Boylston	Tahanto Regional High School	Building Complete	Core Program	New Construction	DBB	PMA Construction Services	HMFH Architects, Inc.	CTA Construction Co., Inc.	Strategic Building Solutions, LLC
200800300505	Beverly	Beverly High School	Closeout	Core Program	Addition / Renovation	DBB	HEERY	-	CTA Ventures	-
201300300305	Beverly	Briscoe Middle	Schematic Design	Core Program	New Construction		HEERY	Ai3 Architects LLC	-	-
201300310505	Billerica	Billerica Memorial High School	Schematic Design	Core Program	New Construction		KV Associates, Inc.	Perkins+Will	-	-
201508050605	Blackstone Valley Reg	Blackstone Valley	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201206220505	Blackstone-Millville	Blackstone Millville RHS	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	DiMarinisi & Wolfe Architects Urban Designers	-	Gale Associates, Inc.
201306220010	Blackstone-Millville	Millville Elem	Building Complete	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	CBI Consulting Inc.	MDM Engineering	Simpson Gumpertz & Heger Inc.
201500350651	Boston	Dorchester Academy	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201300350546	Boston	Boston Arts Academy	OPM Selection	Core Program			-	-	-	-
201500350052	Boston	Charles Sumner	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350020	Boston	Curley K-8 School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
		,								



Project Status List

201500350072	Boston	David A Ellis	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201500350080	Boston	Donald Mckay	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
200800350415	Boston	Grover Cleveland		Core Program			-			-
201500350415	Boston	Grover Cleveland	OPM Selection	Accelerated Repair	Windows / Doors		-		-	-
201000350074	Boston	Henry Dearborn Middle School	Design Development	Core Program	New Construction	CM@R	Daedalus Projects Inc	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKe Associates
201000350565	Boston	Quincy Upper School	Feasibility Study	Core Program			Skanska USA Building, Inc	HMFH Architects, Inc.	-	-
201500350380	Boston	Young Achievers	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201400360010	Bourne	James F Peebles Elem	Designer Selection	Core Program			Symmes Maini & McKee Associates, Inc.	-	-	-
201300400305	Braintree	East Middle School	Feasibility Study	Core Program			Hill International Company	Miller Dyer Spears Inc.	-	-
201206250320	Bridgewater- Raynham	Bridgewater Middle School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	-	-	CBI Consulting Inc.
201206250050	Bridgewater- Raynham	Laliberte Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201206250020	Bridgewater- Raynham	Merrill Elementary School	Closeout	Accelerated Repair	Roof	DBB	Vertex Construction Services	Raymond Design Associates, Inc.	-	CBI Consulting Inc.
201409100705	Bristol County Agr	Bristol County Agr High	Eligibility Period	Core Program			-	-	-	-
201400440421	Brockton	Ashfield Middle School	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
							Architectural Consulting			Simpson Gumpertz &
201400440080	Brockton	Barrett Russell School	Design Development		Windows / Doors		Group, LLC Architectural Consulting	Tighe & Bond, Inc.	-	Heger Inc. Simpson Gumpertz &
201400440010	Brockton	Brookfield	Construction	Accelerated Repair	Roof		Group, LLC	Tighe & Bond, Inc.	-	Heger Inc.
201400440035	Brockton	Gilmore	Construction	Accelerated Repair	Roof, Boiler		Architectural Consulting Group, LLC	Tighe & Bond, Inc.	-	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
201100460015	Brookline	Edward Devotion	Design Development	Core Program	Addition / Renovation		Anothony Guigli Town Employee	HMFH Architects, Inc.	-	Consulting Engineering Services, LLC
201500400000	Cambridge	Fletcher/Maynard Academy	OPM Selection	Accelerated Repair	Boiler					
201500490090	Cambridge	Kennedy-Longfellow	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201500490040	Cambridge	Kennedy-Longiellow	OPWI Selection	Accelerated Repair	ROOI		- Vertex Construction	- CSS Architects	- Lockheed Window	- Simpson Gumpertz &
201200500012	Canton	Lt Peter M Hansen	Closeout	Accelerated Repair	Windows / Doors	DBB	Services Vertex Construction	Incorporated CSS Architects	Corporations Lockheed Window	Heger Inc. Simpson Gumpertz &
201200500305	Canton	Wm H Galvin Middle	Closeout	Accelerated Repair	Windows / Doors	DBB	Services	Incorporated	Corporations	Heger Inc.
201408150605	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Eligibility Period	Core Program			-	-	-	-
201300520015	Carver	Carver Elementary School	Schematic Design	Core Program	New Construction		PMA Construction Services	HMFH Architects, Inc.	-	-
200800570050	Chelsea	Clark Avenue School	Construction	Core Program	New Construction	CM@R	Pinck & Co., Inc.	HMFH Architects, Inc.	W. T. Rich Company Inc.	Cannon Design
201500610010	Chicopee	Belcher	OPM Selection	Accelerated Repair	Roof		-	-	-	-
	0							Caolo & Bieniek		Symmes, Maini & McKe
200900610021	Chicopee	Chicopee Academy	Building Complete	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Associates, Inc.	Fontaine Brothers, Inc.	Associates
201500610310	Chicopee	Fairview Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201400630010	Clarksburg	Clarksburg Elementary	Eligibility Period	Core Program			-	-	- Turnor Construction	- Stratogic Building
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Building Complete	Core Program	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Turner Construction Company	Strategic Building Solutions, LLC
200800710505	Danvers	Danvers High School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	Bacon Construction Co, Inc.	Turner Facilities Management Solutions
201400720030	Dartmouth	George H Potter	Construction	Accelerated Repair	Roof		Pinck & Co., Inc.	Russo Barr Associates, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
							Construction Monitoring	Knight, Bagge & Anderson,		

Mas	sachusetts School Building A	uthority								Project Status List
2015007400	015 Deerfield	Deerfield Elem	OPM Selection	Accelerated Repair	Roof		-	-	-	-
2013065000	005 Dighton-Rehoboth	Dighton Elementary	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc.	MDM Engineering	Gale Associates, Inc.
2013065003	305 Dighton-Rehoboth	Dighton Middle School	Construction	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Dietz & Company Architects, Inc. Dietz & Company	MDM Engineering	Gale Associates, Inc.
2013065003	310 Dighton-Rehoboth	Dorothy L Beckwith	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Architects, Inc.	Greenwood Industries, Inc.	Gale Associates, Inc.
2011065000	Dighton-Rehoboth	Palmer River		Green Repair		DBB	-	-	-	-
2008007700)10 Douglas	Douglas Elementary	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering Services, LLC
2008007701		Douglas Intermediate Elementary School	Building Complete	Green Repair	Roof, Windows / Doors, Boiler	DBB	HEERY	DiNisco Design Partnership, Limited	CTA Construction Co., Inc.	Consulting Engineering
2008007905	505 Dracut	Dracut Senior High School	Building Complete	Core Program	Addition / Renovation	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	CTA Construction Co., Inc.	RDK Engineers
2010008205	505 Duxbury	Duxbury High School	Building Complete	Core Program	New Construction - Model School	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc.	Dimeo Construction Company	WSP USA
2010008205		East Bridgewater High School	Building Complete	Core Program	New Construction - Model School	DBB	Hill International Company		Fontaine Brothers, Inc.	Foreman Building Commissioning, LP
2014008600		Maple	Eligibility Period	Core Program			-	-	-	-
2013008800	_	Moreau Hall	Building Complete	Accelerated Repair	Roof	DBB	Skanska USA Building, Inc	Baker/Wohl Architects, Inc.	Capeway Roofing Systems, Inc.	Gale Associates, Inc.
2008091307	705 Essex Agr Tech	Essex Agricultural and Technical High School	Building Complete	Core Program	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge Inc.	Gilbane Building Company	Turner Facilities
2014009300		George Keverian School	Eligibility Period	Core Program		onion.	-	-	-	-
2015009403		Hastings Middle	OPM Selection	Accelerated Repair	Roof		-	-	-	-
2014009505		B M C Durfee High	Eligibility Period	Core Program			-	-	•	-
2009009503	315 Fall River	James Madison Morton Middle School	Closeout	Core Program	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Sebesta Blomberg & Associates, Inc.
2014009604	405 Falmouth	Lawrence	Design Development	Accelerated Repair	Windows / Doors		PMA Construction Services	Civitects PC	-	Gale Associates, Inc.
2008009700	016 Fitchburg	Crocker Elementary		Core Program			-	-	-	-
2009010105	505 Franklin	Franklin High School	Building Complete	Core Program	New Construction - Model School	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Consulting Engineering Services, LLC
2014081806	605 Franklin County	Franklin County Tech	Design Development	Accelerated Repair	Windows / Doors		Strategic Building Solutions, LLC	Habeeb & Associates Architects, Inc.	-	CBI Consulting Inc.
2014010300	001 Gardner	Elm Street School	Construction	Accelerated Repair	Windows / Doors, Boiler		Hill International Company	ICON architecture, inc.	-	Fitzemeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
2012010305	505 Gardner	Gardner High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Five Star Building Corp.	Fitzemeyer & Tocci Associates, Inc.
2012010304	405 Gardner	Gardner Middle School	Closeout	Accelerated Repair	Boiler		Leftfield, LLC	Richard D. Kimball Company, Inc.	Royal Steam Heater Co.	Fitzemeyer & Tocci Associates, Inc.
2008010505	505 Georgetown	Georgetown Middle/High School	Construction	Core Program	Renovation	DBB	Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	L.D. Russo, Inc.	WSP USA
2000010000	3010111	Penn Brook Elementary					Municipal Building	Drummey Rosane		Rist-Frost-Shumway
2009010500	010 Georgetown	School	Building Complete	Core Program	New Construction	DBB	Consultants, Inc.	Anderson, Inc.	Brait Builders Corp.	Engineering, P.C.
				Accelerated Repair	Windows / Doors, Boiler		NETCO Construction Project Managers, Inc.	The S/L/A/M Collaborative	-	CBI Consulting Inc.
2014067400	050 Gill-Montague	Sheffield Elementary	Design Development	Accelerated Repair			Knight Bagge 9 Anderson			Eitzomovor & Toooi
2014067400	-	Sheffield Elementary West Parish Elementary School	Design Development Construction	Core Program	New Construction	CM@R	Inc.	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	Fitzemeyer & Tocci Associates, Inc.
	050 Gloucester 010 Granby	West Parish Elementary			New Construction	CM@R	Inc. Strategic Building Solutions, LLC	Inc. Jones Whitsett Architects, Inc.	W. T. Rich Company Inc.	
2009010700	050 Gloucester 010 Granby Greater Lawrence	West Parish Elementary School	Construction Schematic Design	Core Program	New Construction	CM@R DBB	Inc. Strategic Building Solutions, LLC Vertex Construction Services	Inc. Jones Whitsett Architects,	- E. Amanti & Sons, Inc.	Associates, Inc.



201008250605	Greater New Bedford	Greater New Bedford Vocational Technical High School	Building Complete	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Drummey Rosane Anderson, Inc.	Agostini Construction Co., Inc.	Symmes, Maini & McKee Associates
201501140010	Greenfield	Federal	OPM Selection	Accelerated Repair	Roof, Windows / Doors, Boiler		-	-	-	-
201401140030	Greenfield	Green River	Construction	Accelerated Repair	Roof, Windows / Doors, Boiler		Arcadis U.S., Inc.	Baker/Wohl Architects, Inc.		CBI Consulting Inc.
200901140505	Greenfield	Greenfield High School	Construction	Core Program	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	Shawmut Design and Construction	BVH Integrated Services, P.C.
201106730010G	Groton-Dunstable	Florence Roche School		Green Repair		DBB	-	-	-	-
201106730005G	Groton-Dunstable	Swallow/Union School		Green Repair		DBB	- NETCO Construction	- Habeeb & Associates	- Multitemp Mechanical	- Strategic Building
201306750007	Hamilton-Wenham	Bessie Buker Elementary	Final Audit Approved	Accelerated Repair	Boiler Windows / Doors,	DBB	Project Managers, Inc.	Architects, Inc. Habeeb & Associates	Corporation	Solutions, LLC CBI Consulting Inc. Strategic Building
201306750015	Hamilton-Wenham	Winthrop School	Construction	Accelerated Repair	Boiler	DBB	Project Managers, Inc.	Architects, Inc.	E. Amanti & Sons, Inc.	Solutions, LLC
201406800030	Hampden-Wilbraham	Soule Road		Accelerated Repair	Windows / Doors		exPERTcon, Inc.	The S/L/A/M Collaborative	-	-
201406800305	Hampden-Wilbraham	Thornton Burgess		Accelerated Repair	Windows / Doors		-	-	-	-
201406800310	Hampden-Wilbraham	Wilbraham Middle		Accelerated Repair	Roof		exPERTcon, Inc.	The S/L/A/M Collaborative Mount Vernon Group	-	-
201301220015	Hanover	Sylvester	Feasibility Study	Core Program			P3 Inc.	Architects, Inc.	-	-
201101250005G	Harvard	Harvard Elementary		Green Repair		DBB	-	-	-	-
201301270505	Hatfield	Smith Academy	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	1 1	Civitects PC	Silktown Roofing	Building Enclosure Associates, LLC
201201280035	Haverhill	Caleb Dustin Hunking	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	JCJ Architecture, PC	-	Strategic Building Solutions, LLC
201101280100G	Haverhill	Consentino	Closeout	Green Repair	Windows / Doors	DBB	Vertex Construction Services Vertex Construction	CSS Architects Incorporated CSS Architects	New England Builders & Contractors, Inc. New England Builders &	RDK Engineers Russo Barr Associates, Inc. Russo Barr Associates,
201101280085G	Haverhill	John G Whittier	Closeout	Green Repair	Windows / Doors	DBB	Services Vertex Construction	Incorporated CSS Architects	Contractors, Inc.	Inc. Russo Barr Associates,
201101280075G	Haverhill	Tilton	Closeout	Green Repair	Roof	DBB	Services	Incorporated	Titan Roofing, Inc.	Inc.
201101280080G	Haverhill	Walnut Square	Closeout	Green Repair	Roof, Windows / Doors New Construction -	DBB	Vertex Construction Services Knight, Bagge & Anderson	CSS Architects Incorporated	Titan Roofing, Inc.	RDK Engineers Russo Barr Associates, Inc. Foreman Building
201001310410	Hingham	Hingham Middle School	Building Complete	Core Program	Model School	DBB	Inc.	Ai3 Architects LLC	Brait Builders Corp.	Commissioning, LP
200801330505	Holbrook	Holbrook Junior-Senior High School	Design Development	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201401370045	Holyoke	E N White Elem	Schematic Design	Accelerated Repair	Boiler		-	-	-	-
201201370015	Holyoke	Lt Elmer J McMahon Elem	OPM Selection	Core Program			-	-	-	-
201401370025	Holyoke	Morgan Elem	Schematic Design	Accelerated Repair	Boiler		-	-	-	-
201201370605	Holyoke	Wm J Dean Voc Tech High	Building Complete	Science Lab Initiative	Addition / Renovation	DBB	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	RAC Builders, Inc.	BVH Integrated Services, P.C.
201301380010	Hopedale	Memorial	Final Audit Approved	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Civitects PC	MDM Engineering	Simpson Gumpertz & Heger Inc.
201301390005	Hopkinton	Center	Schematic Design	Core Program	New Construction		Compass Project Management, Inc.	Drummey Rosane Anderson, Inc.	-	-
200801410410	Hudson	John F. Kennedy Middle School	Closeout	Core Program	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
201401410007	Hudson	Mulready Elementary	Design Development	Accelerated Repair	Roof		Atlantic Construction and Management, Inc.	-	-	CBI Consulting Inc.
201401440015	lpswich	Winthrop	OPM Selection	Core Program			-	-	-	-
201501510505	Leicester	Leicester High	OPM Selection	Accelerated Repair	Roof		-	-	-	-



					Roof, Windows /					
201501530025	Leominster	Johnny Appleseed	OPM Selection	Accelerated Repair	Doors		-	-	•	-
201401530030	Leominster	Northwest	Construction	Accelerated Repair	Roof		Architectural Consulting Group, LLC	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
201101540005G	Leverett	Leverett Elementary	Closeout	Green Repair	Roof, Windows / Doors	DBB	Potomac Capital Advisors	DiMarinisi & Wolfe Architects Urban Designers	-	Russo Barr Associates, Inc.
201101550010E	Lexington	Joseph Estabrook	Closeout	Core Program	New Construction	CM@R	Hill International Company	DiNisco Design Partnership, Limited	Shawmut Design and Construction	BVH Integrated Services, P.C.
							Joslin, Lesser + Associates			Foreman Building
200801590505	Longmeadow	Longmeadow High School	Closeout	Core Program	New Construction	CM@R	Inc.	OMR Architects, Inc.	Gilbane Building Company	Commissioning, LP
201401600505	Lowell	Lowell High East Street Elementary	Eligibility Period	Core Program			-	-	-	-
201501610010	Ludlow	School	OPM Selection	Accelerated Repair	Roof, Boiler		-			
200801620505	Lunenburg	Lunenburg High School		Core Program						
201001620505	Lunenburg	Lunenburg High School	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	Cannon Design
201001020000	5					_	Diversified Project	Kaestle Boos Associates,		5
201201630405	Lynn	Breed Middle School	Final Audit Approved	Accelerated Repair	Windows / Doors	DBB	Management NETCO Construction	Inc. Habeeb & Associates	GVW, Inc. Capeway Roofing Systems,	CBI Consulting Inc.
201401630045	Lynn	E J Harrington	Construction	Accelerated Repair	Roof		Project Managers, Inc.	Architects, Inc.	Inc.	CBI Consulting Inc.
00400400005	lypp	Lypp Voo Toch Institute	Final Audit Amarau -	Appolorated Densi-	Roof	DBB	Diversified Project	Kaestle Boos Associates,	Cibeen Boofe Inc	CPI Consulting Inc.
201201630605	Lynn	Lynn Voc Tech Institute	Final Audit Approved OPM Selection		Roof	NDD	Management	Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
201401630420	Lynn	Pickering Middle Thurgood Marshall Middle	OPINI Selection	Core Program			- Joslin, Lesser + Associates	- Paymond Dosign	-	- Rist-Frost-Shumway
200901630305	Lynn	School	Construction	Core Program	New Construction	CM@R	Inc. NETCO Construction	Associates, Inc.	Walsh Brothers, Inc.	Engineering, P.C.
201401630040	Lynn	Wm P Connery	Construction	Accelerated Repair	Roof		Project Managers, Inc.	Habeeb & Associates Architects, Inc.	Gibson Roofs, Inc.	CBI Consulting Inc.
200801680020	Marblehead	Glover School	Building Complete	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	JCJ Architecture, PC	G & R Construction, Inc.	RDK Engineers Sebesta Blomberg &
201101710505	Marshfield	Marshfield High	Building Complete	Core Program	New Construction - Model School	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Ventures	Associates, Inc.
201101720035G	Mashpee	Quashnet School	Danang Complete	Green Repair		DBB	-	-	-	-
200801740505	Maynard	Maynard High School	Closeout	Core Program	New Construction	DBB	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	CTA Construction Co., Inc.	WSP USA
201401750007	Medfield	Ralph Wheelock School	Design Development	Accelerated Repair	Boiler		-	-	-	RDK Engineers
201201760505	Medford	Medford High	Building Complete		Addition / Renovation	DBB	Leftfield, LLC	DiNisco Design Partnership, Limited	G & R Construction, Inc.	Cannon Design
201201100000			5		Windows / Doors,		Architectural Consulting	Dietz & Company		Symmes, Maini & McKee
201301760505	Medford	Medford High	Building Complete	Accelerated Repair	Boiler	DBB	Group, LLC	Architects, Inc.	NB Kenney Company, Inc	Associates Russo Barr Associates,
201401770013	Medway	John D Mc Govern Elem	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	CBI Consulting Inc.	-	Inc.
201401780017	Melrose	Herbert Clark Hoover	Design Development	Accelerated Repair	Windows / Doors		Strategic Building Solutions, LLC	ICON architecture, inc.	-	Simpson Gumpertz & Heger Inc.
201201780505	Melrose	Melrose High	Closeout	Science Lab Initiative	Addition / Renovation	DBB	Hill International Company	Ai3 Architects LLC	G & R Construction, Inc.	WSP USA
201101780050	Melrose	Winthrop		Core Program			-	-	-	-
200801810505	Methuen	Methuen High School	Closeout	Core Program	Addition / Renovation	CM@R	KBA/Trident	Finegold Alexander and Associates Inc.	Consigli Construction Company, Inc.	Environmental Health and Engineering
201501820011	Middleborough	Memorial Early Childhood Center	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201401820505	Middleborough	Middleborough High	Eligibility Period	Core Program			-	-		
201401840003	Middleton	Fuller Meadow	Construction	Accelerated Repair	Roof		Hill International Company	CBI Consulting Inc.	-	Building Enclosure Associates, LLC
201101850090	Milford	Woodland	Construction	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	HMFH Architects, Inc.	Shawmut Design and Construction	Consulting Engineering Services, LLC
201401870005	Millis	Clyde F Brown	Designer Selection	Core Program			Compass Project Management, Inc.	-	-	-
200908300605	Minuteman Voc Tech	Minuteman Regional High School	Schematic Design	Core Program			Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-	-



201107129999	Monomoy	Monomoy Regional High School	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Sebesta Blomberg & Associates, Inc.
201307150505	Mount Greylock	Mt Greylock Reg High	Feasibility Study	Core Program			Dore & Whittier Management Partners, Inc.	Design Partnership of Cambridge, Inc.		-
00807200020	Narragansett	Templeton Center School	Schematic Design	Core Program			Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	-	-
01407250025	Nashoba	Florence Sawyer Sch		Accelerated Repair	Boiler		-	-	-	-
00807250015	Nashoba	Pompositticut Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Symmes Maini & McKee Associates, Inc.	P.J. Stella Construction Corp.	Strategic Building Solutions, LLC
01308520605	Nashoba Valley Tech	n Nashoba Valley Tech H S	Building Complete	Accelerated Repair	Roof	DBB	STV Incorporated	CGKV Architects, Inc.	Stanley Roofing Company, Inc.	CBI Consulting Inc.
01101980031G	Natick	Johnson		Green Repair		DBB	-	-	-	-
01306600305	Nauset	Nauset Reg Middle	Closeout	Accelerated Repair	Roof	DBB	Strategic Building Solutions, LLC	ICON architecture, inc.	Capeway Roofing Systems, Inc.	Russo Barr Associate Inc.
01301990035	Needham	Hillside Elementary	Feasibility Study	Core Program			Steven H. Popper Town Employee	Dore & Whittier Architects, Inc.	-	-
01502010063	New Bedford	Alfred J Gomes	OPM Selection	Accelerated Repair	Windows / Doors		-	-		_
	New Bedford	Casmir Pulaski	OPM Selection	· · ·	Windows / Doors,			-	-	<u>.</u>
01502010123				Accelerated Repair	Boiler Windows / Doors,		-	-	-	-
201502010078	New Bedford	Hayden/McFadden	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
01202010115	New Bedford	John Avery Parker		Core Program	Windows / Doors,		-	-	-	-
01502010115	New Bedford	John Avery Parker	OPM Selection	Accelerated Repair	Boiler		-	-	-	-
00902010070	New Bedford	John Hannigan	Approved Project Vote Pending	Core Program	New Construction		Daedalus Projects Inc	Turowski2 Architecture, Inc.	-	-
V201002010505P2	New Bedford	New Bedford High	Building Complete	Waitlist	Repair		Architectural Consulting Group, LLC	Mount Vernon Group Architects, Inc.	Sparks Company, Inc.	-
01502010045	New Bedford	Sgt Wm H Carney Acad	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
V201002019999	New Bedford	Taylor School at the Sea Lab Marine Science Education Center	Design Development	Waitlist			-	-	-	WSP USA
01102040005	Newburyport	Francis T Bresnahan Elem	Building Complete	Core Program	New Construction - Model School	DBB	HEERY	HMFH Architects, Inc.	CTA Construction Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
01002040305	Newburyport	Rupert A. Nock Middle School	Building Complete	Core Program	Addition / Renovation	CM@R	HEERY	Miller Dyer Spears Inc.	Gilbane Building Company	Fitzemeyer & Tocci Associates, Inc.
							Joslin, Lesser + Associates	DiNisco Design	• • •	Fitzemeyer & Tocci
01102070005	Newton	A E Angier	Construction	Core Program	New Construction	CM@R	Inc.	Partnership, Limited	W. T. Rich Company Inc.	Associates, Inc.
01302070025	Newton	Cabot	Schematic Design	Core Program			Joslin, Lesser + Associates Inc.	Partnership, Limited	-	-
00802079999	Newton	Carr School		Core Program			-	-	-	-
00802079998	Newton	Newton Education Center		Core Program			-		-	
		Freeman-Kennedy					Joslin, Lesser + Associates	-		
00802080005	Norfolk	Elementary School	Closeout	Core Program	New Construction	DBB	Inc.	Inc.	Fontaine Brothers, Inc.	WSP USA
00909150705	Norfolk County Agriculture	Norfolk County Agr	Closeout	Core Program	Addition / Renovation	DBB	Compass Project Management, Inc.	Turowski2 Architecture, Inc.	Brait Builders Corp.	Rist-Frost-Shumway Engineering, P.C.
00802090305	North Adams	Silvio O Conte Middle School	Construction	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Jones Whitsett Architects, Inc.	PDS Engineering and Construction, Inc.	Rist-Frost-Shumway Engineering, P.C.
01402120015	North Attleborough	Roosevelt Avenue	Construction	Accelerated Repair	Boiler		Pinck & Co., Inc.	Consulting Engineering Services, LLC	Falite Brothers Inc.	Bard, Rao + Athanas Consulting Engineers LLC
01107350505	North Middlesex	North Middlesex Reg	Construction	Core Program	New Construction	DBB	HEERY	Symmes Maini & McKee Associates, Inc.	_	Horizon Engineering Associates, LLP
01502170003	North Reading	E Ethel Little School	OPM Selection	Accelerated Repair	Roof		-	-	-	-
01002170505	North Reading			Core Program	Addition / Renovation	CM@R	PMA Construction Services	Dore & Whittier Architects, Inc.	Gilbane Building Company	
201402100025	Northampton	Leeds	Construction	Accelerated Repair	Roof		STV Incorporated	Raymond Design Associates, Inc.	-	Russo Barr Associate
	•							Raymond Design	-	Russo Barr Associate
201402100029	Northampton	R. K. Finn Ryan Road	Construction	Accelerated Repair	Roof		STV Incorporated	Associates, Inc.	-	Inc.

200904060705	Northampton-Smith	Smith Vocational and Agricultural High School		Core Program		DBB	_	_	_	_
200904000703		<u> </u>					Strategic Building	Lamoureux Pagano &		Fitzemeyer & Tocci
201102130003	Northborough	Lincoln Street	Construction	Core Program	Addition / Renovation	n DBB	Solutions, LLC	Associates, Inc.	-	Associates, Inc.
200908530605	Northeast Metro Voc	Northeast Metro Reg Voc		Core Program			-	-	-	-
200902180505	Norton	Norton High School	Building Complete	Core Program	Addition / Renovatior	CM@R	Pinck & Co., Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.	Rist-Frost-Shumway Engineering, P.C.
		· · ·						Consulting Engineering		Symmes, Maini & McKee
201402200010	Norwood	Cornelius M Callahan	Construction	Accelerated Repair	Boiler	DDD	PMA Construction Services	Services, LLC	George T. Wilkinson, Inc.	Associates
201102200075G	Norwood	George F. Willett		Green Repair		DBB	-		-	
200802230010	Orange	Dexter Park Dexter Park		Core Program			-	-	-	-
201302230010	Orange	Dexiel Faik		Core Program			- Architectural Consulting	-	•	-
201402240005	Orleans	Orleans Elementary	Design Development	Accelerated Repair	Windows / Doors		Group, LLC	Tighe & Bond, Inc.	-	Gale Associates, Inc.
200802260405	Oxford	Oxford Middle School	Closeout	Core Program	Repair	DBB	Diversified Project Management	CGKV Architects, Inc.	J.J. Cardosi, Inc.	Cannon Design
	Pathfinder Voc Tech	Pathfinder Voc Tech	Construction	Assolated Danait	Roof	DBB	exPERTcon, Inc.	Baker/Wohl Architects, Inc.	Allied Restoration	Building Enclosure Associates, LLC
201308600605	Pathinder voc Tech	Pathinder voc Tech	Construction	Accelerated Repair	RUUI	DBB	experition, inc.	Baker/Wohr Architects, Inc.	Corporation	Associates, LLC
								DiNisco Design	Bacon-Agostini	BVH Integrated
200802290305	Peabody	Higgins Middle School	Construction	Core Program	New Construction	DBB	Daedalus Projects Inc	Partnership, Limited	Construction Joint Venture	
201102290007G	Peabody	John E Burke	Closeout	Green Repair	Roof, Windows / Doors, Boiler	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201402290016	Peabody	John E. McCarthy	Construction	Accelerated Repair	Roof, Windows / Doors		Hill International Company	Civitects PC	-	Thompson & Lichtner Co., Inc.
201402200010	readedy	Peabody Veterans Memorial		/ locororated / topan	20010		This international company			
201502290510	Peabody	High	OPM Selection	Accelerated Repair	Roof		-	-	-	-
201102290027G	Peabody	William A Welch Sr	Closeout	Green Repair	Roof	DBB	Daedalus Projects Inc	LPBA/ Architects, Inc.	-	Sebesta Blomberg & Associates, Inc.
201302310010	Pembroke	Hobomock Elementary	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.	CBI Consulting Inc.
201302310015	Pembroke	North Pembroke Elem	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310013	1 ombrono	Pembroke Community	01000041	/ locororated / topan	11001	000			r dai er riegan een, mei	obi oonoalang no.
201302310305	Pembroke	Middle School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Paul J. Rogan Co., Inc.	CBI Consulting Inc.
201302310505	Pembroke	Pembroke High School	Closeout	Accelerated Repair	Roof	DBB	Pinck & Co., Inc.	The S/L/A/M Collaborative	Greenwood Industries, Inc.	CBI Consulting Inc.
									Ambient Temperature	CBI Consulting Inc. Strategic Building
201307450405	Pentucket	Pentucket Reg Middle	Closeout	Accelerated Repair	Roof, Boiler	DBB	Arcadis U.S., Inc.	CGKV Architects, Inc.	Corporation	Solutions, LLC
201107500007G	Pioneer Valley	Pearl E Rhodes Elem		Green Repair		DBB	-	-	-	-
201002360510	Pittsfield	Taconic High School	Design Development	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drummey Rosane	-	Strategic Building Solutions, LLC
201002300310	T Monord		Design Development	oole Hogiani		owert	okanska oorr ballallig, illo			Rist-Frost-Shumway
201202390515	Plymouth	Plymouth South High	Construction	Core Program	New Construction		Ted Gentry Associates, Inc Atlantic Construction and	Ai3 Architects LLC Raymond Design	-	Engineering, P.C.
201302420505	Provincetown	Provincetown High	Schematic Design	Core Program			Management, Inc.	Associates, Inc.	-	-
201502430020	Quincy	Beechwood Knoll Elem	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-		-	
	· ·				New Construction -		Tishman Construction			Sebesta Blomberg &
200802430315	Quincy	Central Middle School	Closeout	Core Program	Model School	DBB	Corporation of MA	Ai3 Architects LLC	H.V. Collins Co., Inc. Lockheed Window	Associates, Inc. Simpson Gumpertz &
201402430075	Quincy	Francis W Parker	Construction	Accelerated Repair	Windows / Doors		PMA Construction Services	-	Corporations	Heger Inc.
201402430035	Quincy	Lincoln-Hancock Comm Sch	Construction	Accelerated Repair	Windows / Doors		PMA Construction Services	-	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.
201302430060	Quincy	Merrymount	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates	Alpha Contracting Associates, Inc.	Simpson Gumpertz & Heger Inc.
201302430060	Quincy	Merrymount	OPM Selection	Accelerated Repair	Roof	000	-	-	-	-
	· ·					222		Habeeb & Associates		Simpson Gumpertz &
201302430510	Quincy	North Quincy High	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Architects, Inc.	GVW, Inc.	Heger Inc.



							Joslin, Lesser + Associates			
201302430320	Quincy	Reay E Sterling Middle	Feasibility Study	Core Program			Inc.	Ai3 Architects LLC	-	-
201302430110	Quincy	Wollaston School	Construction	Accelerated Repair	Windows / Doors	DBB	Skanska USA Building, Inc	Habeeb & Associates Architects, Inc.	Northeast Energy Control Systems	Simpson Gumpertz & Heger Inc.
201402440018	Randolph	J F Kennedy Elem	Design Development	Accelerated Repair	Windows / Doors		STV Incorporated	Taylor & Burns, Inc.	-	Gale Associates, Inc.
201302440410	Randolph	Randolph Community Middle	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	AAlanco Service Corporation	Consulting Engineering Services, LLC
201302440505	Randolph	Randolph High	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	Taylor & Burns, Inc.	John F. Shea Company, Inc.	Gale Associates, Inc.
201402440505	Randolph	Randolph High	Design Development	Accelerated Repair	Windows / Doors		STV Incorporated	Taylor & Burns, Inc.	-	Gale Associates, Inc.
201502480056	Revere	Garfield Elementary School	OPM Selection	Accelerated Repair	Roof		-	-	-	- Diet Freet Churgurau
201002480035	Revere	Staff Sergeant James J. Hill School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Drummey Rosane Anderson, Inc.	CTA Construction Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
200802510305	Rockland	John W. Rogers Middle School	Closeout	Core Program	New Construction	CM@R	Daedalus Projects Inc	Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
201202530005	Rowe	Rowe Elem	Building Complete	Core Program Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	- KV Associates, Inc.	-	- Gilbane Building Company	- Rist-Frost-Shumway Engineering, P.C.
200902580305G 201002580050G	Salem	Saltonstall School	Closeout	Green Repair	Roof, Windows / Doors, Boiler, Building Envelope	CM@R	KV Associates, Inc.	Reinhardt Associates, Inc.		Rist-Frost-Shumway Engineering, P.C.
2010025000506	Saugus	Belmonte Middle School	Closeout	Core Program	Repair	CM@R	Skanska USA Building, Inc	Fletcher Thompson Architecture Engineering,	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
201202620505	Saugus	Saugus High		Science Lab Initiative	9		-	-	-	-
201402620505	Saugus	Saugus High	OPM Selection	Core Program					-	-
201202640305	Scituate	Gates Intermediate School	Design Development	Core Program	New Construction		Daedalus Projects Inc	Dore & Whittier Architects, Inc.	-	WSP USA
201208710605	Shawsheen Valley Voc Tech	Shawsheen Valley Voc Tech High School	Closeout	Accelerated Repair	Boiler	DBB	Diversified Project Management	Shekar & Associates, Inc.	NB Kenney Company, Inc	Fitzemeyer & Tocci Associates, Inc.
201102690010G	Sherborn	Pine Hill		Green Repair		DBB	-		-	-
201302710005	Shrewsbury	Beal School		Core Program			-	- Lamoureux Pagano &	-	-
200802710305	Shrewsbury So Middlesex Voc	Sherwood Middle School	Closeout	Core Program	New Construction	CM@R	PMA Construction Services	0	Gilbane Building Company	RDK Engineers Russo Barr Associates,
201308290605	Tech Reg	Joseph P Keefe Tech HS	Final Audit Approved	Accelerated Repair	Roof	DBB	PMA Construction Services	Associates, Inc.	Greenwood Industries, Inc.	Inc.
200811119999	Somerset-Berkley	Somerset-Berkley High	Building Complete	Core Program	New Construction - Model School	DBB	Skanska USA Building, Inc	Ai3 Architects LLC	Bacon-Agostini Construction Joint Venture	Horizon Engineering Associates, LLP
200902740111E	Somerville	East Somerville Community School at Cummings	Closeout	Core Program	Renovation	CM@R	PMA Construction Services	, ,	Gilbane Building Company	Foreman Building Commissioning, LP
201302740505	Somerville	Somerville High	Feasibility Study	Core Program			PMA Construction Services		-	-
200902780015	South Hadley	Plains School	Construction	Core Program	New Construction	DBB	Arcadis U.S., Inc.	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Strategic Building Solutions, LLC
201408730605	South Shore Reg Voo Tech	c So Shore Voc Tech High	Design Development	Accelerated Repair	Boiler		exPERTcon, Inc.	Richard D. Kimball Company, Inc.	-	Consulting Engineering Services, LLC
201407650505	Southern Berkshire	Mt Everett Regional	Construction	Accelerated Repair	Roof, Boiler		NETCO Construction Project Managers, Inc.	Dietz & Company Architects, Inc.	Titan Roofing, Inc.	Strategic Building Solutions, LLC
200908760605	Southern Worcester Cty VT	Bay Path Regional Vocational Technical High School	Building Complete	Core Program	Addition / Renovatior	n CM@R	HEERY	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
			• • • • • • • •						· · · · · · · · · · · · · · · · · · ·	• · · · ·

201107660305	Southwick-Tolland	Powder Mill	Building Complete	Core Program	Repair	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
201107660505	Southwick-Tolland	Southwick-Tolland Regional High	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
200807660010	Southwick-Tolland	Woodland Elementary School	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	JCJ Architecture, PC	PDS Engineering and Construction, Inc.	BVH Integrated Services, P.C.
200807670505	Spancar E Brookfield	David Prouty High School		Core Program			Dore and Whittier Architects, Inc.	Design Partnership of Cambridge, Inc.		
01502810350	Springfield	STEM Middle Academy	OPM Selection	Accelerated Repair	Roof		Architects, Inc.	-	-	-
01502810550	opinigheid	Chestnut Accelerated	OT WI Delection	Accelerated Repair	11001		Atlantic Construction and	-		Building Enclosure
01302810310	Springfield	Middle School	Closeout	Accelerated Repair	Roof	DBB	Management, Inc.	CBI Consulting Inc.	J.D. Rivet & Co., Inc.	Associates, LLC
01502810035	Springfield	Daniel B Brunton	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
01102810125E	Springfield	Dryden Memorial	Closeout	Core Program	Addition / Renovation	CM@R	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	
	Continential of	Elias Brookings	Building Complete	Care Dragnom	New Construction	CM@R	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Morganti/Aquadro & Cerruti	BVH Integrated
01102810030E	Springfield	0		Core Program			,	,	Consigli Construction	Foreman Building
20014137	Springfield	Forest Park Middle School	Closeout	Waitlist	Addition / Renovation	CM@R	Arcadis U.S., Inc. Atlantic Construction and	Perkins Eastman	Company, Inc.	Commissioning, LP
1302810530	Springfield	High School/Science-Tech	Closeout	Accelerated Repair	Roof	DBB	Management, Inc.	CBI Consulting Inc.	Kronenberger & Sons Restoration, INc.	Building Enclosure Associates, LLC
01402810328	Springfield	John F Kennedy Middle	Design Development		Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	-	Building Enclosure Associates, LLC
		•							Alpha Contracting	Building Enclosure
1402810110	Springfield	Kensington Avenue	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Gale Associates, Inc.	Associates, Inc.	Associates, LLC
1302810060	Springfield	Margaret C Ells	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Allied Restoration Corporation	Building Enclosure Associates, LLC
1502810155	Springfield	Mary M Walsh	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
1302810355	Springfield	South End Middle School	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	CBI Consulting Inc.	Titan Roofing, Inc.	Building Enclosure Associates, LLC
0902810355	Springfield	Springfield Central High	0.00004	Green Repair		DBB	-		-	-
01202810500	Springfield	Springfield Central High	Building Complete		Addition / Renovation		Leftfield, LLC	DiNisco Design Partnership, Limited	Morganti/Aquadro & Cerruti	Horizon Engineering Associates, LLP
0802819999	Springfield	Springfield Public Day High School		Core Program			-	-	-	-
		Springfield Public Day High		-			Atlantic Construction and			Building Enclosure
1302810550	Springfield	School	Closeout	Accelerated Repair	Roof	DBB	Management, Inc.	CBI Consulting Inc.	-	Associates, LLC
1502810550	Springfield	Springfield Public Day High School	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
0902840405	Stoneham	Stoneham Middle School	Building Complete	Core Program	Addition / Renovation	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Shawmut Design and Construction	RDK Engineers
1302850010	Stoughton	Helen Hansen Elementary	Building Complete	Accelerated Repair	Windows / Doors	DBB		Russo Barr Associates, Inc.	Lockheed Window	Building Enclosure Associates, LLC
		Elementally			Roof, Windows /		Atlantic Construction and			Building Enclosure
01402850025	Stoughton	Joseph H Gibbons	Construction	Accelerated Repair	Doors		Management, Inc.	CGKV Architects, Inc.	-	Associates, LLC
01302850014	Stoughton	Joseph R Dawe Jr Elem	Building Complete	Accelerated Repair	Windows / Doors	DBB	1.7		Lockheed Window Corporations	Building Enclosure Associates, LLC
1202050505	Stoughton	Stoughton High	Feasibility Study	Core Program			Compass Project Management, Inc.	Drummey Rosane Anderson, Inc.	_	_
01302850505	oloughton	otoughton migh	i casibility Study	Sole FloyIdIII			manayement, mu.	Anderson, me.	-	- Building Enclosure
01302850020	Stoughton	West Elementary	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Russo Barr Associates, Inc.	Titan Roofing, Inc.	Associates, LLC
01502850020	Stoughton	West Elementary	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	- Hasiaaa Farsiana '
00802870005	Sturbridge	Burgess Elementary School	Closeout	Core Program	Addition / Renovation	DBB	Lamoureux Pagano & Associates, Inc.	Drummey Rosane Anderson, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
01402880025	Sudbury	General John Nixon Elem	Construction	Accelerated Repair	Roof, Windows / Doors		0.	Baker/Wohl Architects, Inc.	Silktown Roofing	Building Enclosure Associates, LLC
00802900305	Sutton	Sutton Middle School	Building Complete	Core Program	Addition / Renovation	DBB	Strategic Building Solutions, LLC	Flansburgh Associates, Inc.	Brait Builders Corp.	RDK Engineers
01102910010	Swampscott	Hadley	Closeout	Core Program	New Construction	DBB	Hill International Company	Mount Vernon Group Architects, Inc.	-	-
01202920505	Swansea	Joseph Case High		Science Lab Initiative			-	-	-	-
01202920305	Swansea	Joseph Case Jr High		Core Program			-	-	-	-

Project Status List

					D () //: 1 /					
201502930007	Taunton	Edmund Hatch Bennett	OPM Selection	Accelerated Repair	Roof, Windows / Doors		-		-	-
				· · ·	Roof, Windows /					
201502930042	Taunton	Joseph H Martin Mulcahey Elementary	OPM Selection	Accelerated Repair	Doors		-	-	-	-
201402930015	Taunton	School	Eligibility Period	Core Program			-	-	-	-
		Tewksbury Memorial High	0	0 5	New Construction -	866		Symmes Maini & McKee	074.14	Sebesta Blomberg &
200802950505	Tewksbury	School	Closeout	Core Program	Model School	DBB	HEERY Strategic Building	Associates, Inc.	CTA Ventures	Associates, Inc. Fitzemeyer & Tocci
201408780605	Tri County	Tri County Reg Voc Tech	Construction	Accelerated Repair	Boiler		Solutions, LLC	Shekar & Associates, Inc.	-	Associates, Inc.
201403010505	Tyngsborough	Tyngsborough High School	Construction	Accelerated Repair	Roof, Boiler		Municipal Building Consultants, Inc.	CSS Architects Incorporated	Greenwood Industries, Inc.	Strategic Building
201403010303	ryngsborougn	ryngoborougn riigh Concor	Construction	/ looololated / lopali	rtool, Dollor		Conounanto, mo.	moorporated		
200202040505	Uxbridge	Uxbridge High	Final Audit Approved	Coro Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.	Shawmut Design and Construction	Turner Facilities Management Solutions
200803040505	Oxbridge	Oxbridge High	Final Addit Approved	Cole Plogram	New Construction	CIMER	Gary Kaczmarek	Lamoureux Pagano &	Construction	Fitzemeyer & Tocci
200907750305	Wachusett	Mountview Middle School	Construction	Core Program	New Construction	DBB	Town Employee	Associates, Inc.	CTA Construction Co., Inc.	Associates, Inc.
201003050310	Wakefield	Galvin Middle School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Tappe Associates, Inc.	Bond Brothers, Inc.	B2Q Associates, Inc.
201000000010							NETCO Construction	·	Brownord, mor	
201303070015	Walpole	Fisher	Closeout	Accelerated Repair	Roof	DBB	Project Managers, Inc.	ICON architecture, inc.	Rockwell Roofing, Inc.	Gale Associates, Inc.
201103080505G	Waltham	Waltham High School		Green Repair		DBB	-	•	-	•
201403080505	Waltham	Waltham High School John W. Decas Elementary	Eligibility Period	Core Program			-	-	-	-
201503100003	Wareham	School	OPM Selection	Accelerated Repair	Roof, Boiler		-	-	-	-
201103100017	Wareham	Minot Forest		Core Program			-	-	-	-
	Marcham	Warehom Conier Llinh	Classout	Assolated Dansit	Deef	DDD	Lill International Company	Ticks & Dond Inc	Capeway Roofing Systems,	
201303100505	Wareham Watertown	Wareham Senior High Watertown Middle	Closeout OPM Selection	Accelerated Repair Accelerated Repair	Roof Windows / Doors	DBB	Hill International Company	rigne & Bond, Inc.	Inc.	Inc.
201503140305	Watertown	Watertown Middle	OFIN Selection	Accelerated Repair	WIIIdows / Doors		-	-	-	- Russo Barr Associates,
201403150005	Wayland	Claypit Hill School	Design Development	Accelerated Repair	Windows / Doors		Pinck & Co., Inc.	CGKV Architects, Inc.	-	Inc.
200903160015	Webster	Park Avenue Elementary School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Dore & Whittier Architects, Inc.	CTA Construction Co., Inc.	Cannon Design
200303100013	11050101		Ballaring Complete	eere rregram	How concluded	000	This international company	CSS Architects		Carinon Doolgin
201403170305	Wellesley	Wellesley Middle	Construction	Accelerated Repair	Windows / Doors		Arcadis U.S., Inc.	Incorporated	Paul J. Rogan Co., Inc.	Gale Associates, Inc.
200803170505	Wellesley	Wellesley Senior School	Closeout	Core Program	New Construction	CM@R	-	Symmes Maini & McKee Associates, Inc.	-	Rist-Frost-Shumway Engineering, P.C.
200000110000				0			Architectural Consulting	CSS Architects		Russo Barr Associates,
201303180005	Wellfleet	Wellfleet Elementary	Closeout	Accelerated Repair	Roof	DBB	Group, LLC	Incorporated	DDC Construction Inc.	Inc.
201103220005G	West Boylston	Major Edwards Elementary	Closeout	Green Repair	Windows / Doors	DBB	URS Corporation	Reinhardt Associates, Inc.		Cannon Design
201103220505G	West Boylston	West Boylston Jr-Sr High		Green Repair		DBB	-	-	-	•
201503230005	West Bridgewater	Spring Street School	OPM Selection	Accelerated Repair	Roof		-	-	-	-
		West Bridgewater Middle-					Strategic Building	Flansburgh Associates,		
201003230505	West Bridgewater	Senior High School	Building Complete	Core Program	New Construction	DBB	Solutions, LLC	Inc.	CTA Construction Co., Inc.	Cannon Design
		West Springfield High			New Construction -		Strategic Building	Symmes Maini & McKee		Turner Facilities
200903320505	West Springfield	School	Building Complete	Core Program	Model School	DBB	Solutions, LLC	Associates, Inc.	Fontaine Brothers, Inc.	Management Solutions
200002210205	Westborough	Gibbons Middle School	Design Development	Core Program	Repair		HEERY	Habeeb & Associates Architects, Inc.	_	BVH Integrated Services, P.C.
200903210305	**esiborougn	Abner Gibbs Elementary	Baaigii Bavelopiilelit	oore i rogram	New Construction -			Jones Whitsett Architects,		Horizon Engineering
200903250020	Westfield	School	Construction	Core Program	Model School	DBB	Skanska USA Building, Inc		Fontaine Brothers, Inc.	Associates, LLP
201303260025	Westford	Col John Robinson	Construction	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	GTC Construction Management	CBI Consulting Inc.
201303260007	Westford	Day Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Strategic Building Solutions, LLC	Gale Associates, Inc.	J.J. Cardosi, Inc.	CBI Consulting Inc.
_0.000200007		, ,			Roof, Windows /		Atlantic Construction and	CSS Architects	Independent Roofing Co.	Building Enclosure
201303270005	Westhampton	Westhampton Elem School	Closeout	Accelerated Repair	Doors, Boiler	DBB	Management, Inc.	Incorporated	Inc.	Associates, LLC
200903300012	Weston	Field Elementary School	Building Complete	Core Program	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Colantonio, Inc.	Foreman Building Commissioning, LP
201103310305G	Westport	Westport Middle		Green Repair		DBB	-	-	-	-
_011000100000										



201403310305	Westport	Westport Middle	OPM Selection	Core Program			-	-	-	-
201103360080G	Weymouth	William Seach		Green Repair		DBB	KBA Architects	-	-	-
200803400005	Williamsburg	Anne T. Dunphy School	Building Complete	Core Program	Addition / Renovation	DBB	Arcadis U.S., Inc.	Drummey Rosane Anderson, Inc.	Enfield Builders, Inc.	B2Q Associates, Inc.
201203420060	Wilmington	North Intermediate	Closeout	Accelerated Repair	Windows / Doors	DBB	Diversified Project Management	-	-	CBI Consulting Inc.
200903420505	Wilmington	Wilmington High School	Building Complete	Core Program	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
200803449999	Winchester	Parkhurst Elementary School		Core Program			-	-	-	-
201003440505	Winchester	Winchester High School	Construction	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	RDK Engineers
200803460505	Winthrop	Winthrop High School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	,	Gilbane Building Company	WSP USA
201203470060	Woburn	Wyman	Approved Project Vote Pending	Core Program	New Construction		Municipal Building Consultants, Inc.	DiNisco Design Partnership, Limited	-	Fitzemeyer & Tocci Associates, Inc.
201203480052	Worcester	Chandler Magnet	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480055	Worcester	Clark St Community	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480060	Worcester	Columbus Park	Building Complete	Accelerated Repair	Windows / Doors, Boiler	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers Russo Barr Associates, Inc.
201203488099	Worcester	Dr. James Caradonio Center	r Closeout	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers Russo Barr Associates, Inc.
201503480090	Worcester	Flagg Street	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201503480177	Worcester	Francis J McGrath Elem	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201403480100	Worcester	Goddard Sch/Science Tech	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	Lambrian Construction Corp.	Russo Barr Associates, Inc.
201503480115	Worcester	Grafton Street	OPM Selection	Accelerated Repair	Windows / Doors, Boiler		-	-	-	-
201203480140	Worcester	Jacob Hiatt Magnet	Closeout	Accelerated Repair	Boiler	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	CAM HVAC & Construction, Inc.	RDK Engineers
201503480140	Worcester	Jacob Hiatt Magnet	OPM Selection	Accelerated Repair	Windows / Doors		-	-	-	-
201203480145	Worcester	Lake View	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480175	Worcester	May Street	Closeout	Accelerated Repair	Windows / Doors	DBB	Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201203480200	Worcester	Nelson Place	Design Development	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano & Associates, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
201403480520	Worcester	South High Community	Eligibility Period	Core Program			-	-	-	-
201303480230	Worcester	Tatnuck	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
201403480240	Worcester	Union Hill School	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201403480260	Worcester	West Tatnuck	Construction	Accelerated Repair	Windows / Doors		Architectural Consulting Group, LLC	ICON architecture, inc.	J.J. Cardosi, Inc.	Russo Barr Associates, Inc.
201303480225	Worcester	Worcester Arts Magnet Sch	Building Complete	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	The S/L/A/M Collaborative	GVW, Inc.	Russo Barr Associates, Inc.
					D	DDD	Architectural Consulting		O antes et a de Nie true de Jaco	
201303480420	Worcester	Worcester East Middle	Building Complete	Accelerated Repair	Boiler	DBB	Group, LLC	The S/L/A/M Collaborative	Contractor's Network, Inc.	RDK Engineers

APPENDIX B 2015 & 2016 ESTIMATED BID DATES

2015 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.


Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollme	nt Project	Start	Finish	Construct	cNotes	Oct 11.4	Neulas	Deeldd	lan 115	Fab 14 F	May 14 F	A	NA 14 F	1	1.1.14 5	
Classesta	355	Budget \$ 39.6	Mon	Thu 1/8/15	Budget	GMP issued:	Oct '14	Nov '14	Dec '14	Jan '15	Feb '15	Mar '15	Apr '15	May '15	Jun '15	Jul '15	Aug
Gloucester	300	φ 39.0	10/20/14	1110/13	5 \$ 50.0	January	10/20	iloucester -	West Parish ES	1/8							
Milford	985	\$ 60.9		Tue 1/20/15	\$ 48.4	GMP issued: January	11/3		ord - Woodland	1/2	0						
Winthrop	970	\$ 80.2		Thu 4/16/15	\$ 61.9	GMP issued: April				1/12 2/4		op - Winthrop N 25	1S/HS 4/16				
Northborough	270	\$ 25.5	Mon 2/9/15	Fri 5/1/15	\$ 18.2	NTP issued: April				2	-	borough - Linco	In Street ES	5/1			
Georgetown	720	\$ 7.8		Thu 3/12/15	\$ 5.9	NTP issued: March				George 2	/9	orgetown MS/H 3/12 /26					
North Middlesex RSD	870	\$ 89.0	Wed 4/8/15	Thu 5/21/15	\$ 68.8	NTP issued: June						North Mic		North Middl 5/7			
Haverhill	1005	\$ 61.5		Mon 5/18/15	\$ 50.0	GMP issued: May						Have	rhill - Caleb I 4/14	Dustin Hunkin	g MS 3		
Plymouth	1005	\$ 107.8		Wed 7/1/15	\$ 83.8	NTP issued: July								Plymouth	Plymouth So 6/19		
Chelsea	670	\$ 57.3		Tue 10/6/15	\$ 46.0	GMP targeted: September									-,	7/22 🗕	(
Boston	600	\$ 73.5	Mon 8/3/15	Thu 9/17/15	\$ 60.2	GMP targeted: September											oston - /3 🛑
Abington	1115	\$ 96.4	Tue 9/1/15	Thu 10/15/15	\$ 77.2	NTP targeted: December											
Holbrook	1095	\$ 103.0		Mon 11/23/15	\$ 79.8	GMP targeted: November											
Scituate	710	\$ 72.9	Wed 10/21/15	Fri 12/18/15	\$ 61.9 5	NTP targeted: December											
Total	10370	\$ 875.4			\$ 692.1												

Note: Budget values are in millions.

The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

1/15		≥ 3/17 1/22 ⊆	-	\$ 3/31
	2/24	DBB Project	2/21	CMR Project

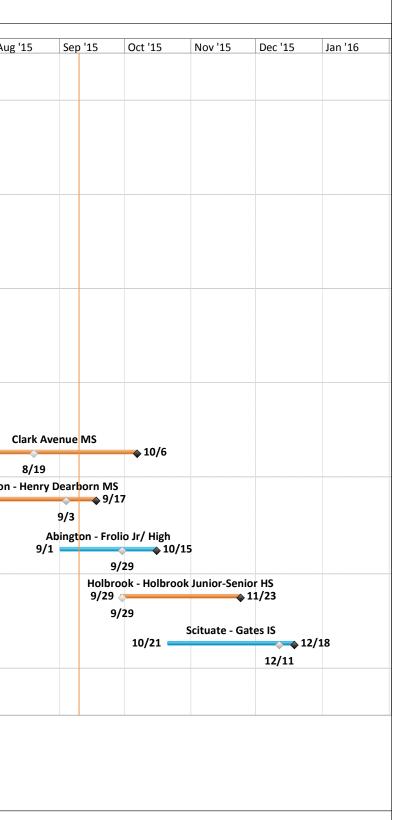

09/09/2015

2016 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

District	Enrollme	ent Project	Start	Finish	Construct	icNotes															
		Budget			Budget		Nov '15	Dec '15	Jan '16	Feb '16	Mar '16	Apr '16	May '16	Jun '16	Jul '16	Aug '16	Sep '16	Oct '16	Nov '16	Dec '16	Jan '17
Worcester	600	\$ 58.2	Wed 12/16/15	Tue 5 4/5/16	\$ 46.5	GMP targeted:		12/16	Worcest	ter - Nelson Plac	•	♦ 4/5									
						April 2016					3/8										
Westborough	550	\$ 26.8	Wed 1/13/16	Thu 2/18/16	\$ 21.6	GMP targeted: February		Ň		Sarah W. Gibbo											
Woburn	410	\$ 31.8	Wed 5/4/16	Thu 6/30/16	\$ 26.2	NTP targeted: July 2016							oburn - Wyma /4	n Elementary 6/10	School 🔷 6/30						
Brookline	830	\$ 113.4	Fri 5/13/16	Thu 6/23/16	\$ 92.2	GMP targeted: August						E	Brookline - Edw 5/13		School 5/23						
Pittsfield	920	\$ 116.1	Thu 6/16/16	Fri 7/29/16	\$ 97.7	GMP targeted: August								Pittsfield - 6/16	Taconic High 7/2						
Total	3310	\$ 346.3			\$ 284.2																

Note: Budget values are in millions. The project start date represents the Filed-Sub bid solicitation date, gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

1/15	*	♦ 3/17	1/22 🥯		\$ 3/31
	2/24	DBB P	roject	2/21	CMR Project

09/09/2015

APPENDIX C CONSTRUCTION STATUS REPORT

Projects in Construction MSBA Grant Basis and Maximum Grant Amount Data Reported as of September 9, 2015

Core F	Program and Waitli	st Totals	\$2,781,946,636														
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	
										CAPITAL PIPE	LINE PROJECTS		TION				
Core Program Totals			\$2,779,970,553						\$12,306								
Assabet Valley Assabet Valley Voc H S	Vocational / Technical	CTA Construction Co., Inc.	\$46,764,740	1,000	Bid	367,565	\$127	\$41,523,764	\$113	Design/Bid/Build	01-Apr-13	31-Aug-15	0	90%	\$3,153,519		This project is a 10-phase major re nearing completion of Phase 10. P scope includes complete renovatio scope also includes lighting, roofin
Athol-Royalston Riverbend	Elementary School	Fontaine Brothers, Inc.	\$35,191,363	545	Bid	95,726	\$368	\$21,101,359	\$220	Design/Bid/Build	08-Dec-14	14-Jun-16	0	19%	\$69,466	0.197%	Site utilities and roadway work are are underway.
Berlin-Boylston Tahanto Reg High	Junior High School	CTA Construction Co., Inc.	\$32,162,000	560	Bid	126,100	\$255	\$24,629,999	\$195	Design/Bid/Build	10-May-11	01-Jul-13	0	99%	\$1,026,723	3.282%	The new school building is in servi repairs.
Chicopee Chicopee Academy	Middle School	Fontaine Brothers, Inc.	\$30,776,990	825	Bid	176,425	\$174	\$21,508,080	\$122	Design/Bid/Build	01-Jul-14	11-Aug-15	0	92%	\$1,730,462	5.623%	Finish work is complete with punch underway. FF&E delivery and insta
Douglas Douglas Elementary	Elementary School	CTA Construction Co., Inc.	\$24,275,111	552	Bid	83,100	\$292	\$19,026,763	\$229	Design/Bid/Build	02-Mar-12	26-Aug-13	0	100%	\$627,104		The new school building is in service
Dracut Dracut Senior High	High School	CTA Construction Co., Inc.	\$45,900,000	1,160	Bid	226,844	\$202	\$38,377,028	\$169	Design/Bid/Build	27-Aug-12	29-Aug-14	0	98%	\$2,224,148	4.846%	All spaces have been turned over t punch list work items are being add
East Bridgewater East Bridgewater High	High School	Fontaine Brothers, Inc.	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/Build	10-Aug-11	25-Jun-13	0	98%	\$2,398,294		Outstanding HVAC issues are beir
Franklin Franklin High	High School	Bacon-Agostini Construction Joint Venture	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$239	Design/Bid/Build	16-Oct-12	25-Jul-14	0	98%	\$1,075,558	1.239%	The new building and parking area sport light poles are near completion
Georgetown Georgetown Middle/High	Junior High School	L.D. Russo, Inc.	\$5,861,090	720	PFA	128,670	\$46	\$3,543,961	\$28	Design/Bid/Build	15-Apr-15	21-Dec-15	0	55%	\$223,809	3.819%	Demolition and abatement are com waterproofing are nearing completi
Georgetown Penn Brook	Elementary School	Brait Builders Corp.	\$32,875,975	770	Bid	98,000	\$335	\$26,976,145	\$275	Design/Bid/Build	26-Sep-13	01-Jun-15	0	95%	\$3,648,277	11.097%	Site work is being completed arour installation is complete. Demolition
Greater Lawrence RVT Gr Lawrence Reg Voc Tech	Vocational / Technical	E. Amanti & Sons, Inc.	\$4,361,641	1,400	Bid	360,000	\$12	\$3,551,593	\$10	Design/Bid/Build	04-Jun-14	12-Dec-14	0	99%	\$260,493	5.972%	Project includes the replacement o top mechanical units, and ventilatio commissioning, training and closed This will be resolved as part of the
Greater New Bedford Gr New Bedford Voc Tech	Vocational / Technical	Agostini Construction Co., Inc.	\$12,181,500	2,060	Bid	487,530	\$25	\$10,757,696	\$22	Design/Bid/Build	13-Sep-13	19-Dec-14	0	100%	\$1,273,194	10.452%	The building is complete and in ser pump replacement and miscellane
Hingham Hingham Middle School	Middle School	Brait Builders Corp.	\$48,436,000	1,020	Bid	176,385	\$275	\$41,227,552	\$234	Design/Bid/Build	07-Jun-12	01-May-14	0	99%	\$714,526	1.492%	Demolition of the existing building i been completed.
Marblehead Glover	Elementary School	G & R Construction, Inc.	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Design/Bid/Build	25-Jun-12	20-Dec-13	0	100%	\$791,625	3.794%	The new school building is complet is planned for the Fall of 2015.
Marshfield Marshfield High	High School	Brait Builders Ventures	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/Build	16-Aug-12	01-Jun-14	0	99%	\$2,144,654	0.000%	Remaining work consists of punch building continues which will be foll
Monomoy Monomoy Regional High School	High School	Fontaine Brothers, Inc.	\$49,374,000	700	Bid	168,000	\$294	\$41,433,695	\$247	Design/Bid/Build	11-Feb-13	02-Sep-14	0	99%	\$1,001,743	2.52%	Remaining punch list items and lar
Newburyport Francis T Bresnahan Elem	Elementary School	CTA Construction Co., Inc.	\$28,190,000	660	PFA	112,517	\$251	\$20,841,757	\$185	Design/Bid/Build	14-Mar-13	19-Aug-14	0	99%	\$1,086,168	3.963%	Punch list work is remaining. The c
North Adams Silvio O Conte Middle	Middle School	PDS Engineering and Construction, Inc.	\$21,877,496	310	Bid	78,119	\$280	\$17,831,491	\$228	Design/Bid/Build	28-Apr-14	22-Jul-15	86 behind	86%	\$935,615		Mechanical, electrical, fire suppres repairs are also ongoing followed b well as millwork finish installation a building. The new roof at the east the playground with concrete formi
North Middlesex North Middlesex Reg	High School	CTA Construction Co., Inc.	\$68,829,726	870	PFA	180,530	\$381	\$44,223,062	\$245	Design/Bid/Build	25-May-15	14-Jul-17	0	3%	\$0	0.000%	Contractor has mobilized. Site wor
Northborough Lincoln Street	Elementary School	Brait Builders Ventures	\$18,450,000	270	PFA	52,920	\$349	\$14,514,966	\$274	Design/Bid/Build	27-Apr-15	01-Sep-16	0	8%	\$0	0.000%	Mechanical, electrical and plumbin
Peabody J Henry Higgins Middle	Middle School	Bacon-Agostini Construction Joint Venture	\$76,735,661	1,340	Bid	227,314	\$338	\$47,562,204	\$209	Design/Bid/Build	10-Mar-14	01-Jul-16	0	42%	(\$580,616)	-0.773%	Foundations, structural steel and c masonry veneer, and AVB (air vap Administration Wings. Masonry co and Gym as well as Administration utility work is ongoing as well as fin electrical rough-ins are underway.
Plymouth Plymouth South High	High School	Bacon-Agostini Construction Joint Venture	\$88,163,542	1,005	PFA	248,081	\$355	\$60,612,309	\$244	Design/Bid/Build	06-Jul-15	05-May-17	0	1%	0%	0.000%	The Contractor has mobilized and
Revere Staff Sergeant James J. Hill School	Elementary School	CTA Construction Co., Inc.	\$33,897,336	690	Bid	103,650	\$327	\$24,309,968	\$235	Design/Bid/Build	25-Mar-14	17-Aug-15	0	97%	\$1,050,055	3.098%	GC is in the process of completing
Somerset-Berkley Somerset-Berkley High	High School	Bacon-Agostini Construction Joint Venture	\$69,407,000	1,000	Bid	222,826	\$311	\$52,553,676	\$236	Design/Bid/Build	16-Jul-12	20-Jun-14	0	99%	\$833,063	1.266%	Exterior work continues with develops school continues in preparation for
South Hadley Plains Elementary	Elementary School	Fontaine Brothers, Inc.	\$21,391,144	270	Bid	63,377	\$338	\$17,380,907	\$274	Design/Bid/Build	08-May-14	04-Sep-15	0	93%	\$988,952	4.623%	Roofing, doors and windows are no ongoing. Site work continues. The
Southwick-Tolland Powder Mill	Middle School	PDS Engineering and Construction, Inc.	\$13,556,194	545	Bid	95,775	\$142	\$11,289,029	\$118	Design/Bid/Build	07-Jun-13	24-Aug-15	0	98%	\$814,281	6.007%	Phase 4 (Classroom Wing 2) is co work ongoing.
Southwick-Tolland Southwick-Tolland Regional High	High School	Fontaine Brothers, Inc.	\$25,307,990	790	Bid	165,995	\$152	\$19,838,420	\$120	Design/Bid/Build	05-Aug-13	3-Sep-15	0	95%	\$2,062,067	8.320%	This is a 5-phase project. Phase 4 Rooms (Phases 5B & 5C) are near connection at the Woodland Element trees, finish paving at the bus loop
Southwick-Tolland Woodland Elementary	Elementary School	PDS Engineering and Construction, Inc.	\$7,172,052	400	Bid	67,800	\$106	\$6,077,790	\$90	Design/Bid/Build	07-Jun-13	24-Aug-15	0	98%	\$700,343	9.765%	Phase 4 of 4 (East Wing) is compl
Sutton Sutton Middle School	Junior High School	Brait Builders Corp.	\$41,230,800	840	PFA	179,040	\$230	\$32,998,403	\$184	Design/Bid/Build	01-Jul-11	05-Mar-15	0	99%	\$1,691,778	4.211%	Remaining punch list and Commiss

*Includes Alternates	\$1,714,013,293
Construction Status	Est Max Total Facilities Grant
	\$1,708,526,854
or renovation. Scope includes multiple building systems, site and ADA upgrades. The project is D. Punch list work for Phases 1-6 is complete and punch list for Phases 7-9 is ongoing. Phase 10 ations to the cafeteria, the remaining vocational spaces and girls' locker rooms. The remaining ofing, HVAC, electrical, ceilings, flooring, windows and site work.	\$28,790,301
are ongoing. The work to export excess site materials is continuing. Foundations and steel erection	\$26,011,620
arvice. The District is working to resolve issues associated with final change orders and rain screen	\$18,733,021
nch list work ongoing. Kitchen equipment is installed. Building commissioning and trainings are nstallation is complete.	\$28,813,458
ervice. Final site work is scheduled for completion during the fall of 2015.	\$16,456,925
ver to the District except the baseball field which is awaiting the Designer's acceptance. Remaining addressed.	\$34,137,202
being addressed and are scheduled to be completed in the near future.	\$40,164,584
reas are complete. Construction of the synthetic field as well as landscaping and installation of the letion.	\$54,558,408
completed. Interior improvements in classrooms, corridors, and Gymnasium continue. Roofing and pletion.	\$3,377,260
round the new building. Commissioning and punch list work are ongoing. FF&E delivery and tion of existing building is underway.	\$18,864,538
nt of cooling towers, chiller plant, HVAC pumps, HVAC controls, domestic hot water heaters, roof lation throughout the shop areas. The only work remaining is the chiller and cooling tower start up, seout. The team is currently investigating a noise level issue with the above ceiling unit heaters. the final commissioning process.	\$2,627,875
service. Replacement of the cooling tower has been completed and is operational. Cooling tower aneous punch list work to be completed in the near future.	\$11,573,133
ng is complete. Landscaping and field installation is complete. Commissioning of the building has	\$23,653,420
plete and in service. Site work is complete and final acceptance inspection of the landscaping work	\$9,316,827
nch list items, system checkouts, and technology interfacing. Demolition of the existing high school followed by final site restoration.	\$46,550,599
landscaping items are being addressed.	\$27,654,507
ne commissioning consultant completed the 10-month walk through for the final commissioning.	\$15,676,427
pression, and plumbing work continue throughout the building. Installation of sheetrock and plaster ad by priming and painting. Ceiling grid installation is underway on the second and third floors as an and window and door trim. Exterior masonry repairs continue on the east and north sides of the ast entry addition and copper flashing throughout are nearing completion. Site work continues for rrming and placing.	\$20,508,670
work and foundations have begun.	\$39,373,276
bing rough installations are progressing throughout the interior of the building.	\$9,925,570
and concrete slabs are currently near completion. Light gauge metal framing, exterior sheathing, vapor barrier) installation are complete in the Academic Wing as well as the Gym and continues in the Music and Auditorium areas. Roofing has been completed for the Academic Wing tion Wing. Window installation has begun and currently in progress in the Administration Wing. Site s final grading for the South Parking Area. Installation of duct work continues. HVAC piping and ay. Drywall has begun in the Academic West Level 3.	\$38,652,137
nd excavation is underway with foundation work to immediately follow.	\$46,241,232
ting work to close out the project including punch list items.	\$28,099,048
velopment of the softball fields, including fencing and seeding. Abatement of the existing high for demolition.	\$46,722,150
e nearly complete. Ceiling and fixture installations as well as painting and interior finishes are The building is scheduled to be open on September 8, 2015.	\$13,676,432
complete and occupied. Phase 5 of 5 (Administration) is complete with final cleaning and punch list	\$8,437,002
e 4A (Alternate Gym) is progressing with the completion of finish work. The Band Room and Locker nearly complete. Roof installation is nearly complete. The new sewer pipe installation to the ementary School entrance is complete. Site work is complete except hydro seeding, landscaping pop and sidewalks.	\$19,572,669
mplete with punch list work ongoing. Classroom modulars have been removed from the site.	\$4,620,410
missioning items are being addressed.	\$26,120,512

Projects in Construction MSBA Grant Basis and Maximum Grant Amount Data Reported as of September 9, 2015

Core F	Program and Waitli	st Totals	\$2,781,946,636														
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	
		-								CAPITAL PIPE	LINE PROJECTS		TION				
Core Program Totals			\$2,779,970,553						\$12,306								
Wachusett Mountview Middle	Middle School	CTA Construction Co., Inc.	\$43,122,257	800	Bid	126,200	\$342	\$28,959,805	\$229	Design/Bid/Build	21-May-14	19-Apr-16	0	49%	\$389,350	0.903%	Site work has been proceeding in road around the new school has b installation is complete at the new the composite wall panels (curtain panels is nearing completion. Cer Classroom painting is ongoing. Ce installed. Installation of mechanic
Webster Park Avenue Elementary	Elementary School	CTA Construction Co., Inc.	\$32,370,001	720	Bid	109,597	\$295	\$24,190,915	\$221	Design/Bid/Build	08-Jul-13	06-Feb-15	0	99%	\$995,064	3.144%	Playgrounds are complete. Rema of the site as well as minor interior
West Bridgewater West Bridgewater Jr-Sr	Junior High School	CTA Construction Co., Inc.	\$46,267,000	625	Bid	141,250	\$328	\$34,404,274	\$244	Design/Bid/Build	01-Oct-13	9-Jul-15	0	88%	\$307,797		The new building has been occupi new building. Remediation of the the new access road and parking
West Springfield West Springfield High	High School	Fontaine Brothers, Inc.	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/Build	22-Nov-11	31-Dec-13	0	99%	\$3,032,663	4.304%	Punch list and field maintenance y
Westfield Abner Gibbs	Elementary School	Fontaine Brothers, Inc.	\$25,578,000	600	Bid	95,573	\$268	\$21,444,000	\$224	Design/Bid/Build	24-Aug-12	01-Jun-16	0	7%	\$0		Work stoppage due to preliminary vacated but city awaiting National The project team is working on clo
Weston Field Elem School	Elementary School	Colantonio, Inc.	\$24,537,966	355	Bid	65,390	\$375	\$19,872,289	\$304	Design/Bid/Build	21-Dec-12	04-Aug-14	0	100%	\$2,141,978	8.729%	Remaining punch list items consis
Williamsburg Anne T Dunphy	Elementary School	Enfield Builders, Inc.	\$8,990,457	170	Bid	37,859	\$237	\$7,625,327	\$201	Design/Bid/Build	05-Apr-13	29-Aug-14	0	100%	\$683,518	7.603%	Miscellaneous punch list work and
Auburn Auburn Middle	Middle School	Fontaine Brothers, Inc.	\$36,412,806	560	Bid	100,395	\$363	\$23,350,958	\$233	CM-at-Risk	27-Feb-14	07-Jul-15	0	98%	\$139,506	0.393%	Project is complete. Minor punch
Ayer-Shirley Ayer-Shirley Regional Middle/High School	High School	Consigli Construction Company, Inc.	\$44,516,576	495	Bid	144,072	\$309	\$32,082,505	\$223	CM-at-Risk	19-Feb-13	31-Aug-15	0	92%	\$1,024,746	2.309%	This is a 6-phase Addition/Renova Phases 1a, 1b, 2a, 2b, 3a and 3b HVAC, electrical, roof, fire protecti
Chelsea Clark Avenue School	Middle School	W. T. Rich Company Inc.	\$46,046,367	670	PFA	115,235	\$400	\$29,311,076	\$254	CM-at-Risk	23-Feb-15	29-Jun-18	0	1%	\$0	0.000%	Interior abatement work and buildi
Concord-Carlisle Concord Carlisle High	High School	Turner Construction Company	\$76,143,704	1,225	Bid	219,871	\$346	\$53,607,000	\$244	CM-at-Risk	20-Feb-13	13-Feb-15	0	95%	\$2,704,713	3.552%	All building systems have been su Although some time was lost due
Duxbury Duxbury High	Junior High School	Dimeo Construction Company	\$105,475,520	1,735	Bid	322,105	\$327	\$73,368,123	\$228	CM-at-Risk	12-Sep-12	09-Jun-14	0	98%	\$6,853,482	6.883%	Site work continues on both forme sidewalks and curbs. Finish gradin
Essex Agr Tech Essex Agr and Tech Inst	Vocational / Technical	Gilbane Building Company	\$110,217,451	1,440	Bid	337,000	\$327	\$79,334,889	\$235	CM-at-Risk	07-May-12	27-Aug-14	0	99%	\$3,018,720	2.739%	Punch list work is nearly complete Fish Barn repairs are complete.
Gloucester West Parish	Elementary School	W. T. Rich Company Inc.	\$29,995,466	355	PFA	65,679	\$457	\$18,591,872	\$283	CM-at-Risk	07-Jul-14	12-May-16	0	55%	\$46,365	0.155%	Academic Wing exterior envelope MEP work are ongoing. Window Wing.
Greater Lowell Voc Tec Gr Lowell Reg Voc Tech	Vocational / Technical	Consigli Construction Company, Inc.	\$52,472,010	1,990	Bid	505,766	\$104	\$38,997,643	\$77	CM-at-Risk	04-Nov-13	31-Aug-15	0	95%	\$2,661,724		This is a 3-phase Addition/Renova February 23, 2015. The new kitch and were utilized by the school at
Greenfield Greenfield High	High School	Shawmut Design and Construction	\$53,507,787	585	Bid	160,650	\$333	\$37,812,150	\$235	CM-at-Risk	27-Mar-13	31-Oct-15	0	90%	\$866,920	1.620%	The new school building is in serv Spring of 2016.
Haverhill Caleb Dustin Hunking	Middle School	Shawmut Design and Construction	\$58,998,100	1,005	PFA	147,996	\$399	\$34,446,742	\$233	CM-at-Risk	20-Apr-15	30-Dec-16	0	8%	\$0	0.000%	Building foundations are complete story mid-section is ongoing. Con
Lunenburg Lunenburg High	Junior High School	Shawmut Design and Construction	\$59,570,728	820	PFA	169,018	\$352	\$39,057,924	\$231	CM-at-Risk	15-Aug-14	25-Mar-16	0	46%	\$88,795	0.149%	Slab-on-grade installation is comp Gym, Auditorium & Locker Room a framing work is also underway. Fla
Lynn Thurgood Marshall Mid	Middle School	Walsh Brothers, Inc.	\$67,725,244	1,100	PFA	181,847	\$372	\$49,913,764	\$274	CM-at-Risk	27-Jun-14	06-Jun-16	0	63%	\$0	0.000%	Site work includes front entrance/ mechanical work, and finish work exterior/interior CMU work and sky
Milford Woodland	Elementary School	Shawmut Design and Construction	\$48,381,844	985	Bid	132,539	\$365	\$31,853,445	\$240	CM-at-Risk	01-Apr-15	28-Jul-16	0	21%	\$21,486		Gym building exterior envelope is is complete. Slab-on-grade and e ongoing. Administration building s grading and pavement are ongoin
Newburyport Rupert A Nock Middle	Middle School	Gilbane Building Company	\$20,877,414	845	PFA	161,500	\$129	\$14,924,391	\$92	CM-at-Risk	18-Mar-13	10-Oct-14	0	99%	\$2,036,392	9.754%	Miscellaneous punch list items are through for the final commissioning
Newton A E Angier	Elementary School	W. T. Rich Company Inc.	\$30,179,957	465	PFA	74,960	\$403	\$16,758,548	\$224	CM-at-Risk	22-Aug-14	18-Dec-15	0	54%	(\$10,570)	-0.040%	Concrete foundations are nearly of progress. Structural steel is comp Air vapor barrier is complete. Exter done except for edge detailing. In protection, electrical and plumbing
North Reading North Reading High	Junior High School	Gilbane Building Company	\$101,328,353	1,370	Bid	267,939	\$378	\$66,726,592	\$249	CM-at-Risk	01-May-12	21-Aug-15	0	94%	\$2,754,052	2.718%	Delivery of furniture is ongoing. La deficiencies identified for correction
Norton Norton High	High School	W. T. Rich Company Inc.	\$27,023,541	700	Bid	162,000	\$167	\$20,590,559	\$127	CM-at-Risk	12-Mar-12	31-Jan-14	0	100%	\$1,366,532	5.131%	Roof top unit punch list issue is or unit noise and vibration issue.

*Includes Alternates	\$1,714,013,293
Construction Status	Est Max Total Facilities Grant
	\$1,708,526,854
in Shrewsbury Street with utility connections, paving and curb restoration to follow. The perimeter s been cut to subgrade and base material placed for paving. Binder installation to follow. Masonry ew Middle School and washing is 50% complete. Insulated metal panel installation is complete and ain walls) are 60% complete overall and complete in the academic building. Installation of precast Ceramic tile is complete, except for grout, in the 3rd floor hall, and about to begin on the 2nd floor. Ceiling grids have been installed in the 3rd floor classrooms. Rooftop HVAC units have been nical/electrical/plumbing rough-ins continues throughout the building.	\$24,279,591
maining items to be completed include miscellaneous landscaping, final paving along the west side	\$28,102,666
rior and exterior punch list items. upied for the start of the new school year. Punch list work items remain to be completed within the he existing building has been completed and demolition began on August 4, 2015. Construction of ng area continues.	\$26,385,058
e work continues. Site warranty issues are being addressed. The commissioning report is	\$60,722,795
ary injunction based upon project site status as Article 97 "Protected Land". Preliminary Injunction al Park Service approval for use of site. The General Contractor has demobilized from the site. closing out the General Contractor's contract.	\$21,281,639
sist of mostly site work.	\$8,004,886
and warranty items continue to be addressed.	\$6,808,088
ch list and seasonal commissioning remain to be completed.	\$19,761,870
ovation project. Two general classroom sections (section C) and the Gym were completed in 2014. 3b are complete and punch list is ongoing. Renovation work throughout the building included action, plumbing, masonry and windows.	\$34,704,031
ilding demolition have been completed (Phase 1).	\$36,093,628
successfully started up and commissioned. Demolition, site work and close out are ongoing. ue to unforeseen abatement scope, the project remains on schedule overall.	\$26,795,748
mer school sites. Light pole bases & poles are being installed along with concrete ading for paving and landscape work are ongoing.	\$48,141,830
ete. The HVAC system has outstanding control issues to be addressed. Farmstead paving and	\$72,471,233
pe is nearly complete. Arts/Gym/Cafeteria Wing exterior envelope is ongoing. Interior framing and w installation is complete on the 3rd and 2nd floors. Roofing has started on the Arts/Gym/Cafeteria	\$14,732,645
ovation project. The addition of the new Cafeteria is complete and was turned over to the District on ichen has also been turned over. The 3rd floor Commons have been converted into science labs at the end of the 2014/2015 school year. The new classrooms that occupy the old Testing space o the Discipline Office have been completed and turned over to the District. Work being completed includes demo, abatement and updating of the toilet rooms, roofing, HVAC, unit ventilators,	\$45,839,013
ervice. Final site work is scheduled for completion in the Fall of 2015 and Final Acceptance in the	\$42,146,257
ete. Structural steel framing for the 3-story wing is complete. Structural steel installation for the 2- concrete slab placements are ongoing. Utility installations have started.	\$39,639,497
mplete. Air vapor barrier and spray fireproofing installations are underway throughout the building. m area masonry installations are complete. Rough mechanical, electrical, plumbing and interior Flat roof installation is nearing completion.	\$34,075,598
ce/side walk preparation and utility preparation/pole relocation. All roof work is complete. VCT tile, ork are underway in Building A with drywall, painting, and ceiling work underway in Building B, and skylight installation underway in Building C. Elevator installation is complete.	\$49,690,902
is nearly complete. Interior CMU block installation has started. Academic building structural steel d elevated slabs are complete. Mechanical, electrical, plumbing rough installations and roofing are g structural steel is complete. Roof deck installation has started. Underground utilities, final bing.	\$27,418,234
are remaining to be completed. The commissioning consultant completed the 10-month walk ning.	\$12,785,667
y complete. Pavement and curbing work are in progress. Exterior and interior masonry are in mplete. Interior drywall and metal framing are complete on Levels 2 and 3 with Level 1 in progress. xterior metal panels are being fabricated. Windows installation will be starting shortly. Roofing is Interior painting, ceiling tile, epoxy flooring and wall tiling are starting on the 3rd floor. Fire ing are roughed in on the 3rd floor. HVAC is in progress.	\$10,839,093
Landscaping and final paving are underway. Local inspections have been performed and ction. Abatement and demolition of the old high school is proceeding.	\$47,071,882
ongoing. The closeout process including the final change orders is pending resolution of a roof top	\$20,634,829

Projects in Construction MSBA Grant Basis and Maximum Grant Amount Data Reported as of September 9, 2015

																1		
Core P	Program and Waitli	st Totals	\$2,781,946,636	i													*Includes Alternates	\$1,714,013,293
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	Proposed Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion	Schedule Variance (days)	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
										CAPITAL PIPE	LINE PROJECTS	IN CONSTRUC	TION					
Core Program Totals			\$2,779,970,553						\$12,306									\$1,708,526,854
Southern Worcester Cty VT Bay Path Reg Voc Tech HS	Vocational / Technical	Consigli Construction Company, Inc.	\$57,024,455	1,110	Bid	249,521	\$229	\$41,468,049	\$166	CM-at-Risk	02-Aug-13	01-Sep-15	0	91%	\$3,056,041	5.395%	Project is currently in Phase 10 of a 10-phase project. Phases 1 and 2, which included a new addition that houses Voc. Shops, Science Rooms, Admin Space and a Restaurant/Kitchen, are complete. Phases 3-7 are complete other than punch list items. Phase 8 was completed at the end of June 2015. Phase 9 & 10 are nearly completed and include work to the shop areas, corridors, and locker rooms.	\$44,420,530
Springfield Elias Brookings	Elementary School	Morganti/Aquadro & Cerruti	\$22,733,394	320	Bid	64,800	\$351	\$18,337,328	\$283	CM-at-Risk	01-Jul-13	12-Feb-15	0	99%	(\$243,295)	-1.070%	6 Remaining punch list and warranty issues are being addressed.	\$25,563,992
Stoneham Stoneham Middle School	Middle School	Shawmut Design and Construction	\$33,086,864	775	Bid	136,410	\$243	\$23,430,771	\$172	CM-at-Risk	01-Nov-12	08-Aug-14	0	100%	\$938,808	2.837%	Miscellaneous punch list work is remaining to be completed.	\$21,346,937
Wakefield Galvin Middle School	Middle School	Bond Brothers, Inc.	\$59,756,584	1,070	Bid	187,773	\$318	\$44,899,853	\$239	CM-at-Risk	18-Mar-13	17-Jul-15	0	94%	\$3,332,485	5.577%	The new school building is in service. Final site work is scheduled for completion in the Fall of 2015 and Final Acceptance in the Spring of 2016.	\$32,519,108
Wilmington Wilmington High	High School	Gilbane Building Company	\$67,558,835	960	Bid	192,443	\$351	\$48,060,314	\$250	CM-at-Risk	30-Apr-13	12-Feb-15	0	88%	\$2,175,598	3.367%	Existing high school building has been demolished and removed. Site work has begun. Punch list items were being completed over the Summer months in the new high school.	\$35,674,893
Winchester Winchester High School	High School	Consigli Construction Company, Inc.	\$101,118,622	1,370	PFA	278,925	\$363	\$60,656,324	\$217	CM-at-Risk	23-Apr-14	31-Aug-17	0	42%	\$998,222	0.989%	Phase 1 construction of a new main entrance, administration offices, music wing, Kitchen, Cafeteria, and Media Center is progressing on schedule for completion and occupancy in September 2015. As a result of the extreme past winter conditions and unforeseen existing conditions, the completion of renovations to the Auditorium have been delayed from September 1, 2015 to October 23, 2015. Construction for Phases 2 and 3 are scheduled for completion in August 2016 and August 2017, respectively.	\$42,106,263
Winthrop Winthrop Sr High	Junior High School	Gilbane Building Company	\$63,542,179	970	PFA	187,917	\$338	\$42,616,843	\$227	CM-at-Risk	01-Jul-14	19-Jul-16	0	36%	\$21,065	0.033%	Structural work has been completed in most of the building. Roofing, framing, fireproofing, window installation and electrical work are in progress. Installation of exterior brick has started.	\$39,559,238
Waitlist Totals			\$1,976,083				\$4		\$4									
New Bedford New Bedford High	High School	Sparks Company, Inc.	\$1,976,083	4,000	PFA	454,028	\$4	\$1,669,516	\$4	Design/Bid/Build	27-Aug-14	06-Mar-15	0	98%	\$126,269	6.390%	6 Miscellaneous punch list items remain to be completed.	\$5,486,439
