
## Project Overview Report March 13, 2013

A total of 332 projects that have received invitations from the Board of Directors ("Board") to collaborate with the MSBA are currently in the MSBA's Eligibility Period and Capital Pipeline. The following summary chart provides the number of projects in the Eligibility Period and each phase of the Capital Pipeline:

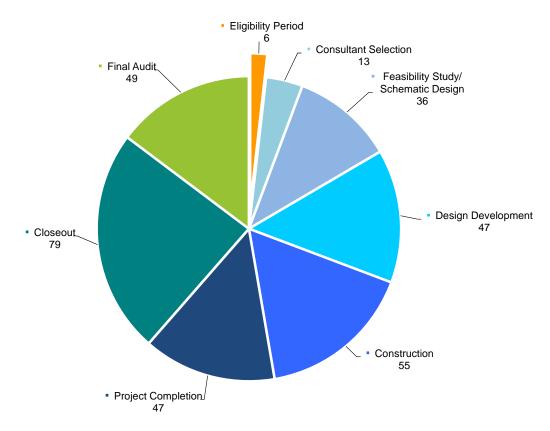

## Statement of Interest ("SOI") Review Status

On January 3, 2013, letters were sent to all Public School Districts in the Commonwealth announcing that the FY 2013 Statement of Interest Process would open on January 9, 2013 and close on April 10, 2013.

- To date 120 Districts have requested User Access to the SOI System
- To date 26 Statements of Interest have been submitted by 13 Districts

#### **Eligibility Period**

There are six districts in the Eligibility Period. One district, Woburn, is seeking local funding and authorization within the next 60 days, and two of the six districts have already secured funding. The remaining three districts have yet to confirm their dates for action.

An agreed-upon enrollment is a key prerequisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA's online enrollment projection tool. Since the last report, one district has completed the enrollment process.

Based upon the schedules anticipated by the districts for completion of the Eligibility Period requirements, staff anticipates recommending the six districts in Eligibility Period for an Invitation to Feasibility Study at upcoming Board meetings.

## **Capital Pipeline**

#### **Consultant Selection**

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an Owner's Project Manager ("OPM"). There are five districts in the Capital Pipeline that need to procure an OPM.

After a district has selected and executed a contract with an OPM, it selects a Designer utilizing either a local designer selection process for projects under \$5 million or the MSBA's Designer Selection Panel ("DSP") for projects over \$5 million. There are eight districts in the Capital Pipeline that are in the process of procuring a Designer.

#### **Feasibility Study**

Once a district has procured an OPM and Designer and a Feasibility Study Agreement has been executed, the district and its consultants must complete two Feasibility Study submittals, the Preliminary Design Program and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that five districts will present their preferred schematic designs to the Board at the upcoming June and July Board meetings.

Prior to consideration by the Board for Project Scope and Budget authorization, a district must submit a schematic design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that five districts will appear before the Board for Project Scope and Budget Agreement authorization at the upcoming June and July Board meetings.

## Commissioning

Since the last report, the MSBA has assigned Commissioning Consultants to an additional 16 projects as presented in the table below. To date, the MSBA has executed 225 Commissioning Consultant contracts, totaling \$17.4 million; 40 contracts have been completed.

District	School	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Greater New Bedford Regional	Greater New Bedford Vocational Technical High School	\$13.70	Symmes, Maini & McKee Associates	\$69,920
Southampton	Norris Elementary School - Accelerated Repair: Roof	\$1.50	Building Enclosure Associates	\$23,500
Norton	Solmonese Elementary School - Accelerated Repair: Roof	\$1.20	Simpson Gumpertz & Heger Inc.	\$35,500
Worcester	Caradonio New Citizens Center, Hiatt Elementary School - Accelerated Repair: Boilers	\$0.66	RDK Engineers	\$16,890
Wayland	-Wayland Middle School - Accelerated Repair: Roof	\$2.45	CBI Consulting Inc.	\$23,150
Old Colony Regional	Old Colony Vocational Technical High School – Roofing and Science Lab Renovation	\$2.18	Consulting Engineering Services, LLC	\$17,900
Leominster	Southeast Elementary School - Accelerated Repair: Roof	\$2.28	Russo Barr Associates, Inc.	\$24,300
Leominster	Southeast Elementary School, Fall Brook Elementary School - Accelerated Repair: Boilers	\$1.82	Horizon Engineering Associates, LLP	\$19,300
Medford	Medford High School – Science Labs	\$10.87	Cannon Design	\$48,800
Springfield	Springfield Central High School – Science Labs	\$25.71	Horizon Engineering Associates, LLP	\$49,800
Attleboro	Studley Elementary School - Accelerated Repair: Roof	\$0.77	CBI Consulting Inc.	\$22,150
Blackstone - Millville Regional	Malone Elementary School, Kennedy Elementary School and Blackstone-Millville Regional High School - Accelerated Repair: Roofs	\$6.98	Gale Associates, Inc.	\$87,810
Quaboag Regional	Warren Elementary School - Accelerated Repair: Boilers	\$0.21	Strategic Building Solutions, LLC	\$9,931
Taunton	Galligan Elementary School- Accelerated Repair: Roof	\$0.54	Gale Associates, Inc.	\$23,370
Worcester	4 Schools - Accelerated Repair: Windows	\$7.32	Russo Barr Associates, Inc.	\$100,550
Greater Lowell Regional	Greater Lowell Technical High School	\$53.10	Horizon Engineering Associates, LLP	\$170,800

Total \$131.28 million Total \$743,671

## **Design Development**

Once a district has secured local funding and has entered into a Project Funding Agreement with the MSBA, it enters the Design Development phase. Currently, there are 47 projects in the Design Development phase with a total estimated construction cost of \$737.1 million: 23 Accelerated Repair projects, six Science Lab Initiative projects, and 18 Core Program projects. The 18 Core Program projects in Design Development have a total estimated construction cost of \$649.9 million:

#### **Elementary School Districts**

Georgetown Newburyport (Bresnahan) South Hadley Webster Williamsburg

#### **Middle School Districts**

Newburyport (Nock) Stoneham Springfield (Brookings) Wakefield

#### **High School Districts**

Assabet Valley Regional Technical
Ayer Shirley Regional
Greater Lowell Regional Technical
Greater New Bedford Regional Technical
Greenfield
Old Colony Regional Technical
Southern Worcester Regional Technical
Southwick-Tolland-Granville Regional
West Bridgewater

#### Construction

When a district issues a Notice to Proceed, the project is advanced to the Construction Phase. Currently, there are 102 projects in the Construction phase with a total estimated construction cost of \$3 billion: 36 Green Repair projects, one Accelerated Repair project, one Science Lab Initiative project, 61 Core Program projects, and three Waitlist projects. The 61 Core Program projects have a total estimated construction cost of \$2.63 billion and are listed below.

## **Elementary School Districts**

# Middle and Middle/High School Districts

## **High School Districts**

Andover
Arlington
Ashburnham-Westminster Regional
Billerica
Brookline (Heath)
Brookline (Runkle)
Douglas
Fairhaven
Lexington

Fairhaven
Lexington
Marblehead
Nashoba Regional
Norfolk
Somerville
Springfield (Dryden)

Sturbridge Westfield Weston Winchester Adams-Cheshire Regional
Burlington
Douglas
Fall River
Hingham
Hudson
Medway
North Reading
Oxford

North Reading
Oxford
Quincy
Rockland
Saugus
Shrewsbury
Sutton

## Addition/Renovation

Danvers
Dracut
Leominster
Lynnfield
Methuen
Norfolk County Agricultural
Norton
Southeastern Regional Voc/Tech

#### New

Berlin-Boylston Regional
Concord-Carlisle Regional
Easthampton
Essex/North Shore Regional Voc/Tech
Grafton
Longmeadow
Maynard
Southbridge
Uxbridge

#### Model

Wilmington

Duxbury
East Bridgewater
Franklin
Hampden-Wilbraham Regional
Marshfield
Monomoy Regional
Natick
Plymouth
Somerset-Berkley Regional
Tewksbury
West Springfield

### **Core Program – Total Project Budget Update**

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the grants authorized by the Board, five projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please also note that staff reported on the budget increases for the three projects shaded below at previous Board meetings.


			Project Fundi	ing Agreement	PFA Bid A	mendment	
District	School Name	Scope	Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	Reason for Increase to Total Project Budget
				Core	Program		
Andover	Bancroft Elementary School	New	\$44,659,837	\$16,773,753	\$50,374,837	IRD*	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Essex North Shore Agricultural & Technical School	Essex North Shore Agricultural & Technical School District	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAM.
Lexington	Estabrook Elementary School	New	\$40,792,248	\$12,250,739	\$42,554,862	TBD*	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District is currently reviewing its project budget to determine the use of the additional appropriation funds it appropriated in excess of the Total Project Budget.
Somerville	East Somerville Community School	Add/ Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Uxbridge	Uxbridge Uxbridge High School		\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.

<sup>\*</sup>PFA Bid Amendment has not been developed to calculate a revised total facilities grant amount. The Total Maximum Facilities Grant will not exceed the Board authorized amount in the PFA but upon review may decrease.

Further, MSBA staff note that two additional districts (North Reading and Stoneham) have reported construction costs higher than their project estimates. Staff is awaiting information from the districts and will provide updates to the Board as they become available.

## **Status of Green Repair Program**

169 projects participating in the Green Repair Program have received authorization to enter into a PFA, totaling \$366,647,226 in Total Project Costs and \$222,885,258 in MSBA grants.

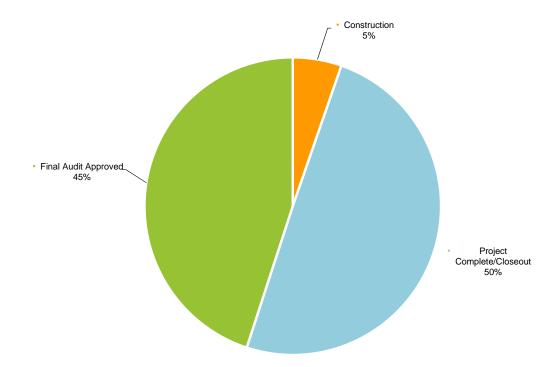

## **Green Repair - Schedule Extension Update**

Eight of the 169 Green Repair Projects did not meet their anticipated construction completion deadline in 2012. Schedule delays can be attributed to bid protests, lead time for windows, and construction delays on site.

The MSBA granted each district a conditional extension to its Project Funding Agreement pending compliance with the following stipulations:

- o The district must submit a detailed, revised construction timeline showing how the work will be completed at each school by no later than August 30, 2013;
- o An Amendment to the Project Funding Agreement between the MSBA and the district must be executed to include the updated project schedule; and
- Any costs that may result from the district's requested extension of the construction schedule
  will be the sole responsibility of the district and are categorically ineligible for reimbursement by
  the MSBA.

Each of these projects has a revised construction schedule and will be complete by the beginning of the 2013-2014 school year. In no event has the extended schedule resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please note that staff reported on the schedule extensions for the six projects shaded below at previous Board meetings:

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Brockton	Brockton High School	Windows and Roof	31-Dec-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building. The roof work is complete.
Haverhill	Consentino Middle School	Windows and Boiler	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline. The boiler project is complete.
Haverhill	John G. Whittier Middle School	Windows	31-Dec-12	31-May-13	Bid protests and lead times caused the window project to extend beyond the 2012 construction deadline.
Lowell	Moody Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Lowell	Washington Elementary School	Windows	15-Aug-12	30-Aug-13	Construction fell behind schedule and the District did not want work being done in an occupied building.
Shrewsbury	Spring Street Elementary School	Roof and Windows	24-Dec-12	31-Jan-13	The district issued a change order to add shrouds over the window wall unit ventilators.
Wachusett Regional	Thomas Prince Elementary School	Roof	23-Mar-12	30-Apr-13	The district issued a change order to replace an existing skylight and due to lead times the work cannot be done until the spring of 2013.
Westport	Westport High School	Roof	4-Sep-12	30-Apr-13	The district issued a change order to add scuppers to the roof and the work will be completed in the spring of 2013.


## **Green Repair - Total Project Budget Update**

Upon receiving the Board's approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement that establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Of the 169 grants authorized by the Board for the Green Repair Program, 15 projects have increased their Total Project Budgets due to acceptance of construction bids higher than the project estimates, or as a result of change orders issued on the project. In no event has the increase in budget resulted in an increase to the Estimated Maximum Total Facilities Grant as authorized by the Board. Please also note that staff reported on the budget increases for 11 of the projects shaded and shown below at previous Board meetings (Arlington; Brockton - Hancock Elementary School and West Junior High School; Fitchburg; Florida; Hancock; Lexington; Narragansett Regional; Pentucket Regional; Reading and Westfield).

			Project Fundi	ng Agreement	PFA Bid A	mendment	
District	School Name	Scope	Total Project Budget	Total Maximum Facilities Grant	Total Project Budget	Total Maximum Facilities Grant	Reason for Increase to Total Project Budget
				Green Re	pair Progra	m	
Arlington	M. Norcross Stratton Elementary School	Roof, Window, Boiler	\$2,445,395	\$739,336	\$2,445,395	\$739,336	Change Orders exhausted the construction contingency.
Boston	Excel High School	Roof	\$1,227,180	\$908,850	\$1,454,735	\$908,850	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	Hancock Elementary School	Roof	\$2,292,164	\$1,814,937	\$2,422,742	\$1,814,937	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Brockton	West Junior High School	Roof	\$2,742,386	\$2,171,001	\$3,069,905	\$2,171,001	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Fitchburg	South Street Elementary School	Boiler	\$701,186	\$560,949	\$705,391	\$501,079	Change Orders exhausted the construction contingency.
Florida	Gabriel Abbott Memorial School	Roof	\$380,310	\$213,172	\$389,422	\$188,804	Project included \$80,153 in Change Orders that offset bid savings and exhausted the construction contingency.
Hancock	Hancock Elementary School	Roof/ HVAC	\$277,450	\$125,740	\$400,805	\$125,740	District elected to accept the base bids in Phases 2 and 3 that were higher than the approved budget. District needs to appropriate the overage.
Lexington	Lexington High School	Roof	\$1,122,890	\$381,221	\$1,197,444	\$381,221	District elected to accept base bid and alternates. District appropriated additional funds to support overage.
Narragansett Regional	Phillipston Memorial Elementary School	Boiler	\$143,225	\$85,712	\$161,232	\$83,275	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
North Attleborough	Falls Elementary School	Windows	\$701,263	\$361,433	\$710,000	\$348,948	District elected to accept the base bid that was higher than the approved budget. District's original appropriation was for \$710,000; therefore the overage was covered.
Peabody	John E. Burke Elementary School	Roof, Window, Boiler	\$2,909,873	\$1,452,745	\$3,473,534	\$1,431,417	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Peabody	William A. Welch Elementary School	Roof	\$1,280,511	\$646,728	\$1,437,800	\$630,732	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Pentucket Regional	Dr. John C.Page Elementary School	Roof, Window, Boiler	\$3,148,424	\$1,618,920	\$3,272,630	\$1,618,920	District elected to accept the base bid that was higher than the approved budget. District appropriated additional funds to support overage.
Reading	Birch Meadow Elementary School	Window	\$735,846	\$347,393	\$787,640	\$347,393	District elected to accept the base bid that was higher than the approved budget. Town Accountant certified that the FY2011 School Committee Operating Budget had an appropriation and encumbrance for the additional costs of the project.
Westfield	Westfield Vocational Technical High School	Roof, Window, Boiler	\$8,442,762	\$5,296,989	\$8,895,495	\$5,296,989	District elected to accept the base bid that was higher than the approved budget. District also approved an amendment to its Designer contract which increased the fee. District appropriated additional funds to support overage.


## **Status of Accelerated Repair Program**


Currently there are a total of 24 districts, representing 36 projects, in the Accelerated Repair Program. All projects are under contract with consultants and have advanced into the Preferred Schematic or Project Scope and Budget Phases. At the April 3, 2013 meeting of the Board of Directors, MSBA staff will recommend a Project Funding Agreement ("PFA") with two districts, representing five projects totaling \$8,783,112 in Total Project Costs. With the Board's approval, 36 projects will have been authorized to enter into a PFA, totaling \$63,009,653 in Total Project Costs and a maximum of \$38,267,952 in MSBA Total Facilities Grant funding.

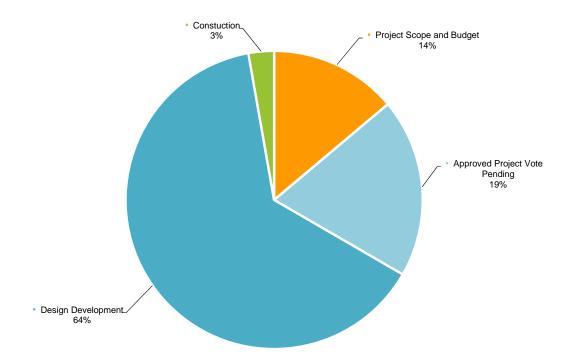

Of the 36 projects, 29 are scheduled to complete construction in 2013, and 7 are scheduled to complete construction in 2014.

## 2012-2013 Eligibility Period Status

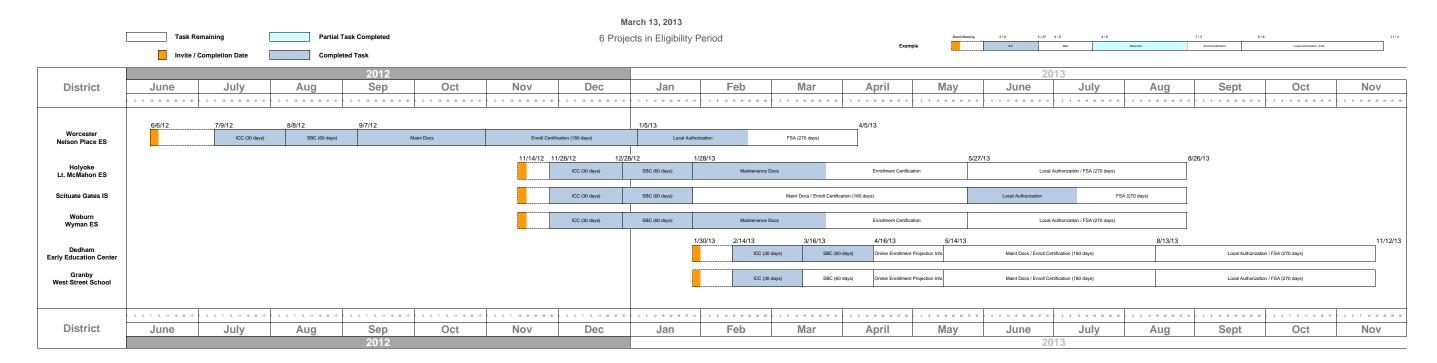


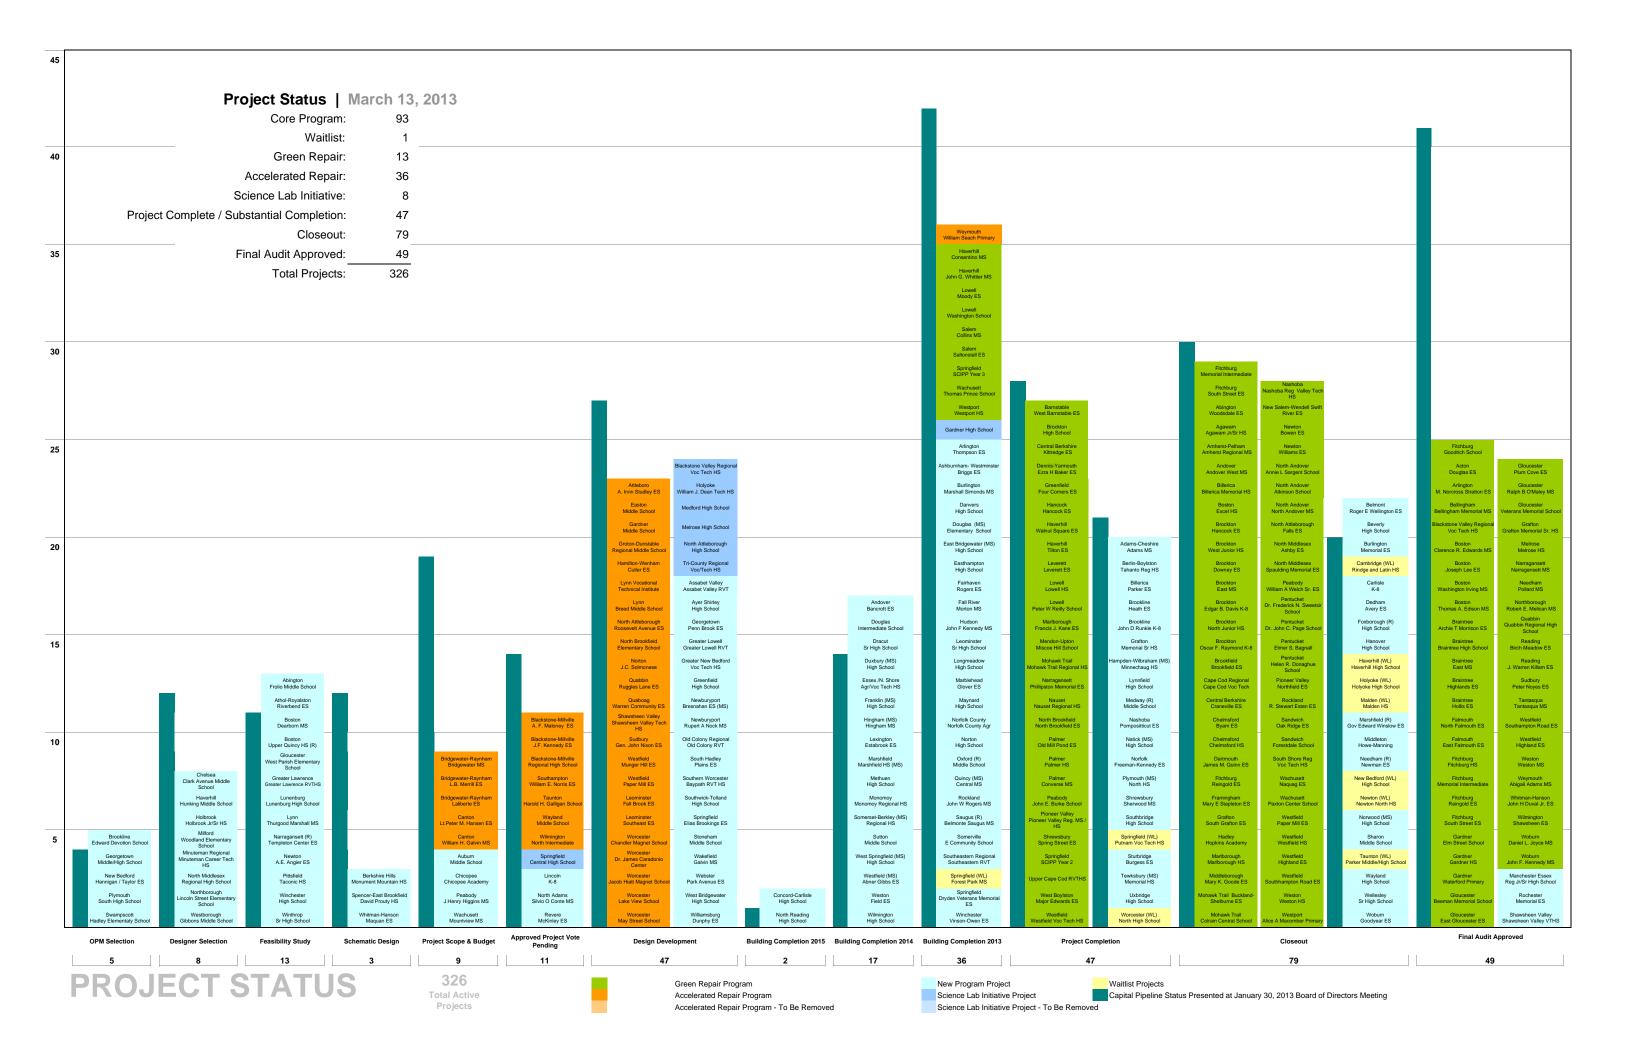


#### 2013 Estimated Bid Dates

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

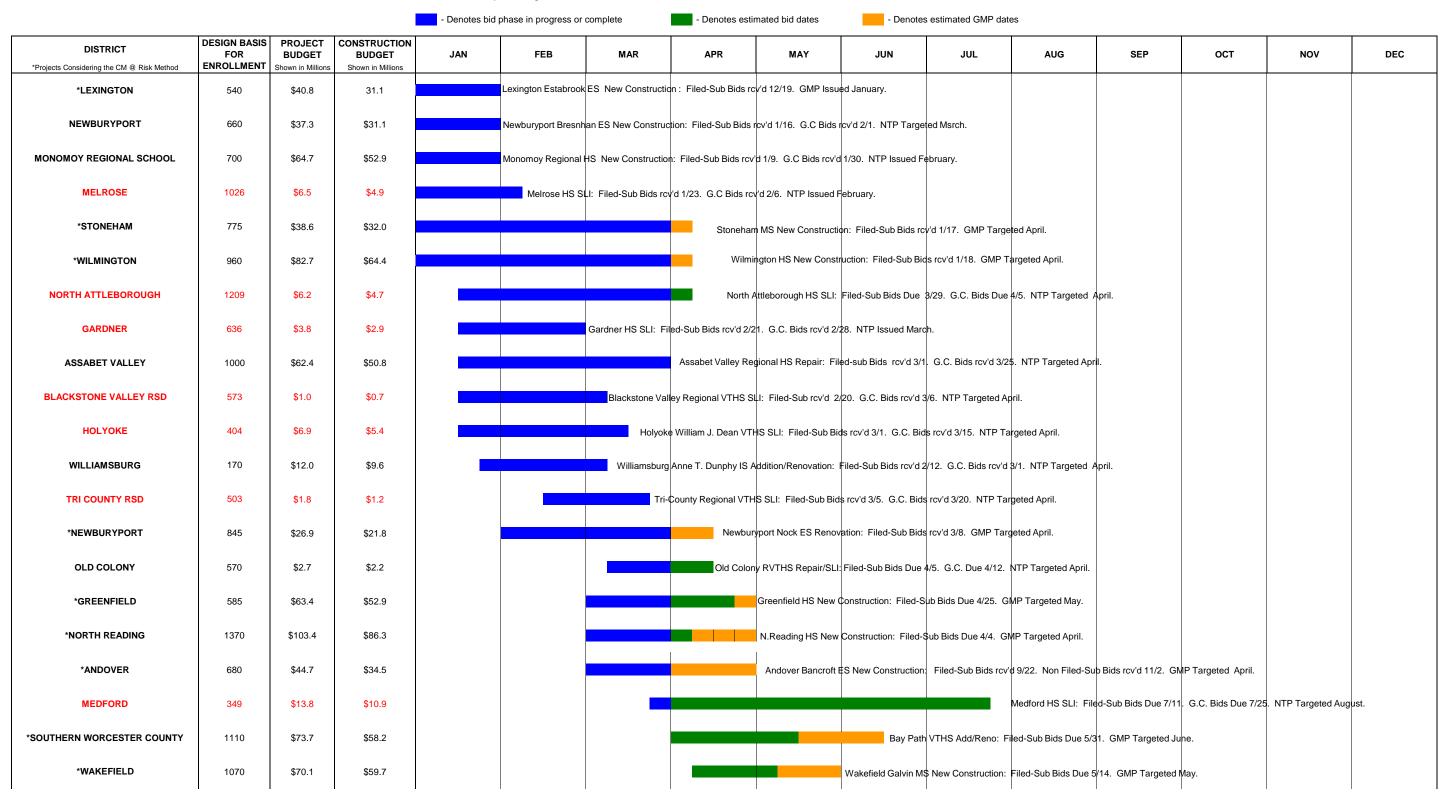

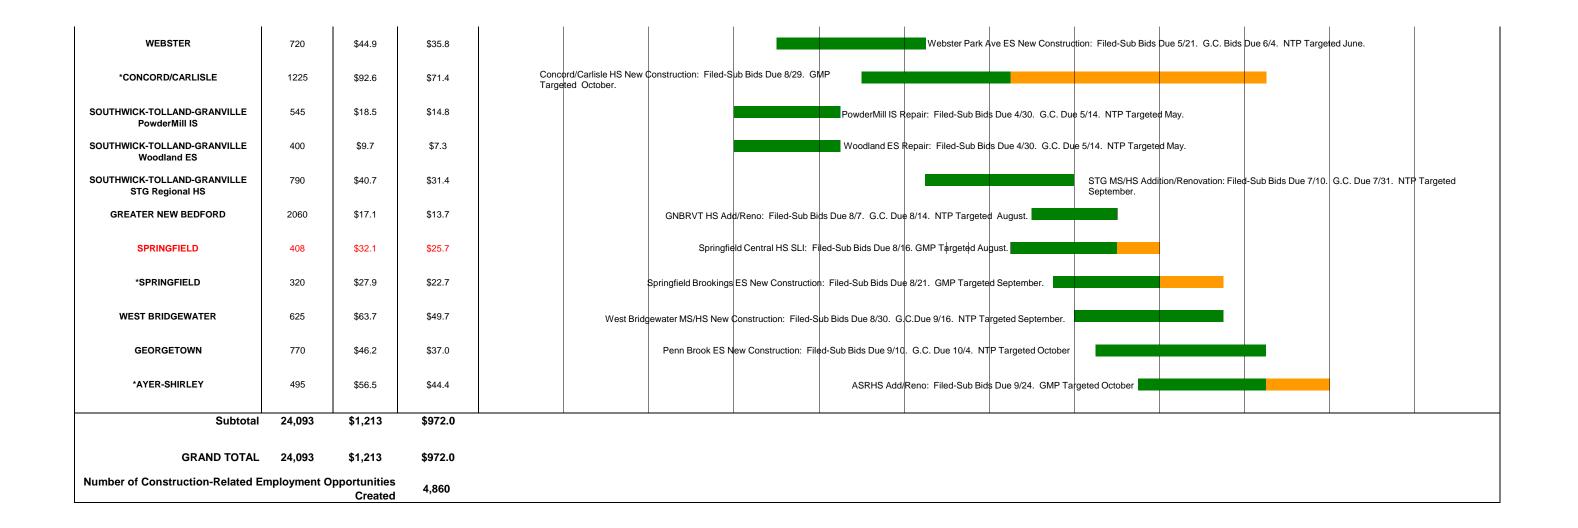


2

January 9, 2013

## **2014 Estimated Bid Dates**

Note bid dates are **Estimates ONLY**. Please contact Districts for exact information.

Total Project Budget denotes total District costs and does not denote the basis of the MSBA Total Facilities Grant.

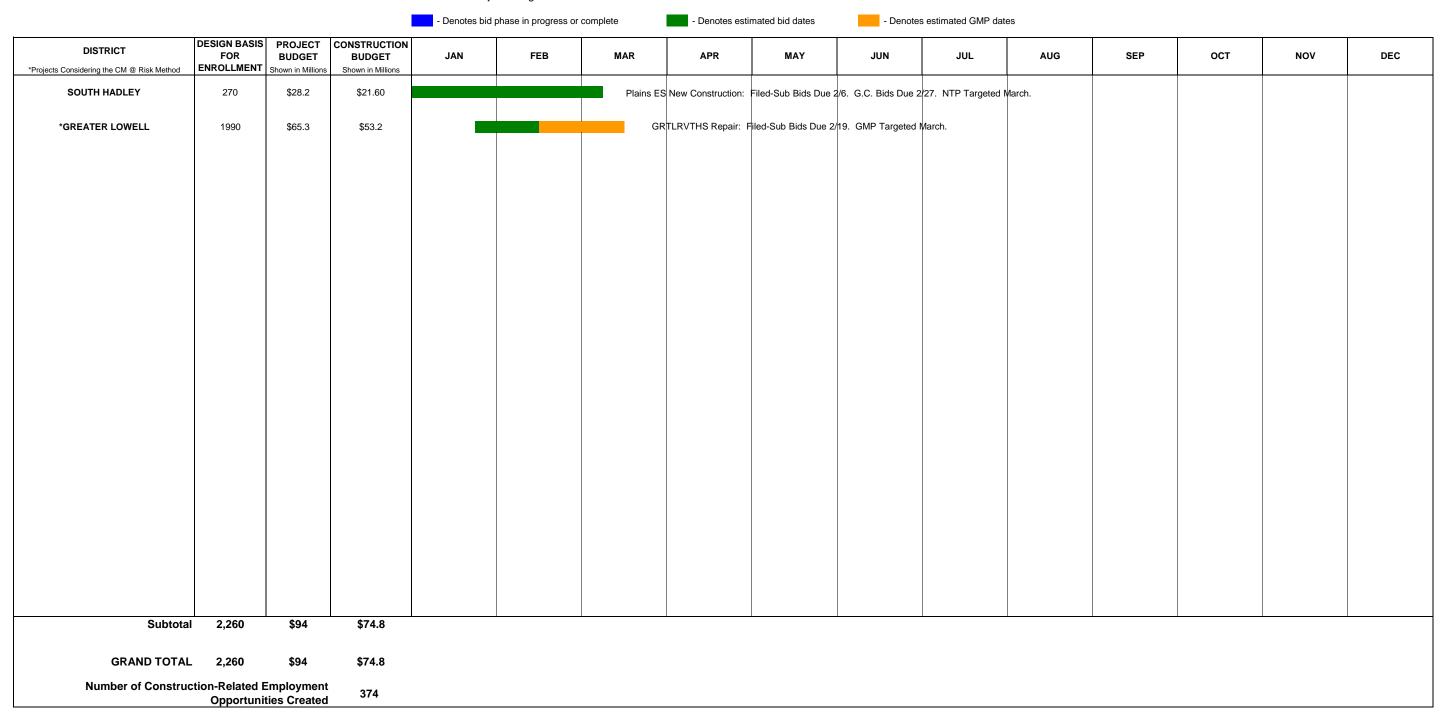

#### Projects in Construction MSBA Grant Basis and Maximum Grant Amount Data Reported as of February 28, 2013

New Program and Wait List Pr	rogram Totals		\$2,578,357,885	55,428		10,660,139							*Includes Alternates			\$1,779,174,210	
Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantial Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
New Program Tota	ala.		\$0.400.704.004	53,368		40.400.440	\$245		\$184		CAPITAL PIPE	LINE PROJECTS IN CON	STRUCTION				\$4.540.444.E7E
New Flogram Tota	115		\$2,489,734,921	33,300		10,196,449	<b>\$245</b>		\$104	D /D: //			1			The new school building is fully enclosed. Windows have been installed and testing is in process. Roofing is complete except flashing.	\$1,618,111,575
Arlington	K-5	G&R Construction	\$15,340,026	380	Bid	57,614	\$266	\$12,403,811	\$215	Design/Bid/ Build	7-Apr-12	28-Jun-13	10 days	58%	1.00%	Masonry is approximately 85% complete. MEP work is progressing from the top floor downward. Wall board, ceiling, and bathroom tile installation is in process on the top floor.	\$9,441,396
Berlin-Boylston Tahanto Reg MS/HS	6-12	СТА	\$32,162,000	560	Bid	126,100	\$255	24,629,999	\$195	Design/Bid/ Build	10-May-11	1-Jul-13		97%	3.00%	Students occupied the new school building on January 3, 2013. Punch list and Commissioning items are being completed after school hours. Abatement of the adjacent existing school is progressing to allow demolition. Subsequently, ball field construction, final landscaping and site work will be completed.	\$19,849,301
Billerica Parker ES	K-5	СТА	\$22,842,500	500	Bid	89,093	\$256	\$17,913,441	\$201	Design/Bid/ Build	15-Sep-10	29-Aug-12	90 days	98%	-0.01%	The new building is substantially complete. Phase II, demolition and site work was completed November 21, 2012. Landscaping to be completed in the Spring.	\$15,851,020
Brookline Heath ES	K-8	Nauset	\$6,284,185	560	Bid	80,952	\$78	\$4,807,436	\$59	Design/Bid/ Build	29-Sep-11	15-Aug-12		99%	3.63%	Punch list work and commissioning remaining. Exterior punch list work to be completed in the Spring.	\$3,173,407
Brookline Runkle ES	PK-8	G&R Construction	\$20,715,300	560	Bid	104,000	\$199	\$17,668,440	\$170	Design/Bid/ Build	10-Nov-10	10-Sep-12		95%	7.94%	Misc. punch list work remaining.	\$11,135,430
Carlisle Carlisle K-8	K-8	H.V. Collins Co. Inc	\$15,277,344	700	Bid	140,312	\$109	\$11,342,751	\$81	Design/Bid/ Build	9-Feb-11	31-Aug-12		100%	3.65%	The project is complete.	\$6,988,636
Danvers Danvers HS	9-12	Bacon Construction	\$53,834,164	1,000	Bid	246,251	\$219	\$43,710,809	\$178	Design/Bid/ Build	14-Nov-10	2-Jul-13		91%	2.15%	Work is continuing on the Phase I punch list. Phase II work is underway on exterior closure precast wall panels, curtain walls and interior masonry partitions in the cafeteria, lobby areas and Central Offices.	\$37,324,055
Douglas Douglas ES	2-5	СТА	\$23,857,111	552	Bid	83,100	\$287	\$19,026,763	\$229	Design/Bid/ Build	Mar-12	22-Jun-13		63%	0.00%	Site work continues. Metal stud and GWB 90% complete. Exterior sheathing and roofing 99%. MEP rough-ins, testing windows and AVB, interior & exterior masonry and interior finishes ongoing.	\$17,611,449
Douglas Douglas IS	6-8	СТА	\$12,081,767	448	Bid	88,245	\$137	\$9,417,212	\$107	Design/Bid/ Build	Mar-12	31-Jan-14		30%	0.00%	Site work continues. Gym and auditorium complete. No work is currently being performed while school is in session.	\$9,319,891
Dracut Dracut HS	9-12	СТА	\$47,290,611	1,160	PFA	174,671	\$271	\$29,420,210	\$168	Design/Bid/ Build	27-Aug-12	17-Aug-14		13%	0.00%	Work is ongoing to close the building envelope for new classroom and gymnasium wings. Installations of MEP and FP systems within the crawl space, Lower B wing and upper/lower C wings continue.	\$36,499,334
East Bridgewater E. Bridgewater Jr/Sr HS	7-12	Fontaine Brothers	\$65,409,000	950	Bid	213,544	\$306	\$47,684,117	\$223	Design/Bid/ Build	10-Aug-11	24-Jun-13		75%	0.70%	Millwork and casework have begun on all floors. All finishes are underway. Site work will continue when weather permits.	\$43,317,092
Easthampton Easthampton HS	9-12	Fontaine Brothers	\$30,934,000	510	Bid	110,400	\$280	\$24,511,000	\$222	Design/Bid/ Build	16-May-11	15-Jan-13	35 days	94%	1.38%	Building achieved Substantial Completion on February 19, 2013. Commissioning of MEP and related building systems is underway. Building being made ready for FF&E deliveries and installations.	\$24,104,384
Fairhaven Rogers ES	K-5	СТА	\$19,099,606	370	Bid	77,871	\$245	\$14,996,521	\$193	Design/Bid/ Build	21-May-12	4-Jul-13		61%	1.00%	The Versico roofing system has been installed and metal edging installation is in process. RTU's and exhaust fans have been set on the roof. Interior light gauge metal framing is complete. MEP rough-ins complete in some areas and progressing in others. Drywall installation is progressing. Ceramic wall tile and porcelain floor tile installation have begun in Area B restrooms.	\$13,994,641
Fall River Morton MS	6-8	J&J Contractors	\$37,654,000	625	Bid	130,576	\$288	\$29,921,971	\$229	Design/Bid/ Build	4-Nov-11	24-Jun-13		70%	8.97%	Millwork and casework have begun on all floors. All finishes are underway. Site work will continue when weather permits.	\$38,251,808
Foxborough	9-12	СТА	\$12,961,769	885	Bid	218,500	\$59	\$10,337,436	\$47	Design/Bid/ Build	25-Jan-10	31-Oct-11		100%	9.26%	Final completion achieved December 4, 2012.	\$7,226,509
Foxborough HS Franklin	9 - 12	Agostini/Bacon	\$86,778,700	1,650	Bid	306,543	\$283	\$73,191,801	\$238.77	Design/Bid/	16-Oct-12	15-Oct-14		3%	0.37%	Site work and utility installation have progressed. Concrete foundation installations are underway. Structural steel has been delivered	\$54,558,408
Franklin HS Hampden-Wilbraham	9-12	Fontaine Brothers	\$48,597,500	1,225	Bid	231,467	\$210	\$37,499,962	\$162	Build Design/Bid/	22-Jul-10	28-Jun-12		99%	2.29%	and installation is underway.  Remaining site work will be completed in the Spring.	\$34,863,838
Minnechaug HS Hingham	6-8	Brait Builders	\$50,432,439	1,020	PFA	176,385	\$286	\$38,006,989	\$215	Build Design/Bid/	7-Jun-12	30-Dec-14		40%	0.00%	Structural steel nearly complete. Masonry installation has begun and interior framing started in phase one.	\$25,909,580
Hingham MS  Hudson  John F Kennedy MS	5-7	Corp. Agostini/Bacon	\$35,102,573	715	Bid	118,850	\$295	\$28,373,294	\$239	Build  Design/Bid/ Build	28-Sep-11	22-Nov-13		70%	1.37%	Working on interior finishes throughout the building. Epoxy floor in toilet rooms is ongoing as well as millwork. Continued corridor tile flooring and wall tiles. Installation of light fixtures, sprinkler heads, and work on elevator fit out are ongoing. Work in locker rooms and	\$24,005,749
Lynnfield	9-12	E.A. Colangeli	\$2,886,991	740	Bid	10,950	\$264	\$2,322,687	\$212	Design/Bid/	25-Jun-12	1-May-13	96 days	81%	5.90%	gym area continue. Metal panels on the exterior of the building are near completion.  Addition is completed and occupied. Work in parking areas is deferred until Spring as a result of schedule impact from differing site	\$1,828,473
Lynnfield HS  Marblehead Glover ES	K-3	G&R Construction	\$20,868,000	425	Bid	79,108	\$264	\$16,977,513	\$215	Build Design/Bid/ Build	25-Jun-12	9-Dec-13		16%	1.00%	condition: elevated levels of nickel.  Demolition of the existing elementary school is complete. New school footing and foundation work is nearly complete. Installation of under=slab drainage and plumbing is in process. Steel delivery and erection is scheduled to start before the end of March 2013.	\$9,688,418
Marshfield High School	9 - 12	Brait Brothers	\$84,980,000	1,310	Bid	267,469	\$318	\$64,604,850	\$242	Design/Bid/	Aug-12	7-Jul-14		18%	0.24%	Structural steel installation nearing completion and slab on deck installation complete in the academic wing. Roof installation has	\$48,607,274
Maynard	8-12	CTA	\$36,650,000	410	Bid	121,520	\$302	\$30,630,013	\$252	Build Design/Bid/	18-Aug-11	6-Dec-13		68%	0.96%	begun. Concession Stand nearing completion.  Window, curtain wall and storefront entrance installations have been completed in all areas. Drywall completed in all areas. Interior	\$23,483,860
Maynard HS Middleton	4-6	CTA	\$18,210,000	553	Bid	83,934	\$217	\$14,529,671	\$173	Build Design/Bid/	06-Apr-10	30-Jul-11		100%	6.93%	finish work is underway.  Final completion achieved November 30, 2012.	\$12,311,976
Howe-Manning ES Monomoy	9-12	Fontaine Brothers	\$54,624,105	700	PFA	168,000	\$325	\$37,291,799	\$222	Build Design/Bid/	11-Feb-13	30-Jun-14		0%	0.00%	Notice to Proceed issued on February 11, 2013.	\$29,696,270
Regional High School  Nashoba	K-5	P.J. Stella Construction/Brait	\$23,640,900	600	Bid	98,030	\$241	\$18,427,425	\$188	Build Design/Bid/	15-Jun-10	31-Aug-12		100%	4.35%	Project is complete with a few remaining punch list items and minor control issues.	\$15,239,622
Pompositticut ES  Natick		Builders Brait Builders	***************************************				***			Build Design/Bid/		-					
Natick HS	9-12	Corp.	\$63,303,452	1,300	Bid	254,225	\$249	\$53,213,182	\$209	Build	13-Sep-10	15-Jun-12		99%	3.35%	Contractor to complete tennis court surfacing in the Spring.  Animal Science Building: Completion of MEP rough-in targeted for late March. Exterior sheathing and window installation to be	\$38,209,033
Norfolk County Agricultural HS	9-12	TLT Construction Corp.	\$21,508,952	550	Bid	114,816	\$187	\$15,546,739	\$135	Design/Bid/ Build	27-Mar-12	9-May-14	30 days	44%	0.21%	completed by mid-March. Agricultural Mechanical Building: MEP rough-in is nearly complete. Exterior finish siding is in progress. Painting and pipe/duct insulation have started. Equine Center and Equipment Garage: Foundations are being prepped for preengineered buildings to be delivered by the end of March.	\$14,119,915
Norfolk Freeman-Kennedy ES	3-6	Fontaine Brothers	\$25,354,966	585	Bid	96,410	\$263	\$20,023,001	\$208	Design/Bid/ Build	9-Nov-10	13-Aug-12		91%	5.11%	New building is complete and currently in use. Final punch list items are ongoing. Final paving, seeding, as well as miscellaneous landscaping to be completed in the Spring.	\$15,861,760
Oxford Oxford MS	5-8	S.O.M./ J.J. Cardosi	\$5,085,217	652	Bid	117,000	\$43	\$5,085,217	\$43	Design/Bid/ Build	1-Jun-12	26-Aug-13		25%	5.16%	Roof replacement complete. Window project, HVAC, ADA, and floor replacement work scheduled for Summer 2013.	\$3,483,589
Plymouth Plymouth HS	9-12	J&J Contractors	\$67,687,000	1,350	Bid	267,497	\$253	\$51,579,703	\$193	Design/Bid/ Build	3-May-10	22-Jun-12	30 days	98%	5.49%	Punch list work ongoing. Site work to be completed in the Spring.	\$41,810,972
Quincy Central MS	6-8	H.V. Collins Co. Inc	\$32,540,712	620	PFA	114,975	\$283	\$24,440,102	\$213	Design/Bid/ Build	24-May-12	5-Sep-13		35%	0.49%	Egotings foundations and structural stool complete Metal stud. CWP MED rough ins. CMU exterior deposits and site utilities are	
Somerset Berkley Somerset Berkley RHS	9-12	Bacon-Agostini	\$69,407,000	1,000	Bid	222,826	\$311	\$52,042,575	\$234	Design/Bid/ Build	3-Jul-12	15-Aug-14		17%	0.28%	Structural steel installation is complete and spray fireproofing has begun intermittently due to low temperatures. Roof installation and roof drainage installation has begun. The gray water tank and associated piping was installed along with other site utilities.	\$49,050,210
Sturbridge Burgess ES	K-6	Fontaine Brothers	\$22,946,000	860	Bid	131,630	\$174	\$17,591,000	\$134	Design/Bid/ Build	10-Aug-10	1-Oct-12		99%	7.00%	Both the new addition and the adjacent building renovations are complete and in use. Abstement and demolition of the existing school	
Sutton MS/HS	6-12	TLT Construction Corp.	\$41,230,800	840	Bid	179,040	\$230	\$32,998,403	\$184	Design/Bid/ Build	1-Jul-11	31-Dec-14	21 days	53%	1.55%	Drywall installation continues at the first and second floor hallways and media center. Interior finishes, including flooring and casework, are progressing in the classrooms and administration offices.	\$27,837,016

#### Projects in Construction MSBA Grant Basis and Maximum Grant Amount Data Reported as of February 28, 2013

Project	Grade	Contractor	Total Construction Cost*	Projected Enroll	PFA or Bid Data	Proposed Square Footage	Construction Cost per Square Foot	Building Cost	Building Cost per Square Foot	Project Type	Construction Start	Estimated Substantia Completion Date	Reporting Variance from Schedule	Physical Progress (%)	Change Orders (%)	Construction Status	Approximate Maximum Grant Amount *
Tewksbury Tewksbury HS	9-12	CTA/Methuen Construction Co.	\$51,600,000	1,100	Bid	218,781	\$236	\$40,159,651	\$184	Design/Bid/ Build	15-Oct-10	3-Aug-12		95%	3.59%	Punch list work ongoing. Site work to be completed in the Spring.	\$36,622,570
West Springfield West Springfield HS	9-12	Fontaine Brothers	\$85,006,020	1,270	Bid	257,525	\$330	\$56,875,181	\$221	Design/Bid/ Build	14-Dec-11	31-Dec-13		64%	0.54%	Exterior framing for the gym and pool continues. Interior painting and ceiling grid installation have begun in Bldg A & B. Millwork deliveries started in March.	\$68,808,290
Weston	4-5	Colantonio	\$24,537,966	355	PFA	65,390	\$375	\$19,872,289	\$304	Design/Bid/	21-Dec-12	15-May-14		5%	0.37%	Building mass site excavation is near completion. Footings to be placed starting in mid-March. Temporary parking lots and bus loop are	\$8,610,302
Field ES  Winchester  Vinson-Owen ES	K-5	СТА	\$21,064,999	420	PFA	74,774	\$282	15,558,357	\$208	Build  Design/Bid/ Build	17-Feb-12	21-Jun-13		75%	1.98%	in place.  Footings, foundations, steel, masonry, roof, MEP rough-ins, permanent power and windows are complete. Site work is approximately 80% complete. Metal stud framing, sheathing and GWB are 99% complete. Interior finishes are 50% complete. Elevator installation is underway. Curtain wall and exterior wall panels are 75% complete and testing is underway.	\$10,399,222
Adams-Cheshire	6-12	Gilbane	\$33,474,193	805	Bid	174,758	\$192	24,009,952	\$137	CM-R	17-May-11	31-Jul-12		99%	2.46%	Misc. punch list work remaining.	\$28,243,131
Hoosac Valley MSHS Andover	K-5	Skanska	\$34,527,063	680	PFA	67,600	\$511	21,966,698	\$325	CM-R	14-May-12	27-Oct-14		25%	0.00%	Steel erection and metal decking are complete. Underground plumbing is nearly complete. Contractor has started electrical rough in as	\$16,773,753
Bancroft ES  Ashburnham Westminster, JR  Briggs ES	PK-5	Consigli	\$24,780,000	520	Bid	87,085	\$285	18,202,478	\$209	CM-R	9-Mar-12	31-Dec-13		64%	0.09%	well as concrete slab pours.  The new school building is framed, sheathed, waterproofed and masonry is complete. Roofing is nearly complete. Mechanical, plumbing, electrical and fire protection rough-ins are ongoing on both floors. Elevator installation is in process. Prime and first coat priming and painting are complete in Building A and the Pre-K area.	\$16,353,447
Burlington	6-8	СТА	\$24,612,440	880	Bid	151,000	\$163	\$18,988,987	\$126	CM-R	15-Apr-11	17-May-13		99%	2.77%	Building renovation work is completed and remaining punch list work is ongoing. Athletic field work is expected to recommence as weather will allow.	\$16,933,103
Marshall Simonds MS  Dedham	K-5	Consigli	\$18,174,209	310	Bid	62,723	\$290	\$13,528,098	\$216	CM-R	15-Oct-10	1-Jan-12		99%	6.50%	The new school building is complete and in service. Two final commissioning items are being resolved.	\$10,778,452
Avery ES  Duxbury HS	6-12	Dimeo	\$104,950,377	1,735	Bid	322,105	\$326	\$81,178,481	\$252	CM-R	9-Jul-12	3-Jul-14		17%	0.11%	Site work, utilities, backfill, footings and foundation work completed at main building and Field House. Steel erection and detailing completed on main building Area A and 50% on Area B. Area A enclosed with temp heat to allow deck to be placed and start steel fireproofing. Permanent gas and electrical services activated. Exterior masonry walls underway.	\$51,406,497
Essex North Shore Agricultural & Technical High School	9-12	Gilbane	\$110,217,451	1,440	PFA	337,000	\$327	\$79,334,889	\$235	CM-R	7-May-12	30-Jun-14		23%	0.20%	Under-slab utilities, MEP rough-ins, exterior/interior framing, slabs-on-grade and roof installation ongoing. Main gas service tap started.	\$77,500,000
Grafton Memorial Sr HS	9-12	Dimeo	\$54,881,977	900	Bid	186,000	\$295	\$41,783,110	\$225	CM-R	18-Aug-10	10-Jul-12		100%	6.05%	New building is complete and currently in use. Minor punch list items remain. Commissioning is ongoing.	\$36,108,679
Leominster Leominster SHS	9-12	S.O.M.	\$33,794,797	1,825	Bid	295,859	\$114	\$25,382,707	\$86	CM-R	1-Jul-11	30-Aug-13		90%	5.74%	Work has completed on the 5th of 7 phases. Phase 5 completed work includes renovation of the original science rooms, media center, health occupations, life skills, and computer labs. Renovations have begun on the 6th phase which includes the Administration, Art/Music Wing and remaining C Wing classrooms.	\$30,693,543
Lexington Estabrook ES	K-5	Shawmut Design	\$32,792,348	540	PFA	91,840	\$357	\$22,795,606	\$248	CM-R	20-Jun-12	21-Aug-14		18%	0.00%	Structural steel erection is nearly complete. Half of the second and third floor slabs are in place.	\$13,132,418
Longmeadow	9-12	Gilbane	\$63,685,998	1,000	Bid	236,985	\$269	\$46,573,364	\$197	CM-R	Nov-10	1-Nov-13		74%	0.82%	Interior finish work and final cleaning has concluded in the new addition. Renovation work has commenced in the Central	\$33,067,140
Longmeadow HS  Medway MS	5-8	Consigli	\$18,211,824	800	Bid	223,780	\$81	\$12,885,464	\$58	CM-R	Oct-11	21-Dec-12	60 days ahead	99%	2.43%	Administration offices and other District spaces.  The 4-phase project is substantially complete. The final punch list work is ongoing and commissioning is nearly complete.	\$10,352,981
Methuen Methuen HS	9-12	Terminated Dimeo 12/31/2011. Consigli as of	\$74,749,773	2,075	Bid	368,017	\$203	\$58,040,746	\$158	CM-R	21-Jul-11	Aug-14		25%	0.87%	MEP rough-in work continues in the existing academic wing that is currently being renovated. Drywall is being installed in the utility shafts. The roof is installed and the skylight is in place. Steel erection in the addition is complete and the building envelope is underway.	\$64,503,232
Needham		5/21/2012	*******		5			<b>A</b>		011.5							
Newman ES	K-5	Consigli	\$19,064,745	754	Bid	119,264	\$160	\$13,367,855	\$112	CM-R	16-Jun-10	27-Aug-12		100%	8.40%	The project is complete.  Phase I addition work was completed during the week of Eahrupy school break. Phase II repovations of the 1st and 2nd floor.	\$8,598,929
Norton Norton HS	9-12	WT Rich	\$27,023,541	700	Bid	130,755	\$207	\$20,590,559	\$157	CMR	12-Mar-12	27-Dec-13		52%	2.17%	Phase I addition work was completed during the week of February school break. Phase II renovations of the 1st and 2nd floor classrooms are underway. Asbestos remediation and floor tile removal have commenced.	\$21,484,408
Rockland John Rogers MS/ HS	5-12	Agostini	\$66,362,037	1,525	Bid	275,700	\$241	\$47,724,091	\$173	CM-R	15-Jan-10	8/31/12 for MS May 2013 for HS		93%	5.59%	Phase 4 work continues in the High School. Stair #5 work is ongoing. Stair pans are installed and concrete has been poured. Drywall installation and taping are ongoing. Exterior walls have been framed and sheathed. AVB is complete. Curtain wall is installed. SPED classrooms and District School Offices are framed. Rough MEP's are complete. Misc. site work continues around the campus including posts for chain-link fence and site signage. Punch list work related to Phase 2, 3 and 4 is ongoing.	\$52,837,940
Saugus Belmonte Middle School	6-8	Consigli	\$15,712,630	709	PFA	160,000	\$98	\$11,141,407	\$70	CM-R	23-May-12	3-Sep-13		54%	2.51%	Phase 1A and 1B are complete. Phase 1 punch list items in process. Phase 2 is ahead of schedule by one week. Phase 3 scheduled to start over April vacation. Phase 4 Scheduled to start around April vacation/Summer 2013.	\$10,097,544
Shrewsbury Sherwood MS	5-6	Gilbane	\$33,986,286	900	Bid	129,378	\$263	\$22,823,030	\$176	CM-R	7-Mar-11	31-Oct-13		95%	2.00%	The new school building is in service. Punch list and Commissioning items are being completed after school hours. Abatement of the adjacent existing school is progressing to allow demolition. Subsequently, ball field construction, final landscaping and site work will be completed.	\$22,369,828
Somerville E. Somerville Community School	K-8	Gilbane	\$32,590,244	500	Bid	121,100	\$269	\$24,613,842	\$203	CM-R	7-Nov-11	29-Mar-13		90%	0.32%	HVAC testing and balancing have begun. Classroom wings ready for FFE which will arrive in May. Auditorium and Gym finishes are ongoing. Landscaping to be complete as soon as weather permits. Commissioning is underway.	\$15,237,996
Southbridge Southbridge MS/HS	6-12	Consigli	\$59,307,632	1,050	Bid	199,740	\$297	\$41,487,200	\$208	CM-R	30-Nov-10	18-Jun-12		99%	0.84%	Project closeout is in progress. Landscape maintenance is ongoing. Site and storm water work are anticipated to be completed in the Spring.	\$52,019,398
Southeastern Regional Voc Tech High School	9-12	WT Rich	\$27,200,000	1,370	Bid	308,250	\$88	\$19,996,609	\$65	CM-R	27-Jun-11	20-Jan-14		58%	1.00%	Phase II, interior renovation work and the Gymnasium addition, are complete. Elevator inspection issues are being resolved. Renovation of the existing Gym is in process to create a new media center, classrooms, labs, and copy room. Demolition and renovation are also in process in the rooms over the second floor in Building #3. Final site landscaping work will be completed in Spring/Summer 2013.	\$25,988,607
Springfield Dryden ES	PK-5	Morganti Aquadro & Cerruti	\$10,720,901	280	PFA	38,850	\$276	\$7,217,800	\$186	CM-R	28-Jun-12	1-Nov-13		28%	0.00%	Phase I addition work ongoing for the tornado damaged wing of the existing school. Structural steel is complete. MEP rough ongoing. Masons on site installing brick exterior walls. Windows delivered to site.	\$8,287,993
Uxbridge High School	9-12	Shawmut Design	\$37,293,765	600	Bid	123,000	\$303	\$27,562,625	\$224	CM-R	28-Feb-11	20-Jun-12		99%	2.50%	Minor punch list work remaining within the building. Field work to be completed in the Spring.	\$21,973,620
Wayland ** Wayland HS	9-12	Shawmut Design	\$54,230,819	900	Bid	171,000	\$317	\$37,343,299	\$218	CM-R	28-Jun-10	1-Dec-11		99%	2.76%	Misc. landscaping work to be completed in the Spring.	\$24,051,231
Wellesley	9-12	Turner	\$82,942,222	1,500	Bid	280,000	\$296	\$55,814,300	\$199	CM-R	24-Aug-09	1-May-13		99%	4.59%	The Project is complete and closeout is in progress.	\$40,117,222
Wellesley HS  ** Excludes Field House	0.12	1 (1116)	₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩₩	1,000	Dia	_50,000	Ψ200	\$55,017,000	ψ100	SWITC	_ / / lug-03	1 May-10		5576	1.00/0		ψ.Ο,111,622
	otolo		6420.704.004	0.000		462.000											\$141,213,334
Wait List Program To	otals		\$120,784,964	2,060		463,690											
Springfield Forest Park MS	6-8	Consigli	\$34,745,898	660	Bid	148,800	\$234	\$26,209,932	\$176	CM-R	26-Mar-12	1-Aug-13		53%	0.00%	MEP rough-in work is in progress on all floors. Structural work for toilet and break rooms is ongoing. Window installation work is nearly complete. Plastering and patching work is ongoing on all floors as well as taping and painting. Start-up of roof top equipment is underway.	
Springfield Putnam Voc Tech HS	9-12	Consigli	\$86,039,066	1,400	Bid	314,890	\$273	\$62,949,742	\$200	CM-R	18-May-10	20-Jul-12	60 days ahead	95%	0.66%	Punch list work on new building is complete. Binder placed at Alton Street lot.	\$102,872,837
Worcester North HS	9-12	Gilbane	\$49,145,638	1,200	Bid	239,570	\$205	\$40,860,983	\$171	CM-R	24-Sep-08	Jun-11		99%	3.20%	Phase 4, which includes the parking lots and reconstruction of the ball fields, will be completed by the Fall.	\$45,911,881

You are Currently Viewing Active Projects.

Date of Report:3/13/13

Waitlist

Science Lab Initiative

Last Updated: 3/13/13

Active Projects: 332 **Procurement** CM\GC MSBA ID District School Phase **Project Scope** OPM Designer Cx\_Company Type Knight, Bagge & Anderson 200800010405 Frolio Middle School Ai3 Architects LLC Abington **Feasibility Study** Inc. RF Walsh Collaborative DBB 01100010015G Abington Woodsdale Repair - Accelerated Partners Gale Associates, Inc. Russo Barr Associates. Inc. **Lockheed Window Corporations** C. T. Douglas Elementary 01000020020G Acton School **Final Audit Approved** DBB **CBI** Consulting, Inc. Gibson Roofs, Inc. Repair - Accelerated Adams Memorial Middle 200806030305 Adams-Cheshire School **Project Completion** Addition / Renovation CM@R **URS** Corporation Tessier Associates, Inc. Strategic Building Solutions, LLC Gilbane Building Company Municipal Building 201100050405G Agawam Junior/Senior High Repair - Accelerated DBB Consultants, Inc. **CSS** Architects Incorporated **Building Enclosure Associates** Closeout Agawam Strategic Building Solutions Amherst Regional Middle 201106050405G Amherst-Pelham Repair - Accelerated DBB LLC Bradley Architects, Inc. Russo Barr Associates, Inc. R&R Window Contractors, Inc. School Closeout 01100090310G Andover West Middle DBB Skanska USA Building, Inc Simpson Gumpertz & Heger Inc. Eagle Rivet Roof Services Corporation Andover Closeout Repair - Accelerated Russo Barr Associates, Inc. Dore & Whittier Management Symmes Maini & McKee Associates CM@R 200800090003 Andover Bancroft Elementary School Construction **New Construction** Partners, Inc. Sebesta Blomberg & Associates, Inc. Skanska USA Building, Inc. DBB 01100100055G Arlington M Norcross Stratton Repair - Accelerated PMA Construction Services Turowski2 Architecture, Inc. Federal Construction Corp.| Unicon Inc. **Final Audit Approved** DBB PMA Construction Services HMFH Architects, Inc. 200900100050 Arlington Thompson Elementary School Construction **New Construction** Consulting Engineering Services, LLC G & R Construction, Inc. Ashburnham-John R. Briggs Elementary Lamoureux Pagano & Associates, CM@R 200806100025 Westminster School Construction **New Construction** STV Incorporated Foreman Building Commissioning, LP Consigli Construction Company, Inc. Design Partnership of Cambridge, Assabet Valley Regional Strategic Building Solutions, Assabet Valley 200908010605 Technical High School Design Development Repair - Major DBB LLC Symmes, Maini & McKee Associates Symmes Maini & McKee 200906150020 Athol-Royalston Riverbend Elementary School Feasibility Study Repair- Accelerated Associates, Inc. Mount Vernon Group Architects, Inc. A. Irvin Studley Elementary Tishman Construction 201200160001 School Deisgn Development Corporation of MA CBI Consulting Inc. Attleboro Repair - Accelerated Gale Associates, Inc. Lamoureux Pagano & Associates, 200800170305 Auburn Middle School Project Scope & Budget Skanska USA Building, Inc. Auburn **New Construction** Ayer-Shirley Regional Dore and Whittier Architects, Symmes Maini & McKee Associates, WSP Flack + Kurtz 9999 Ayer-Shirley Middle/High School Design Development Addition / Renovation West Barnstable Elementary 01100200005G Barnstable DBB PMA Construction Services Gale Associates, Inc. CBI Consulting Inc. Paul J. Rogan Co., Inc. School **Project Completion** Repair - Accelerated Bellingham Memorial Middle General Air Conditioning & Heating, Bellingham Daedalus Projects Inc DBB WSP Flack + Kurtz 01100250315G School Final Audit Approved Repair - Accelerated Richard D. Kimball Company, Inc. Inc. Roger Wellington Elementary CM@R Strategic Building Solutions, LLC Skanska USA Building, Inc. 200800260035 Belmont School Closeout **New Construction** PMA Construction Services Jonathan Levi Architects LLC Monument Mountain Regional Strategic Building Solutions, Symmes Maini & McKee Associates, Schematic Design LLC 201006180505 Berkshire Hills High School Inc. Tahanto Regional High HMFH Architects, Inc. 200806200505 Berlin-Boylston School **Project Completion New Construction** DBB PMA Construction Services Strategic Building Solutions, LLC CTA Construction Co., Inc. Mount Vernon Group Architects, 200800300505 **Beverly Beverly HS** Closeout Addition / Renovation HEERY **CTA Construction Co., Inc.** Joslin, Lesser + Associates Symmes Maini & McKee Associates. CTA Construction Co., Inc. | RS 200800310015 Billerica Parker Elementary School **Project Completion** DBB Sebesta Blomberg & Associates, Inc. **New Construction** Hurford **Municipal Building** GVW, Inc. 01100310505G Billerica Memorial High School Repair - Accelerated Consultants, Inc. Knight, Bagge & Anderson, Inc. **Building Enclosure Associates** Strategic Building Solutions Blackstone Valley Regional 201108050605G Blackstone Valley Reg Voc Tech High School DBB Greenwood Industries, Inc. **Final Audit Approved** Repair - Accelerated LLC Reinhardt Associates, Inc. Cannon Design Compass Project 201208050605 Blackstone Valley Reg Blackstone Valley Design Development Science Lab Management, Inc. Flansburgh Associates, Inc. Horizon Engineering Associates, LLP Blackstone Valley A.F. Maloney Elementary **Approved Project Vote** 201206220015 Millville **Pending** Repair- Accelerated School Blackstone Valley -**Approved Project Vote** J.F. Kennedy Elementary 201206220008 Millville School **Pending** Repair- Accelerated

Last Updated: 3/13/13

Massachusetts School Building Authority You are Currently Viewing Active Projects. Date of Report:3/13/13 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	ОРМ	Designer	Cx_Company	CM\GC
WISBAID	Blackstone Valley -	3011001	Approved Project Vote	Froject Scope	туре	OFIVI	DiMarinisi & Wolfe Architects Urban	CX_Company	CIMIGO
201206220505	Millville	Regional High School	Pending	Repair - Accelerated		Arcadis	Designers	Gale Associates, Inc.	
		Clarence R Edwards Middle							
201100350430G	Boston	School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Rist-Frost-Shumway Engineering, P.C.	<u> </u>
201100350522G	Boston	Excel High School	Closeout	Panair Accolorated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	
201100350522G	BOSION	Henry Dearborn Middle	Cioseout	Repair - Accelerated	DBB	Daedalus Projects IIIC	BLW Engineers, Inc.	Simpson Gumpenz & neger inc.	-
201000350074	Boston	School	Feasibility Study			Daedalus Projects Inc	Jonathan Levi Architects LLC		-
		Joseph Lee Elementary				•			
201100350183G	Boston	School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	Gale Associates, Inc.
004000050505	Desten	Outin and United Salara I	Facilities Objects			Maureen Anderson - City	LINATELL Analysis as a line		
201000350565	Boston	Quincy Upper School Thomas A Edison Jr High	Feasibility Study			Employee	HMFH Architects, Inc.		<u> </u>
201100350425G	Boston	School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	BLW Engineers, Inc.	Simpson Gumpertz & Heger Inc.	-
		Washington Irving Middle		'		,,	3	1 1	
201100350445G	Boston	School	Final Audit Approved	Repair - Accelerated	DBB	Daedalus Projects Inc	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	-
	5 1 1	Archie T Morrison Elementary				RF Walsh Collaborative			
201000400033G	Braintree	School	Final Audit Approved	Repair - Accelerated	DBB	Partners  RF Walsh Collaborative	Habeeb & Associates Architects, Inc	c. Cannon Design	Modern Glass & Aluminum, Inc.
201000400505G	Braintree	Braintree High School	Final Audit Approved	Repair - Accelerated	DBB	Partners	Habeeb & Associates Architects, Inc	c Cannon Design	Gibson Roofs, Inc.
201000100000	2.4		· · · · · · · · · · · · · · · · · · ·	. repair / recordiated		RF Walsh Collaborative		2. Gaillion 2 colg.:	0.200000,0
201000400305G	Braintree	East Middle School	Final Audit Approved	Repair - Accelerated	DBB	Partners	Habeeb & Associates Architects, Inc	c. Cannon Design	Modern Glass & Aluminum, Inc.
<b>_</b>						RF Walsh Collaborative			
201000400015G	Braintree	Highlands Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Partners	Habeeb & Associates Architects, Inc	c. Cannon Design	Modern Glass & Aluminum, Inc.
201000400005G	Braintree	Hollis Elementary School	Final Audit Approved	Repair - Accelerated	DBB	RF Walsh Collaborative Partners	Habeeb & Associates Architects, Inc	Cannon Design	Modern Glass & Aluminum, Inc.
2010001000000	Braintiec	Tiolio Liemonary Concer	i mai Addit Approved	Ropali /todoloratoa	555	1 ditilolo	Tiabeeb & Acoociates Atomicette, inc	. Garmon Bedign	Modern Class & Adminiant, me.
201206250320	Bridgewater-Raynham	Bridgewater Middle School	Project Scope & Budget	Repair - Accelerated		Pinck & Co., Inc.			
									_
201206250020	Bridgewater-Raynham	L.B. Merrill Elementary Schoo	Project Scope & Budget	Repair - Accelerated		Pinck & Co., Inc.			
201206250050	Bridgewater-Raynham	Laliberte Elementary School	Project Scope & Budget	Repair - Accelerated		Pinck & Co., Inc.			
201200230030	Dridgewater-rtayrinam	Lamberte Liementary School	1 Toject ocope & Budget	Repail - Accelerated		Timer & Co., me.			
201100440505G	Brockton	Brockton High School	Project Completion	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Gibson Roofs, Inc.
						-	·		
201100440110G	Brockton	Downey Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Built-up Roofing Systems LLC
20110011010	Drookton	Fact lunion Llink Cahool	Classout	Danair Assolarated	DDD	Chanala LICA Duilding Inc	CCC Architecta Incornerated	Diet Freet Chumusu Freinagring D.C.	Deliable Deefing and Cheet Metal 11.C
201100440405G	Brockton	East Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Reliable Roofing and Sheet Metal, LLC
201100440023G	Brockton	Edgar B Davis	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
				'		<u>.                                    </u>			
201100440045G	Brockton	Hancock Elementary School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
0044004404400	D 11	N (1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1			555	OL 1 110A D '11'	000 A 1% 4 1	B: ( F . ( B)	Arden Engineering Constructors, LLC
201100440410G	Brockton	North Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Rist-Frost-Shumway Engineering, P.C.	Built-up Roofing Systems LLC
201100440078G	Brockton	Oscar F Raymond K-8	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
2011001100100		- Coodin Mayinena Me	0.00000.	. repair / recordinated		enamena een Pamamig, me	CCC : wormood moorperated	Chilpson Campona a nager me.	. tomasio : tooming and one of motal, 220
201100440420G	Brockton	West Junior High School	Closeout	Repair - Accelerated	DBB	Skanska USA Building, Inc	CSS Architects Incorporated	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
						Diversified Project	Habeeb & Associates Architects,		
201100450005G	Brookfield	Brookfield Elementary School	Closeout	Repair - Accelerated	DBB	Management	Inc.	Cannon Design	Northeast Energy Control Systems
201100460015	Brookline	Edward Devotion	OPM Selection						
201100400013	DIOUNIIIO	Edward Dovotion	OT WE OCIOCHOTE			Town of Brookline Building			
201000460025	Brookline	Heath Elementary School	Project Completion	Addition / Renovation	DBB	Department	Miller Dyer Spears Inc.	Consulting Engineering Services, LLC	Nauset Construction Corporation
						Town of Brookline Building	Design Partnership of Cambridge,		
200800460045	Brookline	John D. Runkle School	Project Completion	Addition / Renovation	DBB	Department	Inc.	Consulting Engineering Services, LLC	G & R Construction, Inc.

Massachusetts School Building Authority You are Currently Viewing Active Projects.

Date of Report:3/13/13 Active Projects: 332

Science Lab Initiative Last Updated: 3/13/13 Green Repair Accelerated Repair Waitlist

					Procurement				
MSBA ID	District	School Marshall Simonda Middle	Phase	Project Scope	Туре	OPM Construction Monitoring	Designer	Cx_Company	CM\GC
201000480303	Burlington	Marshall Simonds Middle School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	RDK Engineers	CTA Construction Co., Inc.
200800480015	Burlington	Memorial Elementary School	Closeout	New Construction	DBB	Construction Monitoring Services, Inc.	Knight, Bagge & Anderson, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
W20024323	Cambridge	Cambridge Rindge and Latin High School	Closeout	Addition / Renovation	DBB	-	HMFH Architects, Inc.		W. T. Rich Company Inc.
201200500012	Canton	Lt. Peter M. Hansen	Project Scope & Budget	Repair - Accelerated		Vertex Construction Services	S CSS Architects Incorporated		
201200500305	Canton	William H. Galvin Middle School	Project Scope & Budget	Repair - Accelerated		Vertex Construction Services	·		
201008150605G	Cape Cod Region Voc Tech	Cape Cod Region Voc Tech	Closeout	Repair - Accelerated	DBB	URS Corporation	Garcia Galuska DeSousa Consulting Engineers Inc.	Fitzemeyer & Tocci Associates, Inc.	-
200800510025	Carlisle	Carlisle School	Closeout	Addition / Renovation	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	H.V. Collins Co., Inc.
201106350025G	Central Berkshire	Craneville Elementary School	Closeout	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	Titan Roofing, Inc.
201106350035G	Central Berkshire	Kittredge Elementary School	Project Completion	Repair - Accelerated	DBB	Daedalus Projects Inc	Bradley Architects, Inc.	Strategic Building Solutions, LLC	A.J. Schnopp Jr., Construction, Inc.   Alpha Contracting Associates, Inc.
201100560030G	Chelmsford	Byam Elementary School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	s Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	S.O.M. Construction Ent,, Inc.
201100560505G	Chelmsford	Chelmsford High School	Closeout	Repair - Accelerated	DBB	Vertex Construction Services	s Russo Barr Associates, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200800570050	Chelsea	Clark Avenue School	Designer Selection			Pinck & Co., Inc.	-		
200900610021	Chicopee	Chicopee Academy	Project Scope & Budget			Arcadis	Caolo & Bieniek Associates, Inc.		<u>.                                    </u>
200906400505	Concord-Carlisle	Concord-Carlisle Regional High School	Construction	New Construction	CM@R	KV Associates, Inc.	OMR Architects, Inc.	Strategic Building Solutions, LLC	Turner Construction Company
200800710505	Danvers	Danvers High School	Construction	Addition / Renovation	DBB	Construction Monitoring Services, Inc.	DiNisco Design Partnership, Limited	d Turner Facilities Management Solutions	Bacon Construction Co, Inc.
201100720040G	Dartmouth	James M. Quinn Elementary School	Closeout	Repair - Accelerated	DBB		s Russo Barr Associates, Inc.	Gale Associates, Inc.	Capeway Roofing Systems, Inc.
200800730010	Dedham	Avery Elementary School	Closeout	New Construction	CM@R	Construction Monitoring Services, Inc.	Dore & Whittier Architects, Inc.	WSP Flack + Kurtz	Consigli Construction Company, Inc.
201200730005	Dedham	Early Childhood Education Center	Eligibility Period						
201006450005G	Dennis-Yarmouth	Ezra Baker Elementary School	Project Completion	Repair - Accelerated	DBB	STV Incorporated	Knight, Bagge & Anderson, Inc.	CBI Consulting Inc.	Antonelli Construction Co., Inc.
200800770010	Douglas	Douglas Elementary School	Construction	New Construction		HEERY	DiNisco Design Partnership, Limited	d Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800770100G	Douglas	Douglas Intermediate Elementary School	Construction	Repair - Accelerated	DBB	HEERY	DiNisco Design Partnership, Limited	d Consulting Engineering Services, LLC	CTA Construction Co., Inc.
200800790505	Dracut	Dracut Senior High School	Construction	Addition / Renovation	DBB	RF Walsh Collaborative Partners	Mount Vernon Group Architects, Inc	c. RDK Engineers	CTA Construction Co., Inc.
201000820505	Duxbury	Duxbury High School	Construction	New Construction	CM@R	KV Associates, Inc.	Mount Vernon Group Architects, Inc	c. WSP Flack + Kurtz	Dimeo Construction Company
200900830505	East Bridgewater	East Bridgewater High School	Construction	New Construction	DBB	RF Walsh Collaborative Partners	Ai3 Architects LLC	Foreman Building Commissioning, LP	Fontaine Brothers, Inc.
200800860505	Easthampton	Easthampton High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Caolo & Bieniek Associates, Inc.	Consulting Engineering Services, LLC	Fontaine Brothers, Inc.
201200880405	Easton	Easton Junior High School	Design Development	Repair - Accelerated		PMA Construction Services	Russo Barr Associates, Inc.	Gale Associates, Inc.	-
200809130705	Essex Agr Tech	Essex Agricultural and Technical High School	Construction	New Construction	CM@R	PMA Construction Services	Design Partnership of Cambridge, Inc.	Turner Facilities Management Solutions	Gilbane Building Company
200800940020	Fairhaven	Rogers Elementary School	Construction	New Construction	DBB	Daedalus Projects Inc	HMFH Architects, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.

Massachusetts School Building Authority You are Currently Viewing Active Projects. Date of Report:3/13/13 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	ОРМ	Designer	Cx_Company	CM\GC
	2.0	James Madison Morton		r reject ecope	-71-			on_oompany	
200900950315	Fall River	Middle School	Construction	New Construction	DBB	Maguire Group Inc.	Mount Vernon Group Architects, Inc.	Sebesta Blomberg & Associates, Inc.	J & J Contractors, Inc.
201100960005G	Falmouth	East Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100960030G	Falmouth	North Falmouth Elementary School	Final Audit Approved	Repair - Accelerated	DBB	No OPM Compass Project	Keenan and Kenny Architects, Ltd.	Gale Associates, Inc.	Meadows Construction Company LLC
201100970505G	Fitchburg	Fitchburg High School	Final Audit Approved	Repair - Accelerated	DBB	Management, Inc.  Compass Project	BLW Engineers, Inc.	RDK Engineers	Ostrow Electrical Co., Inc.
201000970025G	Fitchburg	Goodrich Kindergarten	Final Audit Approved	Repair - Accelerated	DBB	Management, Inc. Compass Project	BLW Engineers, Inc.	RDK Engineers	CAM HVAC & Construction, Inc.
200900970048G	Fitchburg	Memorial Intermediate	Final Audit Approved	Repair - Accelerated	DBB	Management, Inc.	BLW Engineers, Inc.	RDK Engineers	E. Amanti & Sons, Inc.
201100970048G	Fitchburg	Memorial Intermediate	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
201100970043G	Fitchburg	Reingold Elementary School	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	Lockheed Window Corporations
200900970043G	Fitchburg	Reingold Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	E. Amanti & Sons, Inc.
200900970060G	Fitchburg	South Street Elementary	Closeout	Repair - Accelerated	DBB	Compass Project Management, Inc.	BLW Engineers, Inc.	RDK Engineers	Lockheed Window Corporations
201100970060G	Fitchburg	South Street Elementary	Construction	Repair - Accelerated	DBB	Compass Project Management, Inc.	Knight, Bagge & Anderson, Inc.	Simpson Gumpertz & Heger Inc.	CAM HVAC & Construction, Inc.
200800990505	Foxborough	Foxborough High School	Closeout	Repair - Major	DBB	Construction Monitoring Services, Inc.	Kaestle Boos Associates, Inc.	Consulting Engineering Services, LLC	CTA Construction Co., Inc.
201101000045G	Framingham	Mary E Stapleton Elementary School	Closeout	Repair - Accelerated	DBB	Bargmann, Flendrie & Archetype, Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	Lockheed Window Corporations
200901010505	Franklin	Franklin High School	Construction	New Construction	DBB	Daedalus Projects Inc	Ai3 Architects LLC	Consulting Engineering Services, LLC	Bacon-Agostini Construction Joint Venture
201101030001G	Gardner	Elm Street School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
201101030505G	Gardner	Gardner High School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
201201030505	Gardner	Gardner High School	Construction	Science Lab		Pinck & Co., Inc.	Lamoureux Pagano & Associates, Inc.	Fitzemeyer & Tocci Associates, Inc.	-
201201030405	Gardner	Gardner Middle School	Design Development	Repair - Accelerated		Leftfield, LLC	Richard D. Kimball Company, Inc.	Fitzemeyer & Tocci Associates, Inc.	
200801030020G	Gardner	Waterford Street Primary	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	Reliable Roofing and Sheet Metal, LLC
200901050010	Georgetown	Penn Brook Elementary School	Design Development	New Construction		Municipal Building Consultants, Inc.	Drummey Rosane Anderson, Inc.	Rist-Frost-Shumway Engineering, P.C.	<u>-</u>
200801050505	Georgetown	Georgetown Middle/High School	OPM Selection						
201101070010G	Gloucester	Beeman Memorial School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070020G	Gloucester	East Gloucester Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
201101070042G	Gloucester	Plum Cove Elementary School	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Built-up Roofing Systems LLC
201101070305G	Gloucester	Ralph B O'Maley Middle	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Titan Roofing, Inc.
201101070045G	Gloucester	Veterans Memorial	Final Audit Approved	Repair - Accelerated	DBB	Knight, Bagge & Anderson Inc.	CGKV Architects, Inc.	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.
200901070050	Gloucester	West Parish Elementary School	Feasibility Study			Knight, Bagge & Anderson Inc.	Dore & Whittier Architects, Inc.		_
200801100505	Grafton	Grafton Memorial Senior	Project Completion	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Symmes Maini & McKee Associates Inc.	, Horizon Engineering Associates, LLP	Dimeo Construction Company
_00001100000	5.4.6	Cratton Momonal Como			0111071				2loo contaction company

Last Updated: 3/13/13

Massachusetts School Building Authority You are Currently Viewing Active Projects. Date of Report:3/13/13

Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	ОРМ	Designer	Cx_Company	CM\GC
201101100505G	Grafton	Grafton Memorial Senior	Final Audit Approved	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent,, Inc.
201101100005G	Grafton	South Grafton Elementary	Closeout	Repair - Accelerated	DBB	URS Corporation	CGKV Architects, Inc.	Horizon Engineering Associates, LLP	AAlanco Service Corporation
201201110010	Granby	West Street School	Eligibility Period						
201108230605	Greater Lawrence RVT Greater Lowell Voc	Greater Lawrence Reg Voc Tech Greater Lowell Regional	Feasibility Study	Repair - Major		Vertex Construction Services  Joslin, Lesser + Associates	Richard D. Kimball Company, Inc.		-
200908280605	Tec Tec	Technical High School  Vocational Technical High	Design Development	Repair - Major		Inc.  Construction Monitoring	Knight, Bagge & Anderson, Inc.	Horizon Engineering Associates, LLP	-
201008250605	Greater New Bedford	School	Design Development	Addition / Renovation		Services, Inc.	Drummey Rosane Anderson, Inc.	Symmes, Maini & McKee Associates	
201101140025G	Greenfield	Four Corners	<b>Project Completion</b>	Repair - Accelerated	DBB	P3 Project Planning Construction Monitoring	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	Five Star Building Corp.
200901140505	Greenfield	Greenfield High School Groton Dunstable Regional	Design Development	New Construction	DBB	Services, Inc.	Dore & Whittier Architects, Inc.	BVH Integrated Services, Inc.	Shawmut Design and Construction
201206730305	Groton-Dunstable	Middle School	Design Development	Repair - Accelerated		Collaborative Partners Strategic Building Solutions,	ICON architecture, inc.	Russo Barr Associates, Inc.	-
201101170505G	Hadley	Hopkins Academy	Closeout	Repair - Accelerated	DBB	LLC Coast & Harbor Associates,	CCS Presentation Systems	Russo Barr Associates, Inc.	MDM Engineering
201206750010	Hamilton-Wenham	Cutler School Minnechaug Regional High	Design Development	Repair - Accelerated		Inc.	CBI Consulting, Inc.	Russo Barr Associates, Inc.	
200806800505	Hampden-Wilbraham	5 5	Project Completion	New Construction	DBB	Pinnacle One, Inc.	Mount Vernon Group Architects, Inc.	. Horizon Engineering Associates, LLP	Fontaine Brothers, Inc.
201001210005G	Hancock	Hancock Elementary School	Project Completion	Repair - Accelerated	DBB	-	Westall Architects		Salco Construction Company, Inc.
200801220505	Hanover	Hanover High School Caleb Dustin Hunking Middle	Closeout	New Construction	DBB	PMA Construction Services Joslin, Lesser + Associates	HMFH Architects, Inc.	Horizon Engineering Associates, LLP	Callahan, Inc.
201201280035	Haverhill	School	Designer Selection			Inc.	-		- New England Builders & Contractors,
201101280100G	Haverhill	Consentino Middle School	Construction	Repair - Accelerated	DBB	Vertex Construction Services	CSS Architects Incorporated	RDK Engineers  Russo Barr Associates, Inc.	Inc. P.J. Dionne Company, Inc.
	Haverhill	High School John G Whittier Middle	Closeout						New England Builders & Contractors,
201101280085G	Haverhill	School	Construction	Repair - Accelerated	DBB		CSS Architects Incorporated	Russo Barr Associates, Inc.	Inc.
201101280075G	Haverhill	Tilton Elementary School Walnut Square Elementary	Project Completion	Repair - Accelerated	DBB		CSS Architects Incorporated	Russo Barr Associates, Inc.	Titan Roofing, Inc. P.J. Dionne Company, Inc. Titan
201101280080G	Haverhill	School	Project Completion	Repair - Accelerated	DBB	Knight, Bagge & Anderson	s CSS Architects Incorporated	RDK Engineers  Russo Barr Associates, Inc.	Roofing, Inc.
201001310410	Hingham	Hingham Middle School Holbrook Junior-Senior High	Construction	New Construction	DBB	Inc. Symmes Maini & McKee	Ai3 Architects LLC	Foreman Building Commissioning, LP	Brait Builders Corp.
200801330505	Holbrook	School	Designer Selection			Associates, Inc.	Design Partnership of Cambridge	,	-
W20034396	Holyoke	Holyoke High School	Closeout	Repair - Major	DBB	- Changles LICA Duilding Inc	Inc.	DVII Integrated Consists Inc	·
201201370605	Holyoke Holyoke	Wm J Dean Voc Tech High Lt. McMahon Elementary School	Design Development  Eligibility Period	Science Lab		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	BVH Integrated Services, Inc.	-
200801410410	Hudson	John F. Kennedy Middle School	Construction	New Construction	DBB	PMA Construction Services	OMR Architects, Inc.	WSP Flack + Kurtz	Bacon-Agostini Construction Joint Venture
200801530505	Leominster	Leominster High School	Construction	Addition / Renovation	CM@R	Daedalus Projects Inc	Lamoureux Pagano & Associates, Inc.	Horizon Engineering Associates, LLP	S.O.M. Construction Ent., Inc.
201201530007	Leominster	Fall Brook	Design Development	Repair - Accelerated	OMOR	Compass Project Management, Inc.	Reinhardt Associates, Inc.	Horizon Engineering Associates, LLP	C.C.M. CONGREGATION ETT., IIIO.
			. Jigit = 1 i ti opinione					· · · · · · · · · · · · · · · · · · ·	

Last Updated: 3/13/13

Last Updated: 3/13/13

Massachusetts School Building Authority You are Currently Viewing Active Projects. Date of Report:3/13/13 Active Projects: 332

MCDAID	Diotriot	School	Phase	Drainat Saana	Procurement	ОРМ	Deciman	Cv Company	CM\GC
MSBA ID	District	School	Phase	Project Scope	Туре	Compass Project	Designer	Cx_Company  Horizon Engineering Associates, LLP Russo Bar	
201201530010	Leominster	Southeast School	Design Development	Repair - Accelerated		Management, Inc.	Reinhardt Associates, Inc.	Associates, Inc.	•
							DiMarinisi & Wolfe Architects Urban		
201101540005G	Leverett	Leverett Elementary School	Project Completion	Repair - Accelerated	DBB	Potomac Capital Advisors	Designers	Russo Barr Associates, Inc.	-
201101550010E	Lexington	Joseph Estabrook Elementary School	y Construction	New Construction		RF Walsh Collaborative Partners	DiNisco Design Partnership, Limited	PVH Integrated Services Inc	Shawmut Design and Construction
201101330010E	Lexington	301001	Approved Project Vote	New Construction		raitileis	Dinisco Design Faithership, Limited	BVH Integrated Services, Inc.	Shawmut Design and Construction
200901570025	Lincoln	Lincoln School	Pending	Addition / Renovation		Skanska USA Building, Inc	OMR Architects, Inc.		-
						Joslin, Lesser + Associates			
200801590505	Longmeadow	Longmeadow High School	Construction	New Construction	CM@R	Inc.	OMR Architects, Inc.	Foreman Building Commissioning, LP	Gilbane Building Company
201101600505G	Lowell	Lowell High School	Project Completion	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	_
2011010003030	Lowell	Lowell Flight Control	1 roject completion	Ropali Accolorated	000	NETCO Construction Project	•	Dullaring Errorosure 7 (3300) ates	
201101600027G	Lowell	Moody Elementary School	Construction	Repair - Accelerated	DBB	Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	Paul J. Rogan Co., Inc.
						NETCO Construction Project			
201101600040G	Lowell	Peter W Reilly School	Project Completion	Repair - Accelerated	DBB	Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates	
201101600055G	Lowell	Washington School	Construction	Repair - Accelerated	DBB	NETCO Construction Project Managers, Inc.	ICON architecture, inc.	Building Enclosure Associates  RDK Engineers	Alpha Contracting Associates, Inc.
2011010000000	LOWCII	vvasnington ochool	Construction	Ropali Accolorated	000	Joslin, Lesser + Associates	10014 dioliteotare, inc.	Dullaring Errorosare 7.6350clates   NDN Errigineers	7 lipha Contracting 7 losociates, inc.
200801620505	Lunenburg	Lunenburg High School	Feasibility Study			Inc.	Tappe Associates, Inc.		-
						Diversified Project			
201201630405	Lynn	Breed Middle School	Design Development	Repair - Accelerated		Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	
200901630305	Lynn	Thurgood Marshall Middle School	Feasibility Study			Joslin, Lesser + Associates Inc.	Raymond Design Associates, Inc.		_
		3.1.33.	. odolomy otday			Diversified Project	maye.ia 2 co.g. mecalatec, inc.		_
201201630605	Lynn	Lynn Vocational Tech Institute	e Design Development	Repair- Accelerated		Management	Kaestle Boos Associates, Inc.	CBI Consulting Inc.	
000004040505			B 1 4 B 1 4	A 1122 / D		LIEED)/	EL 18 4 12 4 1	F: 0.T. : A. :	5 A O II
200901640505	Lynnfield	Lynnfield High School	Project Completion	Addition / Renovation	DBB	HEERY	Edward Rowse Architects, Inc.	Fitzemeyer & Tocci Associates, Inc.	E.A. Collangeli Construction Co., Inc.
W20024319	Malden	Malden High School	Closeout	Addition / Renovation	CM@R	URS Corporation	Flansburgh Associates, Inc.		Gilbane Building Company
	Manchester Essex	Manchester Essex Regional					Mount Vernon Group Architects,		
200806980610	Regional	High School	Final Audit Approved	New Construction	DBB	Design Technique Inc.	Inc.		TLT Construction Corporation
200004600020	Marklahaad	Clayer Florenton, School	Construction	Now Construction	DDD	Municipal Building	IC I Architecture DC	DDV Engineers	C. 9. D. Comptunation. Inc.
200801680020	Marblehead	Glover Elementary School Francis J Kane Elementary	Construction	New Construction	DBB	Consultants, Inc.  RF Walsh Collaborative	JCJ Architecture, PC	RDK Engineers	G & R Construction, Inc.
201101700008G	Marlborough	School	Project Completion	Repair - Accelerated	DBB	Partners	Baker/Wohl Architects, Inc.	Building Enclosure Associates	A&A Window Products, Inc.
	-					RF Walsh Collaborative		<del>-</del>	McAnespie, Inc.  Veterans
201101700505G	Marlborough	Marlborough High School	Closeout	Repair - Accelerated	DBB	Partners	Baker/Wohl Architects, Inc.	RDK Engineers Building Enclosure Associates	Development Corporation, Inc.
200801710020	Marshfield	Governor Edward Winslow Elementary School	Closeout	Repair - Major	DBB	Vartay Construction Sarvices	Knight, Bagge & Anderson, Inc.	RDK Engineers	Enterprise Equipment Co., Inc.
200001710020	Warshilled	Liementary concor	01030001	repair iviajor	000	Compass Project	Tringitt, Bagge & Attactson, me.	NDN Engineers	Enterprise Equipment 66., inc.
201101710505	Marshfield	Marshfield High School	Construction	New Construction	DBB	Management, Inc.	Ai3 Architects LLC	Sebesta Blomberg & Associates, Inc.	Brait Builders Corp.
						Municipal Building			
200801740505	Maynard	Maynard High School	Construction	New Construction	DBB	Consultants, Inc.	Tappe Associates, Inc.	WSP Flack + Kurtz	CTA Construction Co., Inc.
201201760505	Medford	Medford High School	Design Development	Science Lab		Leftfield, LLC	DiNisco Design Partnership, Limited	Cannon Design	_
201201100000	Modrord	Woodierd Fright Corroot	200igii 2010iopiiioiit	00:0:100 240		Compass Project	Divided Decigit : artiferent, Emitted	Carnott Boolgit	_
200801770305	Medway	Medway Middle School	Project Completion	Repair - Major	CM@R	Management, Inc.	Knight, Bagge & Anderson, Inc.	Sebesta Blomberg & Associates, Inc.	Consigli Construction Company, Inc.
004004700505						001/0 11 1 1 0	A'0 A 1'' 4 11 0	MOD FL. L. K.	
201201780505	Melrose	Melrose High School	Design Development	Science Lab		CPI/Collaborative Partners  Municipal Building	Ai3 Architects LLC	WSP Flack + Kurtz	Commercial Roofing and Contracting,
201101780505G	Melrose	Melrose High School	Final Audit Approved	Repair - Accelerated	DBB	Consultants, Inc.	Gale Associates, Inc.	Russo Barr Associates, Inc.	Inc.
				-1					
201107100015G	Mendon-Upton	Miscoe Hill School	Project Completion	Repair - Accelerated	DBB	Maguire Group Inc.		. Sebesta Blomberg & Associates, Inc.	Greenwood Industries, Inc.
000004040505	Mathuan	Matheman High October	Construction	Addition / December	01100	IXD A /Taida at	Finegold Alexander and Associates	Facility and the late and Facility and	Disease Constitute in Constitute Constitute
200801810505	Methuen	Methuen High School	Construction	Addition / Renovation	CM@R	KBA/Trident	Inc.	Environmental Health and Engineering	Dimeo Construction Company
Page 6 o	of 12								

Date of Report:3/13/13

You are Currently Viewing Active Projects.

Green Repair Accelera

Accelerated Repair

Waitlist

Science Lab Initiative

Last Updated: 3/13/13

Active Projects: 332 **Procurement** OPM CM\GC MSBA ID District School Phase **Project Scope** Designer Cx\_Company Type Mary K. Goode Elementary 201101820025G Middleborough School Closeout Repair - Accelerated DBB Maguire Group Inc. Habeeb & Associates Architects, Inc. Russo Barr Associates, Inc. J.J. Cardosi, Inc. RF Walsh Collaborative DBB 200801840005 Middleton Howe-Manning School Closeout **New Construction** Partners DiNisco Design Partnership, Limited Foreman Building Commissioning, LP CTA Construction Co., Inc. Joslin, Lesser + Associates 201101850090 Milford Woodland Elementary School Designer Selection **HMFH Architects. Inc.** Inc. Lamoureux Pagano & Associates, Minuteman Regional High 200908300605 Minuteman Voc Tech School (Career Tech) **Designer Selection** Skanska USA Building, Inc. 201107170005G Mohawk Trail Buckland-Shelburne Reg Repair - Accelerated DBB Potomac Capital Advisors Strategic Building Solutions, LLC Closeout Bradley Architects, Inc. 01107170010G Mohawk Trail Colrain Central School Repair - Accelerated DBB Potomac Capital Advisors Bradley Architects, Inc. Strategic Building Solutions, LLC Closeout Mohawk Trail Reg High 01107170505G Mohawk Trail DBB Bradley Architects, Inc. Strategic Building Solutions, LLC School **Project Completion** Repair - Accelerated Potomac Capital Advisors Monomoy Regional High Fontaine Brothers, Inc. 201122229999 Monomov School Construction **New Construction** Skanska USA Building, Inc. Mount Vernon Group Architects, Inc. Sebesta Blomberg & Associates, Inc. DiMarinisi & Wolfe Architects Urban 201107200305G Narragansett Middle School Final Audit Approved Repair - Accelerated DBB Potomac Capital Advisors Rist-Frost-Shumway Engineering, P.C. Narragansett Designers Phillipston Memorial DiMarinisi & Wolfe Architects Urban Designers 201107200003G Narragansett Elementary School **Project Completion** Repair - Accelerated DBB Potomac Capital Advisors Rist-Frost-Shumway Engineering, P.C. Strategic Building Solutions, Symmes Maini & McKee Associates, Templeton Center School Feasibility Study 200807200020 Narragansett Repair - Major LLC Pompositticut Elementary Construction Monitoring Symmes Maini & McKee Associates. 200807250015 Nashoba School **Project Completion** Addition / Renovation DBB Services, Inc. Inc. Strategic Building Solutions, LLC P.J. Stella Construction Corp. Nashoba Valley Technical 200908520605G Nashoba Valley Tech High School Closeout Repair - Accelerated DBB RF Walsh Collaborative DBB 200801980505 Natick High School **Project Completion New Construction** Ai3 Architects LLC Rist-Frost-Shumway Engineering, P.C. Natick Partners **NETCO Construction Project** Capeway Roofing Systems, Inc.| 201106600505G Nauset Nauset Regional High School Project Completion Repair - Accelerated DBB Habeeb & Associates Architects, Inc. CBI Consulting Inc. Modern Glass & Aluminum, Inc. Managers, Inc. Steven H. Popper - Town Consigli Construction Company, Inc. CM@R 200901990050 Needham Newman Elementary School Closeout Repair - Major Drummey Rosane Anderson, Inc. Rist-Frost-Shumway Engineering, P.C. Triumph Leasing Corporation **Employee** 01101990405G Needham Pollard Middle **Final Audit Approved** Repair - Accelerated DBB STV Incorporated Gale Associates, Inc. CBI Consulting Inc. Wayne Roofing Systems, LLC 200902010070 New Bedford John Hannigan **OPM Selection** 201002010505 New Bedford High School DBB New Bedford Closeout Swift River Elementary School Closeout DBB RAC Builders, Inc. 201107280015G New Salem-Wendell Repair - Accelerated Maguire Group Inc. Bradley Architects, Inc. Strategic Building Solutions, LLC Francis T Bresnahan 201102040005 Newburyport Elementary School Design Development **New Construction** HEERY HMFH Architects. Inc. Fitzemeyer & Tocci Associates, Inc. 201002040305 Newburyport Rupert A. Nock Middle School Design Development Addition / Renovation HEERY Miller Dyer Spears Inc. Fitzemeyer & Tocci Associates, Inc. Joslin, Lesser + Associates DiNisco Design Partnership, 201102070005 A E Angier Elementary School Feasibility Study Newton DBB 01102070015G Newton Bowen Closeout Repair - Accelerated **STV Incorporated** Habeeb & Associates Architects, Inc. W20014216 Newton North High School Closeout CM@R Newton **New Construction Turner Construction Co.** Dore & Whittier Architects, Inc. **Dimeo Construction Company Habeeb & Associates Architects,** 201102070125G Newton Williams Elementary School Closeout Repair - Accelerated DBB **STV** Incorporated Freeman-Kennedy Joslin, Lesser + Associates DBB Elementary School **Project Completion New Construction** Flansburgh Associates, Inc. WSP Flack + Kurtz Fontaine Brothers, Inc. 200802080005 Norfolk Norfolk County Norfolk County Agricultural Compass Project 200909150705 High School Construction Addition / Renovation DBB Management, Inc. Turowski2 Architecture, Inc. Rist-Frost-Shumway Engineering, P.C. **TLT Construction Corporation** Agriculture

Massachusetts School Building Authority You are Currently Viewing Active Projects.

Date of Report:3/13/13 Active Projects: 332  Last Updated: 3/13/13

**Procurement** CM\GC MSBA ID District School Phase **Project Scope** OPM Designer Cx\_Company Type Strategic Building Solutions Approved Project Vote 200802090305 North Adams Silvio O Conte Middle School Pending Addition / Renovation Margo Jones Architects, Inc. Municipal Building DBB 01102110018G North Andover Annie L Sargent School Repair - Accelerated Consultants, Inc. ICON architecture, inc. Cannon Design Varieka Construction, Inc. Municipal Building 201102110001G North Andover Atkinson School Closeout DBB Consultants, Inc. ICON architecture, inc. Cannon Design Paul J. Rogan Co., Inc. Repair - Accelerated Municipal Building 201102110305G North Andover North Andover Middle School Closeout Repair - Accelerated DBB Consultants, Inc. ICON architecture, inc. Cannon Design Stanley Roofing Company, Inc. Atlantic Construction and 201102120010G North Attleborough Falls Elementary School Closeout Repair - Accelerated DBB Management, Inc. Gale Associates, Inc. Northeast Energy Control Systems CSS Architects Incorporated 201202120505 North Attleborough North Attleboro High Skanska USA Building, Inc. Kaestle Boos Associates, Inc. Consulting Engineering Services, LLC **Design Development Science Lab** Rossevelt Avenue Elementary 201202120015 North Attleborough Skanska USA Building, Inc Russo Barr Associates, Inc. Gale Associates, Inc. School Design Development Repair- Accelerated North Brookfield Elementary Strategic Building Solutions 201202150015 North Brookfield School Design Development Repair- Accelerated CBI Consulting, Inc. Simpson Gumpertz & Heger Inc. **Vertex Construction** North Brookfield Elementary DBB 201102150015G North Brookfield Repair - Accelerated LPBA/ Architects, Inc. Simpson Gumpertz & Heger Inc. **Lockheed Window Corporations** School **Project Completion** Services Compass Project 201107350010G North Middlesex Ashby Elementary Closeout Repair - Accelerated DBB Management, Inc. Russo Barr Associates, Inc. **Building Enclosure Associates** Greenwood Industries, Inc.| GVW, Inc. North Middlesex Regional Symmes Maini & McKee Associates HEERY 201107350505 North Middlesex High School **Designer Selection** Compass Project 201107350005G North Middlesex Spaulding Memorial Closeout Repair - Accelerated DBB Management, Inc. Russo Barr Associates, Inc. **Building Enclosure Associates** MDM Engineering 201002170505 North Reading North Reading High School Construction Addition / Renovation CM@R PMA Construction Services Dore & Whittier Architects, Inc. Cannon Design Strategic Building Solutions, Lincoln Street Elementary LLC 201102130003 School Designer Selection Northborough Robert E. Melican Middle 201102130305G Northborough **Final Audit Approved** Repair - Accelerated DBB Pinck & Co., Inc. ICON architecture, inc. Strategic Building Solutions, LLC AAlanco Service Corporation School Joslin, Lesser + Associates 201202180015 J C Solmonese **Design Development** Repair - Accelerated Habeeb & Associates Architects, Inc. Simpson Gumpertz & Heger Inc. Norton 200902180505 Norton Norton High School CM@R Pinck & Co., Inc. JCJ Architecture, PC Rist-Frost-Shumway Engineering, P.C. W. T. Rich Company Inc. Construction Addition / Renovation Compass Project DBB Management, Inc. Ai3 Architects LLC Agostini Construction Co., Inc. 200802200505 Norwood Norwood High School Closeout **New Construction** Old Colony Reg Voc Vocational Technical High Vertex Construction Services -Consulting Engineering Services, LLC 200908550605 Tech School Design Development Repair - Maior **Diversified Project** 200802260405 Oxford Oxford Middle School CGKV Architects, Inc. S.O.M. Construction Ent,, Inc. Construction Repair - Maior Management Cannon Design **Diversified Project** Royal Steam Heater Co.| Titan 201102270305G Palmer Converse Middle School **Project Completion** Repair - Accelerated DBB Management Tighe & Bond, Inc. Strategic Building Solutions, LLC Roofing, Inc. Old Mill Pond Elementary **Diversified Project** 201102270008G Palmer School **Project Completion** Repair - Accelerated DBB Management Tighe & Bond, Inc. Strategic Building Solutions, LLC Royal Steam Heater Co. **Diversified Project** Royal Steam Heater Co.| Titan 201102270505G Palmer Palmer High School **Project Completion** Repair - Accelerated DBB Management Tighe & Bond, Inc. Strategic Building Solutions, LLC Roofing, Inc. J Henry Higgins Middle 200802290305 Peabody School **Project Scope & Budget New Construction** Daedalus Projects Inc DiNisco Design Partnership, Limited Daedalus Projects Inc 201102290007G John E Burke School DBB Peabody **Project Completion** Repair - Accelerated LPBA/ Architects, Inc. Sebesta Blomberg & Associates, Inc. 201102290027G Peabody William A Welch Sr Closeout Repair - Accelerated DBB Daedalus Projects Inc LPBA/ Architects, Inc. Sebesta Blomberg & Associates, Inc. DBB 201107450020G Dr Frederick N Sweetsir Closeout Repair - Accelerated PMA Construction Services Knight, Bagge & Anderson, Inc. CBI Consulting Inc./RDK Engineers E. Amanti & Sons, Inc. Pentucket 201107450015G Pentucket Dr John C Page School Closeout Repair - Accelerated DBB PMA Construction Services Knight, Bagge & Anderson, Inc. CBI Consulting Inc./RDK Engineers Capeway Roofing Systems, Inc.

Massachusetts School Building Authority You are Currently Viewing Active Projects.

Date of Report:3/13/13 Active Projects: 332 Last Updated: 3/13/13

**Procurement** OPM CM\GC MSBA ID District School Phase **Project Scope** Designer Cx\_Company Type 201107450005G Pentucket Elmer S Bagnall Closeout Repair - Accelerated DBB PMA Construction Services Knight, Bagge & Anderson, Inc. CBI Consulting Inc./RDK Engineers Gibson Roofs, Inc. DBB 201107450010G Pentucket Helen R Donaghue School Closeout Repair - Accelerated PMA Construction Services Knight, Bagge & Anderson, Inc. CBI Consulting Inc. Gibson Roofs, Inc. Northfield Elementary **Diversified Project** 201107500008G Pioneer Valley Elementary School Closeout DBB Management CGKV Architects, Inc. Strategic Building Solutions, LLC Repair - Accelerated **Diversified Project** Pioneer Valley Reg Middle 201107500505G Pioneer Valley School/High School **Project Completion** Repair - Accelerated DBB Management CGKV Architects, Inc. Strategic Building Solutions, LLC 201002360510 Pittsfield Taconic High School Feasibility Study Skanska USA Building, Inc -201202390515 Plymouth South High School OPM Selection Plymouth 200802390505 Plymouth North High School DBB Plymouth **Project Completion New Construction** Ted Gentry Associates, Inc Ai3 Architects LLC Sebesta Blomberg & Associates, Inc. J & J Contractors, Inc. Quabbin Regional High 201007530505G DBB **Building Enclosure Associates** Quabbin School **Final Audit Approved** Repair - Accelerated Vertex Construction Services LPBA/ Architects, Inc. Kronenberger & Sons Restoration, INc. Ruggles Lane Elementary DBB 201207530030 Quabbin School Design Development Repair - Accelerated Vertex Construction Services Turowski2 Architecture, Inc. Simpson Gumpertz & Heger Inc. Coast & Harbor Associates. Warren Community 201207780005 Quaboag Elementary School **Design Development** Repair - Accelerated Lindgren & Sharples, Inc. Strategic Building Solutions, LLC **Tishman Construction** Central Middle School DBB 200802430315 Quincy Construction **New Construction** Corporation of MA Ai3 Architects LLC Sebesta Blomberg & Associates, Inc. H.V. Collins Co., Inc. Birch Meadow Elementary 201102460005G Reading School **Final Audit Approved** Repair - Accelerated DBB **KBA Architects** LPBA/ Architects, Inc. Russo Barr Associates, Inc. Paul J. Rogan Co., Inc. J Warren Killam Elementary 201102460017G Reading School **Final Audit Approved** Repair - Accelerated DBB **KBA Architects** LPBA/ Architects, Inc. Russo Barr Associates, Inc. Capeway Roofing Systems, Inc. William McKinley Elementary RF Walsh Collaborative **Approved Project Vote** 201002480035 School **Pending** Partners Revere **New Construction Drummey Rosane Anderson, Inc.** 200802500005 Rochester Rochester Memorial School **Final Audit Approved** Addition / Renovation CM@R PMA Construction Services Horizon Engineering Associates, LLP Gilbane Building Company Flansburgh Associates, Inc. John W. Rogers Middle CM@R Agostini Construction Co., Inc. 200802510305 Rockland Construction Daedalus Projects Inc Dore & Whittier Architects, Inc. Consulting Engineering Services, LLC School **New Construction** 201102510025G Rockland R Stewart Esten DBB Daedalus Projects Inc Habeeb & Associates Architects, Inc. Russo Barr Associates, Inc. Northeast Energy Control Systems Closeout Repair - Accelerated CM@R 200902580305G Collins Middle School Rist-Frost-Shumway Engineering, P.C. Salem Construction Repair - Accelerated KV Associates, Inc. Reinhardt Associates, Inc. Gilbane Building Company 201002580050G Salem Saltonstall School CM@R Construction Repair - Accelerated KV Associates. Inc. Reinhardt Associates, Inc. Rist-Frost-Shumway Engineering, P.C. Gilbane Building Company **NETCO Construction Project** Forestdale School DBB Habeeb & Associates Architects, Inc. Gale Associates, Inc. 201102610010G Sandwich Closeout Repair - Accelerated Managers, Inc. Varieka Construction, Inc. **NETCO Construction Project** DBB 00902610025G Sandwich Oak Ridge School Closeout Repair - Accelerated Managers, Inc. Habeeb & Associates Architects, Inc. Gale Associates, Inc. J.J. Cardosi, Inc. Fletcher Thompson Architecture 201002620305 Saugus Belmonte Middle School Construction Repair - Major CM@R Skanska USA Building, Inc Engineering, LLC Consulting Engineering Services, LLC Consigli Construction Company, Inc. 201202640305 Scituate Gates Intermediate School Eligibility Period CM@R Daedalus Projects Inc 200802660305 Sharon Sharon Middle School Closeout Addition / Renovation Kaestle Boos Associates, Inc. Horizon Engineering Associates, LLP Consigli Construction Company, Inc. Shawsheen Valley Shawsheen Valley Voc Tech Construction Monitoring 201008710605 Addition / Renovation DBB Voc Tech High School Services, Inc. Knight, Bagge & Anderson, Inc. Colantonio, Inc. **Final Audit Approved** Shawsheen Valley Voc Tech **Diversified Project** Shawsheen Valley 201208710605 Voc Tech High School Repair- Accelerated Management Shekar & Associates, Inc. Fitzemeyer & Tocci Associates, Inc. **Design Development** Lamoureux Pagano & Associates, CM@R Gilbane Building Company Sherwood Middle School **New Construction PMA Construction Services RDK Engineers** 200802710305 Shrewsbury **Project Completion** Spring Street Elementary 01102710035G Shrewsbury School **Project Completion** Repair - Accelerated DBB PMA Construction Services Habeeb & Associates Architects, Inc. Cannon Design Lambrian Construction Corp.

Date of Report:3/13/13

You are Currently Viewing Active Projects.

Green Repair

Accelerated Repair

Waitlist

Science Lab Initiative

Last Updated: 3/13/13

Active Projects: 332 **Procurement** MSBA ID District School Phase **Project Scope** OPM Designer Cx\_Company CM\GC Type Somerset-Berkley High **Bacon-Agostini Construction Joint** Somerset-Berkley Construction **New Construction** Skanska USA Building, Inc Ai3 Architects LLC Horizon Engineering Associates, LLP Venture 200811119999 School East Somerville Community CM@R 200902740111E Somerville School at Cummings Construction Addition / Renovation PMA Construction Services Maguire Group, Inc. Foreman Building Commissioning, LP Gilbane Building Company 200902780015 South Hadley Plains School **Design Development** Margo Jones Architects, Inc. **New Construction** Arcadis South Shore Reg Voc South Shore Vocational 200808730605G Technical High School Repair - Accelerated DBB Vertex Construction Services Gale Associates, Inc. **Building Enclosure Associates** Tech Closeout Joslin, Lesser + Associates 200802770505 Southbridge Southbridge High School **Project Completion New Construction** CM@R Tappe Associates, Inc. Environmental Health and Engineering Consigli Construction Company, Inc. Inc. William E. Norris Elementary **Approved Project Vote Tishman Construction** 201202750005 Southampton Repair - Accelerated Corporation of MA Reinhardt Associates, Inc. **Building Enclosure Associates Pending** Southeastern Reg Voc Southeastern Regional RF Walsh Collaborative 200908720605 Vocational Technical School CM@R **RDK Engineers** W. T. Rich Company Inc. Construction Addition / Renovation Partners Drummey Rosane Anderson, Inc. Tech Southern Worcester Bay Path Regional Vocational DBB **HEERY** 200908760605 Cty VT Technical High School Design Development Addition / Renovation Kaestle Boos Associates, Inc. **RDK Engineers** Consigli Construction Company, Inc. Strategic Building Solutions 201107660505 Southwick-Tolland Regional High School Addition / Renovation LLC JCJ Architecture, PC BVH Integrated Services, Inc. Design Development Design Partnership of Cambridge, Dore and Whittier Architects. 200807670505 Spencer-E Brookfield David Prouty High School **Schematic Design** Addition / Renovation Inc. **Springfield** SCIPP Year 2 **Project Completion SCIPP Year 3 Springfield** Construction Dryden Veterans Memorial 201102810125E Springfield Elementary School Construction Addition / Renovation CM@R **Arcadis** Drummey Rosane Anderson, Inc. BVH Integrated Services, Inc. Elias Brookings Elementary Design Development CM@R 201102810030E School **Arcadis** Drummey Rosane Anderson, Inc. BVH Integrated Services, Inc. Springfield **New Construction** W20014137 Springfield Forest Park Middle School Construction Addition / Renovation CM@R Arcadis Perkins Eastman Foreman Building Commissioning, LP Consigli Construction Company, Inc. Roger L. Putnam Vocational W20054428 CM@R Springfield Technical High School **New Construction** Pinnacle One, Inc. Drumney Rosane Anderson Inc. Strategic Building Solutions, LLC **Project Completion** Consigli/Morganti Approved Project Vote 201202810500 Springfield Central High School Leftfield, LLC DiNisco Design Partnership, Limited Horizon Engineering Associates, LLP Pending **Science Lab** Joslin, Lesser + Associates Stoneham Middle School CM@R Shawmut Design and Construction 200902840405 Stoneham Design Development Addition / Renovation Tappe Associates, Inc. **RDK Engineers** Lamoureux Pagano & 200802870005 Burgess Elementary School DBB Horizon Engineering Associates, LLP Sturbridge **Project Completion** Addition / Renovation Associates, Inc. Drummey Rosane Anderson, Inc. Fontaine Brothers, Inc. Peter Noyes Elementary Compass Project DBB Gibson Roofs, Inc. 201102880030G Sudbury School Repair - Accelerated Management, Inc. Russo Barr Associates, Inc. **RDK Engineers** Final Audit Approved General John Nixon 201202880025 Sudbury Elementary School Design Development Repair - Accelerated **PMA Construction Services** ICON architecture, inc. Gale Associates, Inc. Strategic Building Solutions 200802900305 Sutton Sutton Middle School Construction Addition / Renovation DBB LLC Flansburgh Associates, Inc. **RDK Engineers TLT Construction Corporation** Hadley Elementary School **OPM Selection** 201102910010 Swampscott **Diversified Project** Tantasqua Regional Jr High DBB 01107700405G Tantasqua School **Final Audit Approved** Repair- Accelerated Management Habeeb & Associates Architects, Inc. Greenwood Industries, Inc. **Approved Project Vote** 201202930057 Harold H Galligan School Gale Associates, Inc. Taunton **Pending** Repair - Accelerated Arcadis Knight, Bagge & Anderson, Inc. Parker Middle/Taunton High Bacon-Agostini Construction Joint Design Partnership of Cambridge, W20014194 Taunton School Closeout Addition / Renovation CM@R Gilbane Building Company Venture Tewksbury Memorial High Symmes Maini & McKee Associates, DBB **HEERY** Sebesta Blomberg & Associates, Inc. CTA Ventures 200802950505 Tewksbury School **Project Completion New Construction** Inc. 201208780605 Tri County Reg Voc Tech **Design Development Science Lab** Collaborative Partners Ai3 Architects LLC Tri County

Massachusetts School Building Authority
You are Currently Viewing Active Projects.
Date of Report: 3/13/13
Active Projects: 332

MSRAID District School Building Authority
Procurement
Type OPM Designer Cx Company

					Procurement				
MSBA ID	District	School	Phase	Project Scope	Туре	OPM	Designer	Cx_Company	CM\GC
201109700605G	Upper Cape Cod Voc		Project Completion	Popair Accolorated	DBB	NETCO Construction Project	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Modern Glass & Aluminum, Inc.
201108790605G	Tech	Upper Cape Cod Voc Tech	Project Completion	Repair - Accelerated	DDD	Managers, Inc.  Joslin, Lesser + Associates	Knight, Bagge & Anderson, Inc.	Gale Associates, Inc.	Wodern Glass & Aluminum, Inc.
200803040505	Uxbridge	Uxbridge High School	Project Completion	New Construction	CM@R	Inc.	Raymond Design Associates, Inc.	Turner Facilities Management Solutions	Shawmut Design and Construction
200000010000	CADITAGO	Chanage Filgit Control	Troject Completion	Trow Contact delicit	OMOTO	Gary Kaczmarek - Town	Lamoureux Pagano & Associates,	Tarrior Facilities Management Colditions	Chamilat Boolgh and Concludetion
200907750305	Wachusett	Mountview Middle School	Project Scope & Budget			Employee	Inc.		-
						Strategic Building Solutions,			
201107750035G	Wachusett	Naquag Elementary School	Closeout	Repair - Accelerated	DBB	LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
0044077500400	) A/	D . O . O		B . A	555	Strategic Building Solutions,	1004/4 17 1	D: 15 10 5 1 1 D 0	MDME
201107750040G	Wachusett	Paxton Center School	Closeout	Repair - Accelerated	DBB	LLC Strategic Building Solutions,	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
201107750045G	Wachusett	Thomas Prince School	Construction	Repair - Accelerated	DBB	LLC	LPBA/ Architects, Inc.	Rist-Frost-Shumway Engineering, P.C.	MDM Engineering
2011011000100	Wadnadatt	Thomas Times Concor	Ochotraction	Ropan Roodiciated	555	Joslin, Lesser + Associates	El Bry ruemicolo, me.	Tribe i robe chamway Engineering, i .o.	WEW Engineering
201003050310	Wakefield	Galvin Middle School	Design Development	New Construction	CM@R	Inc.	Tappe Associates, Inc.	B2Q Associates, Inc.	Bond Brothers, Inc.
			Approved Project Vote			Joslin, Lesser + Associates	DiMarinisi & Wolfe Architects Urban		
201203150305	Wayland	Wayland Middle School	Pending	Repair - Accelerated		Inc.	Designers	CBI Consulting Inc.	
200803150505	Wayland	Wayland High School	Closeout	New Construction	CM@R	KV Associates, Inc.	HMFH Architects, Inc.	WSP Flack + Kurtz	Shawmut Design and Construction
200903160015	Webster	Park Avenue Elementary School	Design Development	New Construction	DBB	RF Walsh Collaborative Partners	Dore & Whittier Architects, Inc.	Cannon Design	_
200903100013	Webster	361001	Design Development	New Construction	DDD	i artifers	Symmes Maini & McKee Associates,	Carrion Design	
200803170505	Wellesley	Wellesley Senior High School	Closeout	New Construction	CM@R	Ryegate, Inc.	Inc.	Rist-Frost-Shumway Engineering, P.C.	Turner Construction Company
		, , ,						, , ,	
201103220005G	West Boylston	Major Edwards Elementary	Project Completion	Repair - Accelerated	DBB	URS Corporation	Reinhardt Associates, Inc.	Cannon Design	-
		West Bridgewater Middle-				Strategic Building Solutions,			
201003230505	West Bridgewater	Senior High School	Design Development	New Construction		LLC	Flansburgh Associates, Inc.	Cannon Design	-
200903320505	West Springfield	West Springfield High School	Construction	New Construction	DBB	Strategic Building Solutions, LLC	Symmes Maini & McKee Associates, Inc.	Turner Facilities Management Solutions	Fontaine Brothers, Inc.
200903320303	vvest Springheid	West Springheid Flight School	Construction	New Construction	DDD	LLC	IIIC.	Turrier Facilities Mariagement Solutions	Tortaine biothers, inc.
200903210305	Westborough	Gibbons Middle School	Designer Selection			HEERY	-		-
	<u> </u>	Abner Gibbs Elementary							
200903250020	Westfield	School	Construction	New Construction	DBB	Skanska USA Building, Inc	Margo Jones Architects, Inc.	Horizon Engineering Associates, LLP	-
0044000500050	) A ( ( ( ) ) )				555	D0 D : DI :			
201103250025G	Westfield	Highland Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.		
201003250025G	Westfield	Highland Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	_
2010002000200	VVCotinoid	Munger Hill Elementary	Tilla Addit Approved	Ropan Roodiciated	555	r o r roject r iarming	rigile a Bolla, illo.	Chategie Banarig Colutions, EEG	
201103250033E	Westfield	School	Design Development	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
				•					
201103250036G	Westfield	Paper Mill Elementary School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
0040005000	)A/ - (C. 1.1	D 1471 - 1 0 1 1	B 1 B 1				K:1.5		
201203250036	Westfield	Paper Mill Elementary School	Design Development	Repair - Accelerated		Vertex Construction Services	Knight, Bagge & Anderson, Inc.	Building Enclosure Associates	
201103250040G	Westfield	Southampton Road Elementary School	Closeout	Repair - Accelerated	DBB	P3 Inc.	Tighe & Bond, Inc.		
2011002000100	VVCotiloid	Southampton Road	Oloscout	Ropan Roodiciated	555	1 0 1110.	right & Boha, mo.		
201003250040G	Westfield	Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	R & H Roofing
		-							
201103250505G	Westfield	Westfield High School	Closeout	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	-
004400050050	\\\ \ = 46° = 1 d	Westfield Voc Tech High	B 1 4 B 1 1 1	Density As I to 1		D0 D 1 (D)		Observation De Maliana Orderia	
201103250605G	Westfield	School	Project Completion	Repair - Accelerated	DBB	P3 Project Planning	Tighe & Bond, Inc.	Strategic Building Solutions, LLC	<u>-</u>
200903300012	Weston	Field Elementary School	Construction	New Construction	DBB	Compass Project Management, Inc.	Jonathan Levi Architects LLC	Foreman Building Commissioning, LP	Colantonio, Inc.
2000000012	7700011	1 Ioid Elomonitary Oction	- Ondi dollon	. 1011 00110111011011		Compass Project	Garcia Galuska DeSousa Consulting		Columbia, inc.
201103300505G	Weston	Weston High School	Closeout	Repair - Accelerated	DBB	Management, Inc.	Engineers Inc.	RDK Engineers	-
				•		Compass Project	·		
201103300305G	Weston	Weston Middle School	Final Audit Approved	Repair - Accelerated	DBB	Management, Inc.	Russo Barr Associates, Inc.	RDK Engineers	Greenwood Industries, Inc.
			<del></del>						

Massachusetts School Building Authority You are Currently Viewing Active Projects. Date of Report:3/13/13 Active Projects: 332

MSBA ID	District	School	Phase	Project Scope	Procurement Type	ОРМ	Designer	Cx_Company	CM\GC
201103310015G	Westport	Alice A Macomber Primary	Closeout	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	<u>-</u>
201103310505G	Westport	Westport High School	Construction	Repair - Accelerated	DBB	Pinck & Co., Inc.	CGKV Architects, Inc.	CBI Consulting Inc.	
201103360310G	Weymouth	Abigail Adams Middle School	Final Audit Approved	Repair - Accelerated	DBB	KBA Architects	Gale Associates, Inc.	Cannon Design	Greenwood Industries, Inc.
201203360080	Weymouth	William Seach Primary	Construction	Repair - Accelerated				B2Q Associates, Inc.	
201107800030G	Whitman-Hanson	John H Duval Jr Elmentary School	Final Audit Approved	Repair - Accelerated	DBB	-	BETA Group, Inc.		S.I. Services, Inc.
200907800025	Whitman-Hanson	Maquan Elementary School	Schematic Design			Knight, Bagge & Anderson Inc.	Turowski2 Architecture, Inc.		-
200803400005	Williamsburg	Anne T. Dunphy School	Design Development	Addition / Renovation	DBB	Arcadis	Drummey Rosane Anderson, Inc.	B2Q Associates, Inc.	-
201203420060	Wilmington	North Intermediate	Approved Project Vote Pending	Repair - Accelerated				CBI Consulting Inc.	_
201103420025G	Wilmington	Shawsheen Elementary School	Final Audit Approved	Repair - Accelerated	DBB	P3 Inc.	Russo Barr Associates, Inc.	CBI Consulting Inc.	Lockheed Window Corporations
200903420505	Wilmington	Wilmington High School	Construction	New Construction	CM@R	Joslin, Lesser + Associates Inc.	Dore & Whittier Architects, Inc.	Symmes, Maini & McKee Associates	Gilbane Building Company
200803440025	Winchester	Vinson-Owen Elementary School	Construction	New Construction	DBB	Skanska USA Building, Inc		Turner Facilities Management Solutions	CTA Construction Co., Inc.
201003440505	Winchester	Winchester High School	Feasibility Study			Skanska USA Building, Inc	Symmes Maini & McKee Associated Inc.	S,	-
200803460505	Winthrop	Winthrop Sr High School	Feasibility Study			Skanska USA Building, Inc	HMFH Architects, Inc.		-
201103470410G	Woburn	Daniel L Joyce Middle School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Reliable Roofing and Sheet Metal, LLC
200803470015	Woburn	Goodyear School	Closeout	New Construction	CM@R	Municipal Building Consultants, Inc.	Tappe Associates, Inc.	Strategic Building Solutions, LLC	Gilbane Building Company
201103470405G	Woburn	John F Kennedy Middle School	Final Audit Approved	Repair - Accelerated	DBB	Municipal Building Consultants, Inc.	Gale Associates, Inc.	Simpson Gumpertz & Heger Inc.	Greenwood Industries, Inc.
201203470060	Woburn	Wyman Elementary School	Eligibility Period			Tishman Construction			
201203480052	Worcester	Chandler Magnet School	Deisgn Development	Repair - Accelerated		Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc. RDK Engineers	
201203488099	Worcester	Dr. James Caradonio Center	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc. RDK Engineers	
201203480140	Worcester	Jacob Hiatt Magnet School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	RDK Engineers	
201203480145	Worcester	Lake View School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480175	Worcester	May Street School	Design Development	Repair - Accelerated		Tishman Construction Corporation of MA	Turowski2 Architecture, Inc.	Russo Barr Associates, Inc.	
201203480200	Worcester	Nelson Place	Eligibility Period			-	-		-
W20004048	Worcester	North High School	Project Completion	New Construction	CM@R	-	Maguire Group, Inc.	Architectural Services	Gilbane Building Company

Last Updated: 3/13/13
