

Massachusetts School Building Authority

CAPITAL PLANNING PROJECT OVERVIEW REPORT

November 17, 2023

TABLE OF CONTENTS

Capital Pipeline Overview	2-4
Statements of Interest (SOIs)	5
Core Program	6-21
Eligibility Period	6-7
Consultant Selection	8-9
Feasibility Study	10
Schematic Design	11
Commissioning	12-13
Design Development	13-14
Summary of Bid Data	15-16
Construction	17-21
Closeout	22
Post Occupancy Evaluation	23
Accelerated Repair Program	24-30
Project Variances	31-33

Appendices

(A) Project Status List

(B) 2023-26 Estimated Bid Dates


(C) School Construction Costs compared to Common Economic Indicators

(D) Construction Status Report

CAPITAL PIPELINE OVERVIEW

Status of Current Projects

A total of 289 projects that have received invitations from the Board of Directors (“Board”) to collaborate with the Massachusetts School Building Authority (“MSBA”) are currently in the MSBA’s Eligibility Period and Capital Pipeline. The summary chart provides the number of projects in Eligibility Period and each phase of the Capital Pipeline. Compared to the prior Project Overview Report, the project total has remained the same. For a detailed look at the Capital Pipeline projects, please go to www.massschoolbuildings.org/building and select “Capital Pipeline Status Chart”.

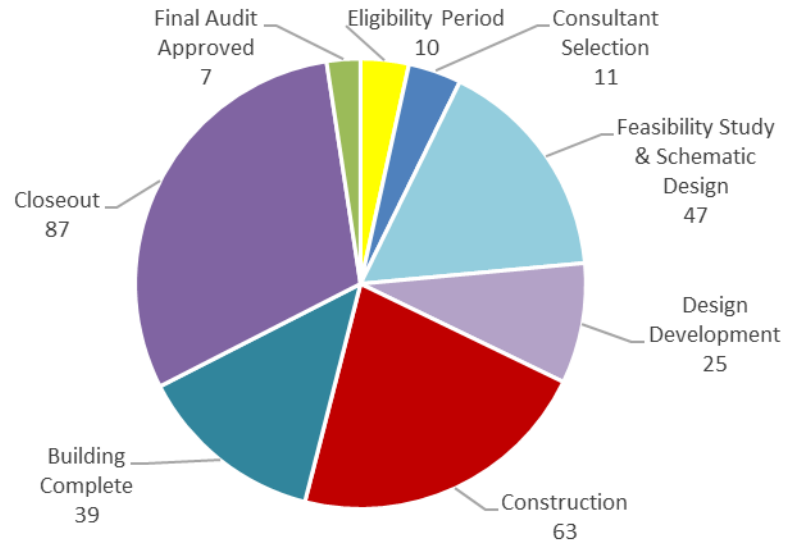

Capital Planning Updates:

The following activities are scheduled for FY 2024:

- Request for Qualifications for the Model School Program was issued on January 25, 2023, with seven designer responses received by the MSBA on May 3, 2023. Staff conducted site visits in August 2023 and provided an update to the Facilities Assessment Committee in September 2023. At the October 25, 2023 Board of Directors meeting, staff recommended and the Board approved six project designs be included in the Model School Program.
- In collaboration with the Supplier Diversity Office, staff held a procurement event, “FY24 Procurement Overview for Engineers, Architects and Project Managers”, on October 11, 2023. The event publicized upcoming opportunities for interested engineers, architects, and project managers to work with the MSBA and its districts. More details about each procurement will be provided in future reports.
 - Technical Services
 - Issuance of RFR: November 9, 2023
 - RFR Response Deadline: December 14, 2023
 - Award of the Contract: April 2024
 - Enrollment Studies
 - School Survey
 - Commissioning Services
 - Accelerated Repair Program Procurements
 - Owner’s Project Managers
 - Designers
 - Heat Pump Pilot Study
- MSBA Roundtables – Upcoming information for FY 2024 is listed below:
 - Commissioning Roundtable held on September 28, 2023 – Topic: Recommissioning

- General Roundtable held on October 19, 2023 – Topic: Decision–making for the next decade: What the new incentive and regulatory environments mean for smart school facilities investments.
- Superintendent Roundtable will be two public information sessions scheduled for November 14, 2023, and January 18, 2024 – Topic: 2024 Statement of Interest Opening
 - Staff conducted a Statement of Interest (“SOI”) public information session on November 14, 2023, to answer questions about the anticipated Accelerated Repair Program re-opening. An additional public information session will be held on January 18, 2024 for staff to provide information pertaining to the 2024 SOI opening and the submittal process.
- Designer Roundtable anticipated for Spring 2024 – Topic: Pending
- Owner’s Project Manager Roundtable anticipated for Spring 2024– Topic: Pending

2023 Progress Report

- * Statements of Interest (“SOIs”) 2023
 - 2023 SOI submittal period opened on Friday, January 13, 2023. It was for the Core Program only. The deadline to file for consideration was Friday, April 14, 2023.
 - MSBA received 63 Core Program SOIs for consideration.
 - Presentation provided on August 2, 2023, to the Facilities Assessment Subcommittee.
 - Senior Study visits commenced in August 2023 and will conclude in October 2023.
 - Presentation provided on November 15, 2023 to the Facilities Assessment Subcommittee.
 - Recommendations for invitation into the Eligibility Period are anticipated at the December 13, 2023 Board of Directors meeting.
- * Eligibility Period – Core Program
 - Ten of the ten 2022 SOIs are currently in the Eligibility Period following their invitations at the December 21, 2022, Board of Directors meeting. One SOI is anticipating an invitation at the December 13, 2023 Board of Directors meeting.
- * Consultant Selection – Core Program
 - Three districts completed Owner’s Project Manager (“OPM”) selection since the last report and three districts are tentatively scheduled to receive MSBA approval for selection of their OPM.
 - Two districts completed Designer selection since the last report while seven districts are in the process of procuring a Designer.
- * Feasibility Study/Schematic Design – Core Program
 - Eight districts are anticipating submittals for their Preferred Schematic Solutions between December 2023 and April 2024.
 - Eight districts are anticipating submittals for their Project Scope and Budget Agreement authorizations between December 2023 and April 2024.
- * Accelerated Repair Program
 - 16 districts received 2022 ARP invitations. 12 received consultant assignments and are proceeding toward Schematic Design submittals. The remaining four districts were removed from the Capital Pipeline.
- * Construction Costs – Core Program
 - In 2023, 18 projects are scheduled to receive sub-bids. MSBA staff anticipates DBB bids or GMP executions for 16 of the 18 projects in 2023.
- * Substantial Completion – Core Program
 - 15 projects were scheduled to reach substantial completion in 2022. The MSBA has received executed certificates for 14 of the 15 projects and anticipates receipt from an additional one project that has declared substantial completion with the certificate routing for signature.

- Eight projects are scheduled to reach substantial completion in 2023. The MSBA has received executed certificates for six of the eight projects.
- * Post Occupancy Evaluations
 - Staff has completed two post occupancy evaluations in FY 2024, with six more anticipated in the remainder of the fiscal year. Individual reports will be prepared for each school evaluated and will be shared with the corresponding districts and consultants

STATEMENTS OF INTEREST (SOIs)

2023 SOI Process

The 2023 SOI submittal period opened on January 13, 2023. The deadline to file SOIs for consideration into the Core Program, which is primarily for projects beyond the scope of the Accelerated Repair Program (“ARP”), including extensive repairs, renovations, additions/renovations, and new school construction was April 14, 2023. Recommendations for invitation into the Eligibility Period are anticipated at the December 13, 2023 Board of Directors meeting.

Please note there was no filing period for the ARP in 2023. Please refer to the October 26, 2022 Board of Directors Memorandum, which outlines the recommendation to temporarily pause the ARP and not accept new SOIs in 2023.

The table below lists the number of SOIs received and Invitations granted for the calendar years 2008 through 2023.

Year	Total Number of SOIs Submitted	Number of Core Program SOIs Submitted	Number of Core Program Invitations	Number of Green Repair or Accelerated Repair Program SOIs Submitted	Number of Green Repair or Accelerated Program Repair Invitations	Number of SCILAB SOIs Submitted	Number of SCILAB Program Invitations
2008	431	425	104	6	6		
2009	237	206	41	31	31		
2010	224	202	19	22	22		
2011	371	184	18	187	149		
2012	280	198	11	69	36	13	11
2013	201	123	17	78	47		
2014	229	110	18	119	51		
2015	158	97	26	61	44		
2016	156	89	17	67	49		
2017	156	83	15	73	36		
2018	130	70	12	60	34		
2019	144	61	11	83	42		
2020	161	71	15	90	25		
2021	118	58	17	60	28		
2022	121	54	10	67	33		
2023	63	63	TBD	N/A	N/A		

2008: MSBA launched the annual filing period.

2011: MSBA opened the annual filing period twice, which included a dedicated opening for interest in the Green Repair Program and the annual opening.

2012: MSBA’s annual filing period captures interest in the newly created Accelerated Repair Program, the 2012 Science Laboratory Initiative and the Core Program.


2023: MSBA’s annual filing period opened for Core Program only. Please refer to the October 26, 2022 Board of Directors Memorandum, which outlines the recommendation to temporarily pause the Accelerated Repair Program and not accept new SOIs in 2023.

CORE PROGRAM

Status of Core Program Projects

Currently, there are 142 Core Program projects in the MSBA’s Eligibility Period and Capital Pipeline. Compared to the prior Project Overview Report, the project total has remained the same.

- 48 projects are in the early phase of the grant program and have not yet secured funding authorizations for the full project.
- 37 projects have secured full project funding and are in Design Development or Construction.
- 57 projects are in Building Complete, Closeout, or Final Audit Approved phases.

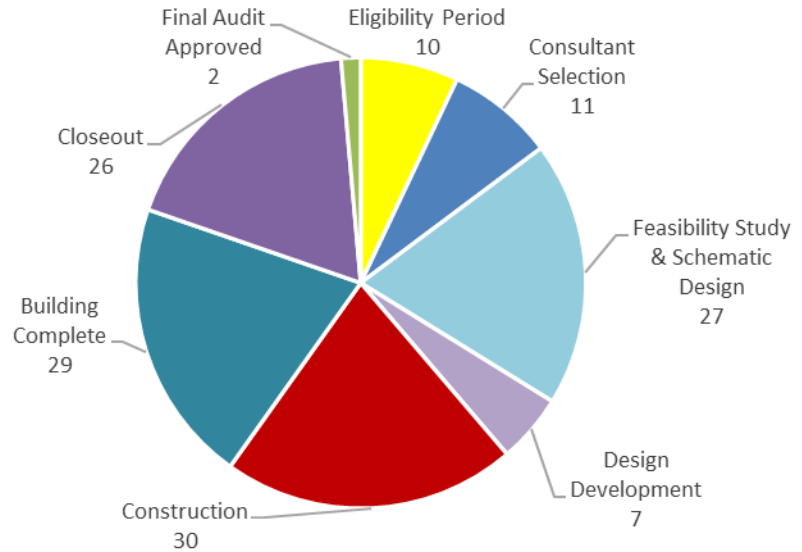

ELIGIBILITY PERIOD

There are 10 districts in Eligibility Period (table below) with all 10 granted 2022 invitations. Six of those districts have secured their local funding.

An agreed-upon enrollment is a key pre-requisite for the MSBA to commence a Feasibility Study with a district. To begin the enrollment projection process, a district must file enrollment information utilizing the MSBA’s online enrollment projection tool.

SOI Year	District	School	Eligibility Period Commencement Date	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
				ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
2022	Blackstone-Millville RSD	Blackstone-Millville RHS	6/1/23	X	X	X	X	X		X	TBD
2022	Brockton	Brockton HS	3/1/23	X	X	X	X	X			April 2024
2022	Chicopee	Barry ES	4/3/23	X	X	X	X	X		X	February 2024
2022	East Bridgewater	Central School	4/3/23	X	X	X	X	X		X	February 2024

SOI Year	District	School	Eligibility Period Commencement Date	30 days	60 days	90 days		180 days		270 days	Date of Invitation to Feasibility Study (Estimated)
				ICC	SBC	Online Enrollment Projection Info	Ed Profile Questionnaire	Maintenance Documents	Enrollment Certification	Local Authorization	
2022	Franklin County RVTSD	Franklin County THS	5/1/23	X	X	X	X	X			February 2024
2022	Marlborough	Richer ES	6/1/23	X	X	X	X	X			TBD
2022	Salem	Salem HS	5/1/23	X	X	X	X	X			TBD
2022	Swansea	Joseph Case JHS	5/1/23	X	X	X	X	X		X	February 2024
2022	West Bridgewater	Rose L. MacDonald ES	3/1/23	X	X	X	X	X	X	X	December 2023
2022	Wrentham	Charles E. Roderick School	6/1/23	X	X	X	X	X		X	TBD

CONSULTANT SELECTION

Owner’s Project Manager Selection

After the district has completed all Eligibility Period requirements and has received a Board Invitation to Feasibility Study, the district procures an OPM. Since the last report, three districts have completed Owner’s Project Manager (“OPM”) selection (shaded in the table below). Currently, there are four districts in the Capital Pipeline in the process of procuring an OPM.

District	School	Anticipated Selection
Longmeadow	Glenbrook Middle School	October 2023
Littleton	Shaker Lane Elementary School	November 2023
North Andover	Kittredge Elementary School	November 2023
Martha’s Vineyard RSD	Martha’s Vineyard High School	December 2023
Old Colony RVTSD	Old Colony RVTHS	February 2024
Dracut	Joseph E. Campbell Elementary School	March 2024

Designer Selection

After a district has selected and executed a contract with an OPM, the district selects a Designer by utilizing either a local designer selection process for projects under \$5 million or the MSBA’s Designer Selection Panel (“DSP”) for projects over \$5 million. Since the last report, two districts completed their Designer selection (shaded in the table below). There are currently seven districts in the Capital Pipeline that are in the process of procuring a Designer.

District	School	Anticipated Selection
Lexington	Lexington High School	October 2023
Leominster	Fall Brook Elementary School	October 2023
Reading	J. Warren Killam Elementary School	November 2023
Millis	Millis Middle/High School	December 2023
Southborough	Margaret A. Neary Elementary School	December 2023
North Attleborough	North Attleborough High School	January 2024
Berkshire Hills RSD	Monument Mountain RHS	January 2024
Longmeadow	Glenbrook Middle School	February 2024
North Andover	Kittredge Elementary School	February 2024

For additional information on the selected consultant teams, see Appendix A.

FEASIBILITY STUDY

Once a district has procured an OPM and a Designer, the district and the district’s consultants must complete two Feasibility Study submittals, the Preliminary Design Program, and the Preferred Schematic Report, prior to Board consideration to proceed into Schematic Design. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will appear before the Board for their Preferred Schematic Design authorizations at the December 2023, February 2024, and April 2024 Board meetings. An additional four districts are in Feasibility Study.

District	School	Anticipated PS Board Date
Agawam	Agawam High School	December 2023
Belchertown	Jabish Brook Middle School	December 2023
North Adams	Greylock Elementary School	December 2023
Burlington	Fox Hill Elementary School	February 2024
Quincy	Squantum Elementary School	February 2024
Revere	Revere High School	February 2024
Canton	Wm H Galvin Middle School	April 2024
South Shore RVTSD	South Shore RVTHS	April 2024

SCHEMATIC DESIGN

Prior to consideration by the Board for Project Scope and Budget Agreement authorization, a district must submit a Schematic Design to the MSBA for review. Based on the most recent data and schedules provided to the MSBA by districts, the MSBA anticipates that eight districts will appear before the Board for Project Scope and Budget Agreement authorizations at the December 2023, February 2024, and April 2024 Board meetings. An additional one district is in Schematic Design.

District	School	Anticipated PS&B Board Date
Lynn	Pickering Middle School	December 2023
New Bedford	John B. DeValles Elementary School	December 2023
Newton	Countryside Elementary School	December 2023
Whittier RVTSD	Whittier RVTHS	December 2023
Dedham	Oakdale Elementary School	February 2024
Clinton	Clinton Middle School	April 2024
Scituate	Hatherly Elementary School	April 2024
Stoughton	South Elementary School	April 2024

COMMISSIONING

The MSBA assigns a Commissioning Consultant after a district has secured local funding for the Board approved project. Since the last report, the MSBA has assigned Commissioning Consultants for five additional projects which are presented in the table below.

District	School	Program	Estimated Const. Cost (million)	Commissioning Consultant	Contract Amount
Boston	2 Schools	ARP	\$2.77	Bard, Rao + Athanas	\$55,000
Boston	2 Schools	ARP	\$11.91	3IVE	\$39,600
Haverhill	Silver Hill	ARP	\$1.09	Fitzmeyer & Tocci Associates	\$24,000
Nashoba Regional	High School	Core	\$199.14	NV5 (RDK)	\$173,909
Quincy	Parker ES	ARP	\$1.09	WSP USA	\$39,500

To date, the MSBA has executed 622 commissioning consultant contracts, totaling \$48.6 million in commissioning fees, for 835 projects at 692 schools, many of whom have been invited to the Capital Pipeline multiple times. Construction budgets for projects being commissioned total \$16.35 billion. To date, 463 work orders have been completed.

The table below represents the status of commissioning assignments sorted by the fiscal year in which the commissioning work orders were issued.

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced*	Percent Complete
FY2010	31	\$4,231,376	\$4,273,277	100%
FY2011	95	\$6,132,890	\$6,058,460	99%
FY2012	52	\$4,373,944	\$4,386,520	100%
FY2013	55	\$3,364,697	\$3,408,897	100%
FY2014	47	\$2,604,062	\$2,541,165	98%
FY2015	44	\$2,277,711	\$2,273,711	100%
FY2016	44	\$3,385,137	\$3,331,748	98%
FY2017	37	\$2,290,661	\$2,248,851	98%
FY2018	44	\$4,138,550	\$4,113,049	99%
FY2019	39	\$3,604,720	\$3,187,340	88%
FY2020	42	\$3,080,166	\$2,657,127	86%
FY2021	12	\$1,524,360	\$814,059	53%

Fiscal Year	No. Work Orders Issued	Value of Work Orders Issued	Total Invoiced*	Percent Complete
FY2022	36	\$3,969,566	\$1,213,877	31%
FY2023	29	\$2,525,001	\$493,577	20%
FY2024	15	\$1,084,167	\$6,946	1%
Total	622	\$48,587,008	\$41,008,604	

*Includes approved additional services over value of Work Order

DESIGN DEVELOPMENT

After a district has secured local funding and has entered into a Project Funding Agreement (“PFA”) with the MSBA, the district enters the Design Development Phase. Currently, there are 25 projects in the Design Development Phase with a total estimated construction cost of approximately \$872 million. Of those 25 projects, 18 are ARP Projects and seven are Core Program Projects. The seven Core Program Projects in Design Development have a total estimated construction cost of approximately \$811 million and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Amherst (K-5) Winchester (PK-5)	Holyoke (6-8) Webster (6-12)	Wakefield (9-12)	Brookline (PK-8) Haverhill (5-8)

District Design Submittals

During the Design Development phase, districts will submit three design submittals (Design Development, 60% Construction Documents, and 90% Construction Documents) for the MSBA to review. MSBA staff reviews the documents to ensure the project is still in compliance with the PFA. The chart below indicates the number of submittals received and reviewed by the MSBA in each fiscal year.

Fiscal Year	DD Reviews	60% Reviews	90% Reviews	Total Reviews
FY2010	5	0	0	5
FY2011	21	24	20	65
FY2012	12	24	28	64
FY2013	20	20	19	59
FY2014	15	13	14	42
FY2015	6	12	13	31
FY2016	10	10	8	28
FY2017	11	10	12	33
FY2018	10	11	9	30
FY2019	17	16	10	43
FY2020	12	16	18	46
FY2021	6	11	19	36
FY2022	15	9	10	34
FY2023	14	22	17	53
Totals	174	198	197	569


SUMMARY OF BID DATA

Based on the most recent data and schedules provided by districts, 18 projects are scheduled to receive sub-bids in 2023, eight projects are scheduled to receive sub-bids in 2024, and four projects are scheduled to receive sub-bids in 2025. Three projects have been added to the table since the last report.

Year	Number of Projects	Design Basis for Enrollment	Project Budget	Construction Budget	Construction Range
2023	18	12,404	\$2.19 billion	\$1.70 billion	\$430 - \$805
2024	8	6,520	\$1.40 billion	\$1.14 billion	\$484 - \$863
2025	4	3,795	\$0.82 billion	\$0.66 billion	\$714 - \$953
Grand Total	30	22,719	\$4.41 billion	\$3.50 billion	


Note: These numbers are based on preliminary information received from the District and are subject to further review and calculation. Data is shown only for projects which have Project Scope and Budget Agreement approval by the Board. For additional information on the bid schedules of these projects, please see Appendix B.

The graph below plots Schematic Design Construction Estimates and Construction Bid Results for new construction projects from November 2020 to present. The projects are presented based on their dates of DBB bids or GMP executions. The graph includes 13 new construction projects in FY 2021, seven new construction projects in FY 2022, 15 new construction projects in FY 2023, and one new construction project in FY 2024. The Orange Line is a trend line for Bid Costs and the Blue Line is a trend line for Schematic Design Construction Estimates. No projects have been added since the last report prepared for the October 25, 2023 Board of Directors meeting.

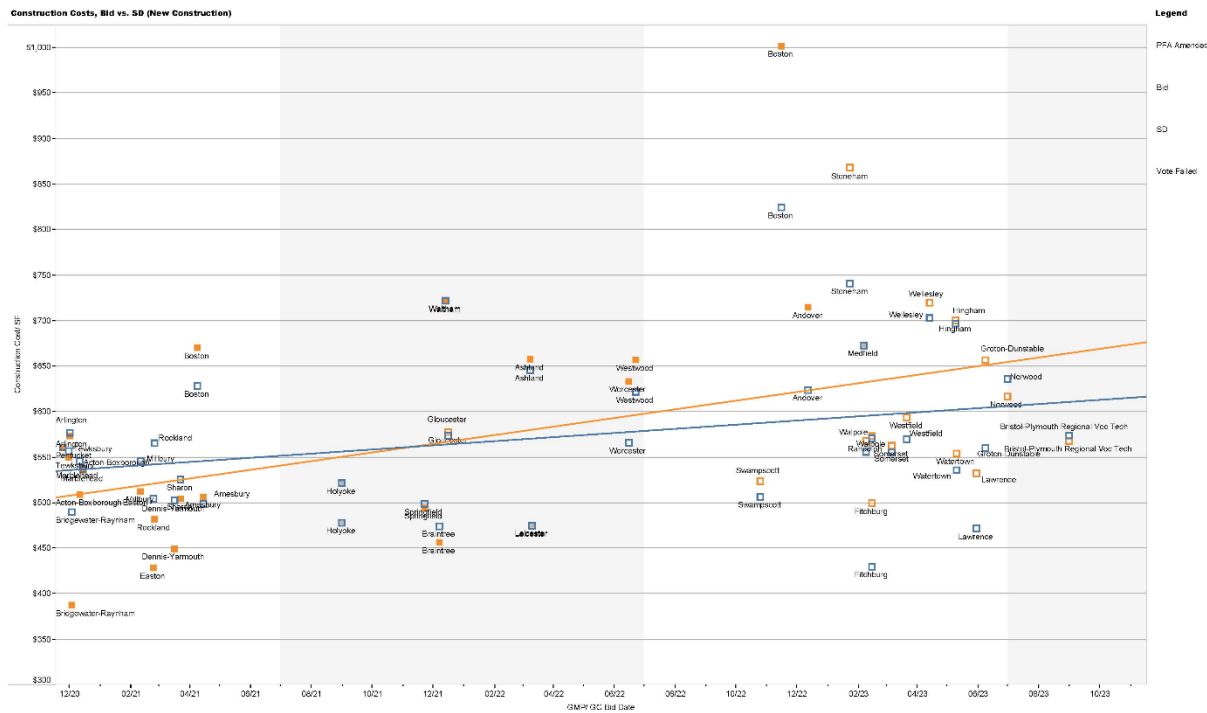

A fully interactive version of the New Construction graph is available on the MSBA website, here: <http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>.

The graph below plots Schematic Design Construction Estimates and Construction Bid Results for addition/renovation projects from November 2020 to present. The projects are presented based on their dates of DBB bids or GMP executions. The graph includes zero addition/renovation projects in FY 2021, one addition/renovation project in FY 2022, four addition/renovation projects in FY 2023, and zero addition/renovation projects in FY 2024. The Purple Line is a trend line for Bid Costs and the Yellow Line is a trend line for Schematic Design Estimates. *No projects have been added since the last Project Overview Report for the October 25, 2023 Board of Directors meeting.*

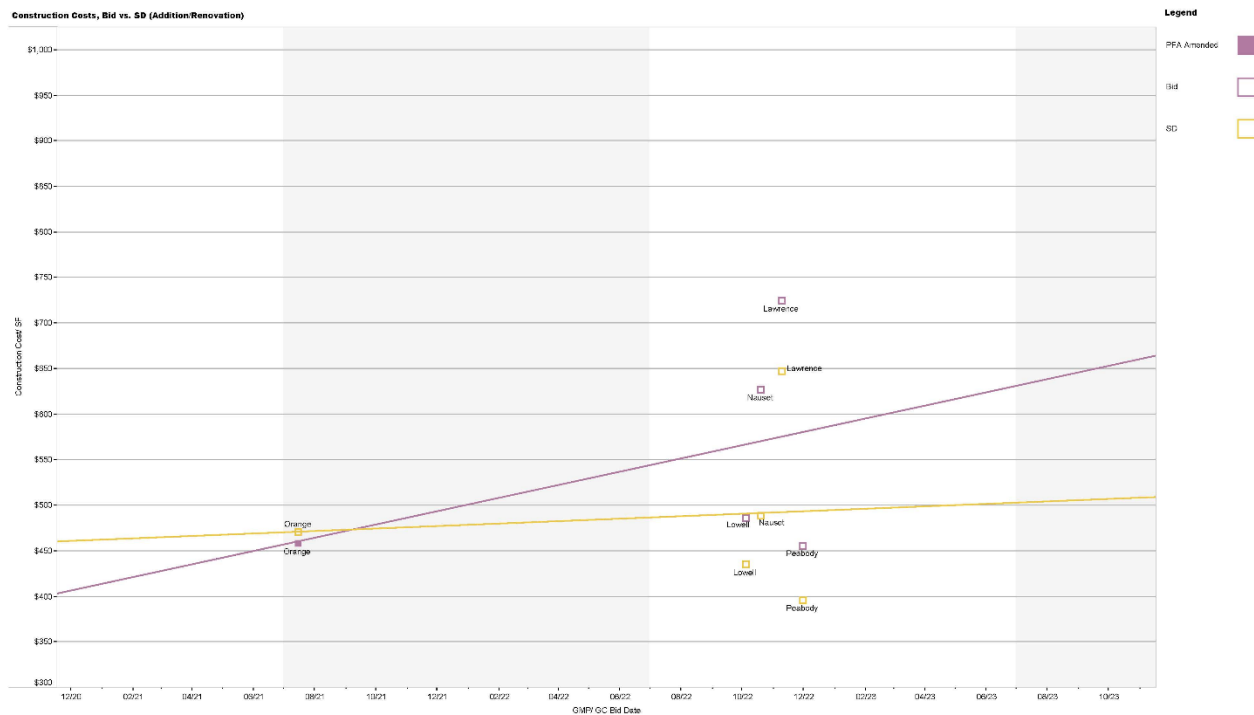

A fully interactive version of the Addition/Renovation graph is available on the MSBA website, here: <http://info.massschoolbuildings.org/TabPub/TableauCostData.aspx>.

CONSTRUCTION

When a district with a Design-Bid-Build Construction project issues a Notice to Proceed, or when a Construction Manager At-Risk project has received bids for the concrete foundation package, the project is advanced to the Construction Phase. Currently, there are 63 projects in the Construction Phase with a total estimated construction cost of \$3.99 billion. Of those 63 projects, 33 are ARP Projects and 30 are Core Program Projects; however, this does not include the 39 projects that have reached substantial completion and are currently in the Building Complete Phase. The 30 Core Program Projects have a total estimated construction cost of \$3.91 billion and are listed below.

Elementary School Districts	Middle and Middle/High School Districts	High School Districts	Other Grade Configurations
Andover (PK-5) Fitchburg (1-5) Groton-Dunstable (K-4) Hingham (PK-5) Orange (PK-6) Peabody (PK-5) Randolph (K-5) Swampscott (K-4) Wellesley (K-5) Westfield (K-4) Westwood (K-5)	Boston Quincy Upper (6-12) Somerset (6-8) Tyngsborough (6-8) Walpole (6-8)	Arlington (9-12) Bristol-Plymouth (9-12) Greater Fall River VT (9-12) Lowell (9-12) Nauset RSD (9-12) Northeast Metro (9-12) Spencer-East Brookfield (9-12) Stoneham (9-12) Waltham (9-12) Watertown (9-12) Worcester Doherty (9-12)	Boston Carter (PK-12) Lawrence Leahy (K-8) Lawrence Oliver (K-8) Norwood (5-8)

Amendment to the Project Funding Agreement (PFA)

Upon receipt of construction bids or the execution of a GMP, a district submits the Contractor's Schedule of Values to the MSBA. MSBA staff will collaborate with the district to reconcile the construction costs from the schedule of values against the estimated construction budget. Afterwards, an amendment to the PFA is executed to reflect the bids received for those projects. The chart, shown below, is the number of amendments to PFAs listed by fiscal year.

Fiscal Year	Total Amendments
FY2012	30
FY2013	31
FY2014	31
FY2015	17
FY2016	22
FY2017	8
FY2018	15
FY2019	13
FY2020	10
FY2021	17
FY2022	20
FY2023	7
FY2024	4

Substantial Completion

15 projects were scheduled to reach Substantial Completion in 2022. They are listed in the table below. The MSBA has received executed certificates for 14 of the 15 projects, and anticipates receipt of the final certificate (Bridgewater-Raynham). Staff will continue to monitor the project for updates.

Project	Enrollment	Contractor	OPM	Designer	Substantial Completion Date*	Building Construction Completion Date**	Variance (days)
Easthampton Maple	1010	Fontaine Brothers	Colliers	Caolo & Bieniek	1-Mar-22	15-Apr-22	45 behind
Boston Boston Arts Academy	500	Lee Kennedy Co.	PMA	Perkins Eastman	4-Apr-22	29-Aug-22	147 behind
Millbury Raymond E. Shaw Elementary	550	Fontaine Brothers	Hill International	Turowski2	29-Jun-22	29-Jul-22	30 behind
Sharon Sharon High	1250	Consigli	PMA	Tappe	25-Aug-22	25-Aug-22	-
Weymouth Maria Weston Chapman Middle	1470	Bond Brothers	Hill International	HMFH	1-Jul-22	22-Aug-22	52 behind
Acton-Boxborough C.T. Douglas Elementary	990	Consigli	Skanska	Arrowstreet	1-Jul-22	26-Aug-22	56 behind
Bridgewater-Raynham Mitchell Elementary School	740	Bacon	CHA	Raymond Design	8-Jul-22		
Gardner Waterford Street ES	925	Bacon	Colliers	Jones Whitsett Architects	12-Sep-22	12-Sep-22	-
West Springfield Philip G Coburn	585	Fontaine Brothers	NV5	TSKP Studio	22-Jul-22	30-Aug-22	39 behind

Project	Enrollment	Contractor	OPM	Designer	Substantial Completion Date*	Building Construction Completion Date**	Variance (days)
Pentucket Regional Senior High School	965	Rich-KBE Pentucket School Joint Venture	Vertex	Dore & Whittier	31-Jul-22	31-Jul-22	-
Attleboro High School	1725	Consigli	Skanska	Kaestle Boos	15-Aug-22	15-Aug-22	-
Dennis-Yarmouth Mattacheese School	760	Commodore Builders	PMA	Perkins Eastman	14-Oct-22	16-Feb-23	125 behind
Easton Center School	760	Brait Builders	PMA	Perkins Eastman	14-Oct-22	20-Dec-22	67 behind
Rockland Jefferson Elementary	760	Brait Builders	PMA	Symmes Maini & McKee	22-Dec-22	22-Dec-22	-
Tewksbury Louise Davy Trahan	790	Consigli	CBRE/HEERY	Flansburgh	28-Oct-22	28-Oct-22	-

*As defined in the executed Construction Contract, once provided to the MSBA

**Date on the Certificate of Substantial Completion, once provided to the MSBA

Eight projects are scheduled to reach Substantial Completion in 2023. They are listed in the table below. Staff will continue to monitor these projects for updates.

Project	Enrollment	Contractor	OPM	Designer	Substantial Completion Date*	Building Construction Completion Date**	Variance (days)
Amesbury Elementary	425	CTA	NV5	DiNisco Design	17-Feb-23	2-August -23	166 behind
Springfield William N. Deberry	800	Fontaine Brothers	Skanska USA Building	DiNisco Design	30-Jun-23	11-Aug-23	42 behind
Ashland David Mindess	635	Shawmut Design and Construction	Vertex (Compass)	Flansburgh	17-Jul-23	7-Aug-23	21 behind
Belmont High School	2215	Skanska USA Building	CHA Consulting	Perkins+Will	18-Aug-23	28-Aug-23	10 behind
Braintree South Middle School	800	Bacon	Hill International	Miller Dyer Spears	21-Aug-23	1-Sept-23	11 behind
Orange Dexter Park	520	J & J Contractors	Hill International	Raymond Design	25-Aug-23		
Gloucester East Elementary	440	WT Rich	CBRE/HEERY	Dore & Whittier	28-Aug-23	28-Aug-23	-
Peabody William A. Welch Sr	390	Consigli	Dore & Whittier	DiNisco Design	24-Nov-23		

CLOSEOUT

After the district's contractor finishes all project work including demolishing the old building, completing site work, and finalizing commissioning, the project proceeds to the Closeout Phase. Once all the project costs have been paid by the District, the District submits its Final Request for Payment Reimbursement via the MSBA's Pro-Pay system. After the District submits all the items identified on the MSBA's Index of Final Closeout, including the Final Request for Payment Reimbursement, the MSBA initiates the Draft Audit Report and sends it to the District for its consideration. The MSBA performs the final audit to determine final total grant amounts. Final payment to the District requires the MSBA Board's approval of the final Total Facilities Grant for the project.

Currently, there are 87 projects in the Closeout Phase including 61 ARP Projects and 26 Core Program Projects. The chart, shown below, lists the Core Program Projects by year of achieved Substantial Completion:

Year	All Project Phases	Final Audit Approved	Closeout	Building Complete
2012	22	22	0	0
2013	24	24	0	0
2014	19	19	0	0
2015	27	25	2	0
2016	12	12	0	0
2017	8	6	2	0
2018	11	10	1	0
2019	13	9	4	0
2020	7	0	6	1
2021	18	1	10	7
2022	14	0	1	13
2023	7	0	0	7
Total	182	128	26	28

POST OCCUPANCY EVALUATION

Approximately three years after an MSBA-funded school building reaches substantial completion, the MSBA will coordinate with districts to distribute post occupancy surveys and pre-visit questionnaires and to schedule building visits with district representatives to complete a Post Occupancy Evaluation (“POE”). The MSBA’s POE process was developed in part to assist the MSBA in understanding that MSBA-funded school building projects are operating as intended and performing as designed. In addition, the collection of technical data accompanied by school district and occupant feedback enables the MSBA, school districts, and the consultant community to apply lessons learned to future school building projects as well as to the ongoing maintenance and operations of MSBA-funded school buildings.

A partial list of the districts invited to participate in POEs in FY 2024 is shown below. Outreach to districts is ongoing, and FY 2024 visits are underway. To date, 19 reports from FY 2022 and FY 2023 have been issued to participating districts.

Project	Enrollment	Contractor	OPM	Designer	Building Construction Completion Date*	POE Visit Date
Northborough Lincoln Street ES	270	Brait Builders	Colliers	Lamoureux Pagano	31-Aug-18	5-Oct-23
Wachusett Mountview MS	800	CTA Construction	Gary Kaczmarek	Lamoureux Pagano	8-Apr-16	17-Nov-23
Marlborough Goodnow Brothers ES	610	Fontaine Brothers	CHA Consulting	Mount Vernon Group	8-April-20	12-Dec-23
Needham Sunita L. Williams ES	430	Bacon Construction	Steven Popper	Dore & Whittier	5-Jul-19	9-Jan-23
Quincy South West MS	430	Bond Brothers	PCA 360	Ai3	20-May-19	23-Jan-23
Braintree East MS	1,180	Shawmut Design and Construction	Hill International	Miller Dyer Spears	14-Oct-20	TBD
Lexington Maria Hastings MS	645	Walsh Brothers	Dore & Whittier	DiNisco	13-Feb-20	TBD
Lunenburg HS	820	Shawmut Design and Construction	NV5	Tappe	17-May-16	TBD
Saugus HS	1,360	Suffolk	PMA	HMFH	1-July-20	TBD
Taunton Mulcahey ES	735	Agostini	CGA	Dore & Whittier	21-Aug-20	TBD

*Date on the Certificate of Substantial Completion, once provided to the MSBA

ACCELERATED REPAIR PROGRAM



The photos above depict the partial boiler replacement at New Bedford’s Trinity Day Academy, serving 83 students. The project replaced the boilers, thus extending the useful life of the 92-year-old building. The project reached Substantial Completion in October 2019 and is scheduled to receive Final Audit Approval at the February 28, 2024 Board of Directors meeting.


Currently, there are 147 ARP projects in the MSBA’s Eligibility Period and Capital Pipeline. The 147 projects include **five** projects approved for Final Audit in FY 2024. Prior to FY 2024, 248 projects received Final Audit approval. The combined 395 projects are located in 134 districts, many of whom have been invited to the ARP multiple times. All the new information that has been updated since the last report is ***italicized and bolded***.

Repair Program	Number of Districts	Number of Projects	Total Project Budgets	Maximum Facilities Grants	Number of Projects Final Audit Approved
2022 Accelerated*	12	27	<i>\$70,890,379</i>	<i>\$45,408,139</i>	-
2021 Accelerated	15	26	\$109,602,763	\$59,925,011	-
2020 Accelerated	15	21	\$81,731,451	\$43,329,550	1
2019 Accelerated	24	38	\$85,180,989	\$52,047,959	12
2018 Accelerated	20	30	\$83,172,480	\$47,018,557	15
2017 Accelerated	19	34	\$117,020,597	\$73,280,673	19
2016 Accelerated	28	48	\$156,598,234	\$83,007,586	39
2015 Accelerated	24	43	\$136,680,652	\$91,974,052	42
2014 Accelerated	34	47	\$108,410,084	\$65,388,035	44
2013 Accelerated	25	45	\$94,650,790	\$54,662,711	45
2012 Accelerated	24	36	\$63,009,653	\$38,267,952	36

* Financial totals reflect Project Funding Agreement approvals through the ***October 25, 2023*** Board of Directors Meeting (21 projects).

2022 Accelerated Repair Program


- Invitations – 16 districts, 33 projects
 - Scope includes 10 roofs, 7 windows/doors, and 16 boilers
- SOI Removal – four districts; six projects (four roof, two boilers)
- **Approved for Project Funding Agreement – 11 districts, representing 21 projects**
- **Total Project Budgets - \$70,890,379**
- **MSBA Total Facilities Grant - \$45,408,139**

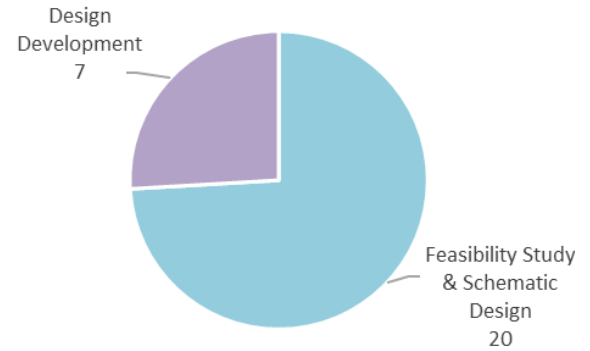

2022 ARP Status Chart

2021 Accelerated Repair Program


- Invitations – 16 districts, 28 projects
 - Scope includes 13 roofs, 11 windows/doors, and eight boilers
- SOI Removal – one district; two projects (two roofs, two windows/doors)
- Approved for Project Funding Agreement – 15 districts, representing 26 projects
- Total Project Budgets - \$109,602,763
- MSBA Total Facilities Grant - \$59,925,011
- 13 of 15 projects reported bids within estimated budget

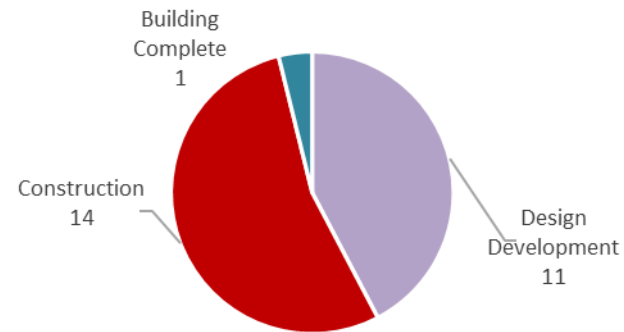

2021 ARP Status Chart

2020 Accelerated Repair Program


- Invitations – 18 districts, representing 25 projects
 - Scope includes 14 roofs, nine windows/doors, and four boilers
- SOI Removal – two districts; three projects (one roof, one windows/doors, one boiler)
- Approved for Project Funding Agreement – 16 districts, representing 22 projects
- Total Project Budgets - \$82,419,849
- MSBA Total Facilities Grant - \$43,679,026
- 71% of projects bid within estimated budget while one district removed its SOI (one roof) following receipt of bids which exceeded the estimated budget
- One project has completed Final Audit

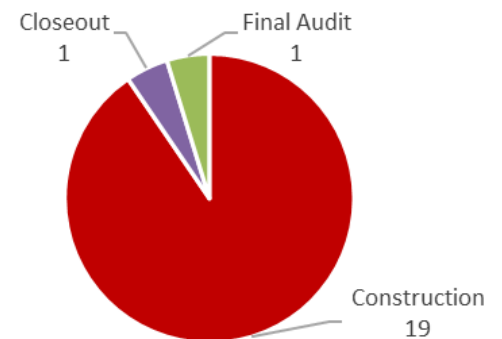

2020 ARP Status Chart

2019 Accelerated Repair Program


- Invitations – 27 districts, representing 42 projects
 - Scope includes 24 roofs and 21 boilers
- SOI Removal – three districts; four projects (one roof, three boilers)
- Approved for Project Funding Agreement – 24 districts, representing 38 projects
- Total Project Budgets - \$85,180,989
- MSBA Total Facilities Grant - \$52,047,959
- Three districts, representing three projects, required a schedule extension following PFA approval
- 97% of projects bid within estimated budget
- **12 projects, or 32%, have completed Final Audit**

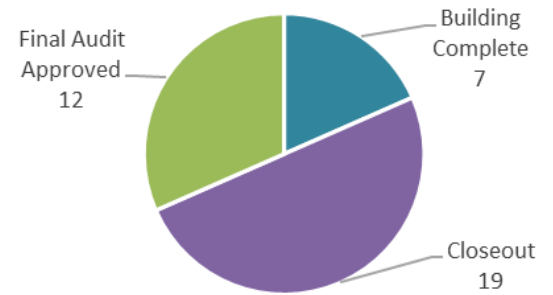

2019 ARP Status Chart

2018 Accelerated Repair Program


- Invitations – 23 districts, representing 34 projects
 - Scope includes 17 roofs, 11 windows/doors, and 14 boilers
- SOI Removal – three districts; four projects (two roofs, two windows/doors, one boiler)
- Approved for Project Funding Agreement – 20 districts, representing 30 projects
- Total Project Budgets - \$83,172,480
- MSBA Total Facilities Grant - \$47,018,557
- Two districts, representing two projects, required a schedule extension following PFA approval
- 90% of projects bid within estimated budget
- 15 projects, or 50%, have completed Final Audit

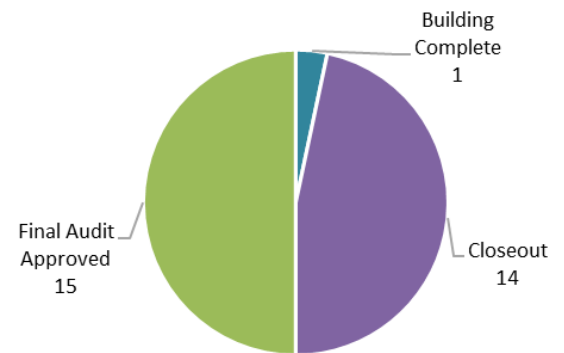

2018 ARP Status Chart

2017 Accelerated Repair Program


- Invitations – 20 districts, representing 36 projects
 - Scope includes nine roofs, 23 windows/doors, and 15 boilers
- SOI Removal - one district; two projects (one boiler; one windows/doors)
- Approved for Project Funding Agreement - 19 districts, representing 34 projects
- Total Project Budgets - \$117,020,597
- MSBA Total Facilities Grant - \$73,280,673
- Three districts, representing six projects, required a schedule extension following PFA approval
- 79% of projects bid within estimated budget
- 19 projects, or 56%, have completed Final Audit.

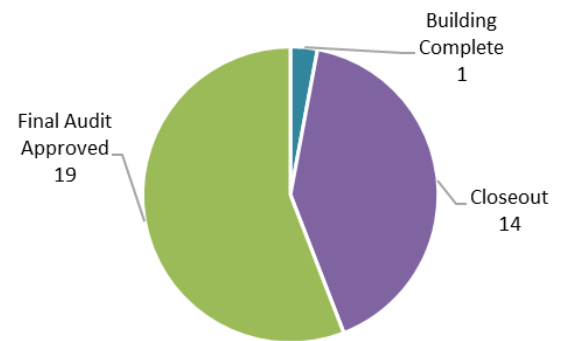

2017 ARP Status Chart

2016 Accelerated Repair Program


- Invitations – 28 districts, representing 49 projects
 - Scope includes 25 roofs, 19 windows/doors, and 13 boilers
- SOI Removal - one project (one boiler)
- Approved for Project Funding Agreements - 28 districts, representing 48 projects
- Total Project Budgets - \$156,598,234
- MSBA Total Facilities Grant - \$83,007,586
- Four districts, representing four projects, required a schedule extension following PFA approval
- 73% of projects bid within estimated budget
- 39 projects, or 81%, have completed Final Audit

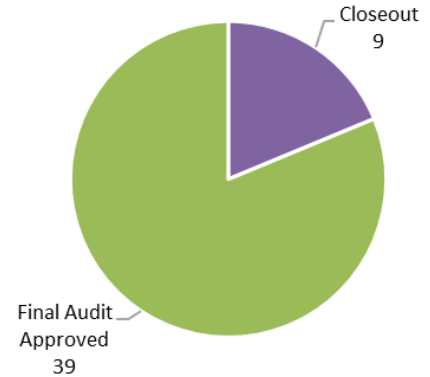

2016 ARP Status Chart

2015 Accelerated Repair Program


- Invitations – 24 districts, representing 44 projects
 - Scope includes 22 roofs, 26 windows/doors, and nine boilers
- SOI Removal – one project
- Approved for Project Funding Agreements – 24 districts, representing 43 projects
- Total Project Budgets - \$136,680,652
- MSBA Total Facilities Grants - \$91,974,052
- One district, representing one project, required two schedule extensions following PFA Approval
- 81% of projects bid within estimated budgets
- 42 projects, or 98%, have completed Final Audit

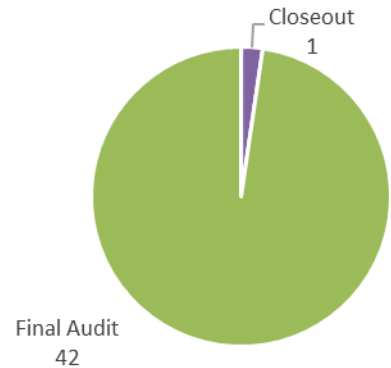

2015 ARP Status Chart

2014 Accelerated Repair Program

- Invitations – 36 districts, representing 51 projects
- SOI Removal – two districts, representing four projects
- Current 2014 ARP projects – 34 districts, representing 47 projects
 - Scope includes 20 roofs, 25 windows/doors, and 13 boilers
- Approved for Project Funding Agreements – 34 districts, representing 47 projects
- Total Project Budgets - \$108,410,084
- MSBA Total Facilities Grants - \$65,388,035
- Four districts, representing six projects, required schedule extensions following PFA approval
- 85% of projects bid within estimated budget
- 44 projects, or 94%, have completed Final Audit

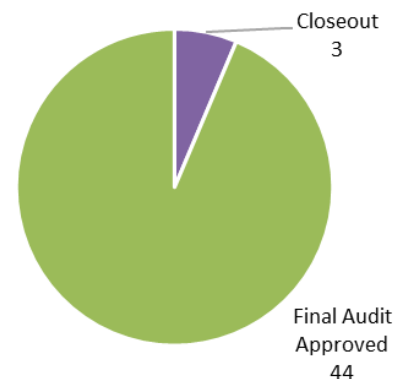

2014 ARP Status Chart

Closed Accelerated Repair Programs

Repair Program	Number of Districts	Number of Projects	Number of Roofs	Number of Windows/ Doors	Number of Boilers	Final Costs Submitted	Final Total Facilities Grants
2013 Accelerated	25	45	30	13	7	\$70,489,512	\$37,769,944
2012 Accelerated	24	36	21	11	7	\$47,748,996	\$28,518,764

Status of Green Repair Program

The Green Repair Program resulted in PFA authorizations totaling \$366,647,226 in Total Project Costs and \$222,889,218 in MSBA grants. All 189 projects from 93 districts have been approved for final grant payments.

2021 Accelerated Repair Projects – Construction Estimate vs. 2022-2023

- 13 of 15 projects reported bids within estimated budget.
- **11 additional projects are anticipated to be reported by the February 2024 Board of Directors meeting.**

District	School	Scope	Project Type	Bid Date	Construction Estimate*	Bid Amount*	Variance from Construction Estimate	Reimbursement Rate	Potential Grant Variance**
Fitchburg	Arthur M Longsjo Middle School	Windows / Doors	DBB	Dec-22	\$3,636,218	\$3,498,000	\$138,218	80.00%	\$110,574
Haverhill	Moody	Partial Roof	DBB	Dec-22	\$646,479	\$325,300	\$321,179	76.84%	\$246,794
Freetown-Lakeville	Assawompset Elementary	Windows / Doors	DBB	Dec-22	\$3,379,255	\$3,144,000	\$235,255	53.53%	\$125,932
Mansfield	Mansfield High	Boiler	DBB	Dec-22	\$1,395,158	\$984,745	\$410,413	52.89%	\$217,067
Gloucester	Ralph B O'Maley Middle	Windows / Doors	DBB	Jan-23	\$5,317,751	\$4,872,000	\$445,751	61.02%	\$271,997
Melrose	Herbert Clark Hoover	Roof	DBB	Jan-23	\$1,881,016	\$1,287,900	\$593,116	49.31%	\$292,465
Melrose	Horace Mann	Roof	DBB	Jan-23	\$1,113,143	\$707,000	\$406,143	49.31%	\$200,269
Springfield	Thomas M. Balliet	Windows / Doors	DBB	Feb-23	\$1,256,855	\$1,567,000	-\$310,145	80.00%	\$0
Wareham	Wareham Senior High	Boiler	DBB	Feb-23	\$1,862,668	\$1,193,200	\$669,468	71.58%	\$479,205
Springfield	Glickman Elementary	Windows / Doors	DBB	Feb-23	\$2,651,697	\$2,053,000	\$598,697	80.00%	\$478,958
Springfield	Springfield Central High	Boiler	DBB	Feb-23	\$1,265,531	\$1,321,746	-\$56,215	80.00%	\$0
Lynn	Capt. William G Shoemaker	Roof	DBB	Feb-23	\$2,681,000	\$1,999,900	\$681,100	79.58%	\$542,019
Braintree	Mary E Flaherty School	Roof	DBB	Feb-23	\$3,440,098	\$3,080,112	\$359,986	50.58%	\$182,081
Braintree	Hollis	Roof	DBB	Feb-23	\$3,846,336	\$1,754,500	\$2,091,836	50.58%	\$1,058,051
Everett	Webster School	Roof	DBB	Jun-23	\$1,333,772	\$1,376,977	-\$43,205	76.63%	\$0
				Total	\$35,706,977	\$29,165,380	\$6,541,597		\$4,205,412

Accelerated Repair Projects – Schedule Extension Update

The MSBA has granted districts conditional extensions to their PFAs pending compliance with the following stipulations:

- The district must submit a detailed, revised, construction timeline that explains how the work will be completed at each school; and
- Any costs that are related to a district requesting an extension to the construction schedule will be the sole responsibility of the district, and those costs are categorically ineligible for reimbursement by the MSBA.

Schedule delays for these districts can be attributed to local funding issues, lead time for materials, and construction delays on site. In no event have the extended schedules resulted in an increase to the Estimated Maximum Total Facilities Grant, as authorized by the Board.

Seven of the 22 2020 ARP Projects revised its construction schedule to reflect substantial completion in 2023 or 2024. Staff has reported previously on the shaded projects listed below, which remain in Construction.

District	School	Scope	Original Construction Completion Date	Updated Construction Completion Date	Reason for Schedule Extension
Weston	Weston High	Roof	1-Nov-22	30-Aug-23	The District and its consultants have determined that bidding for construction in 2023 would better serve the project budget following appropriation of the project funds.
New Bedford	Elwyn G Campbell	Windows / Doors, Boiler	28-Oct-22	25-Aug-23	The District has agreed to revise its construction schedule with its consultants and contractor to complete construction in 2023.
Taunton	H H Galligan	Windows / Doors, Boiler	26-Aug-22	25-Aug-23	The District has agreed to revise its construction schedule with its consultants and contractor to complete the window/door construction in 2023.
Plymouth	Federal Furnace Sch	Roof	16-Sep-22	19-Aug-23	The District has agreed to revise its construction schedule with its consultants and contractor to complete construction in 2023.
Plymouth	Indian Brook	Roof	16-Sep-22	19-Aug-23	The District has agreed to revise its construction schedule with its consultants and contractor to complete construction in 2023.
Plymouth	West Elementary	Roof	16-Sep-22	19-Aug-23	The District has agreed to revise its construction schedule with its consultants and contractor to complete construction in 2023.
Revere	Abraham Lincoln	Windows / Doors	30-Aug-23	23-Aug-24	The District has agreed to revise its construction schedule with its consultants and contractor to complete construction in 2024.

PROJECT VARIANCES

Core Program – Total Project Budget Update

Upon receiving the Board’s approval of the Project Scope and Budget, the MSBA and participating districts enter into a Project Funding Agreement, which establishes the Total Project Budget and the Estimated Maximum Total Facilities Grant for an approved project. Staff has reported on budget increases for the 34 projects below at previous Board meetings. No shading appears where project information is new or updated since the previous Board meeting. In no event has the increase in a budget resulted in an increase to the Maximum Total Facilities Grant, as authorized by the Board.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Maximum Total Facilities Grant	Total Project Budget	Maximum Total Facilities Grant	
Andover	Bancroft ES	New	\$44,659,837	\$16,773,753	\$50,299,859	\$16,575,965	The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies for litigation/settlement costs and other ineligible costs.
Andover	West ES	New	\$151,661,968	\$38,442,820	\$168,066,623	\$38,007,178	The District has appropriated additional funds to cover the costs associated with the construction bid overage.
Ashland	David Mindess ES	New	\$84,387,000	\$27,008,753	\$84,637,000	\$26,371,101	The District has transferred additional funds to cover the costs associated with increased construction costs.
Berlin-Boylston	Tahanto Regional HS	New	\$43,954,901	\$21,148,751	\$43,519,302	\$18,972,041	The District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Blue Hills	Blue Hills Regional Technical School	Add/Reno	\$84,862,768	\$44,210,180	\$88,071,616	\$43,708,007	The District has appropriated additional funds to cover the costs associated with increased construction costs.
Boston	Boston Arts Academy	New	\$124,755,412	\$48,890,620	\$137,370,916	\$48,186,575	The District appropriated additional funds to cover costs associated with increased construction costs and additional contingency for change order costs.
Bristol County Agricultural	Bristol County Agricultural HS	Add/Reno	\$103,750,000	\$53,286,797	\$103,947,718	\$53,095,156	The District received additional funding through the CARES Act for Municipal Government. The federal Coronavirus Aid, Relief, and Economic Security Act (the "CARES Act") includes funds for Massachusetts governments to use to pay costs incurred in responding to the COVID-19 pandemic.
Burlington	Marshall Simonds MS	Add/Reno	\$32,865,272	\$17,143,365	\$34,221,929	\$15,362,127	The District appropriated at its May 2012 annual town meeting through Articles 18: 19, additional funds for the costs associated with the construction of the new field complex and field lighting replacement.
Essex North Shore Agricultural & Technical School District	Essex North Shore Agricultural & Technical HS	New	\$125,000,000	\$77,500,000	\$133,770,000	\$77,500,000	The Board was informed at the March 30, 2011 meeting that the Total Project Budget had increased due to additional ineligible scope that would be funded by DCAMM.
			\$125,000,000	\$77,500,000	\$134,501,368	\$77,500,000	The District has appropriated additional funds to cover the costs associated with increased construction costs for horse tack barn renovations.
Framingham	Fuller Middle School	New	\$98,276,878	\$39,453,932	\$101,141,939	\$38,698,964	The District appropriated additional funds to cover the costs associated with the installation of new turf fields.
Greater New Bedford	Greater New Bedford Vocational and Technical High School	Add/Reno	\$17,099,808	\$13,543,920	\$16,396,429	\$12,258,642	The District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Haverhill	Caleb Dustin Hunking School	New	61,500,000	40,363,276	61,677,024	39,933,953	The District has appropriated additional funds to cover additional costs associated with Furnishings and Equipment.
Hopkinton	Center ES	New	\$45,629,373	\$14,058,455	\$47,129,373	\$14,058,455	The District has appropriated \$1,500,000 of additional funds to cover the costs associated with the construction of a building addition due to an unanticipated increase in enrollment.
Lexington	Joseph Estabrook ES	New	\$40,792,248	\$12,250,739	\$43,392,248	\$12,148,491	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
New Bedford	Irwin Jacobs (Hannigan) ES	New	\$36,747,197	\$22,726,582	\$34,925,392	\$22,372,846	The District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Newburyport	Nock/Molin MS	Add/Reno	\$26,997,326	\$13,697,934	\$28,170,749	\$12,520,326	The District has received additional funding to cover additional construction change order costs.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Maximum Total Facilities Grant	Total Project Budget	Maximum Total Facilities Grant	
North Reading	North Reading MS/HS	Add/Reno	\$107,727,074	\$49,323,123	\$123,227,074	\$49,323,123	This is a CMR project. The estimated, reconciled construction costs tracked over budget at DD (\$9,746,655 over), 60% (\$4,655,965 over), and 90% (\$15,136,846 over). A Town override vote in March 2013 obtained an additional \$15,500,000 in local funding to proceed.
Norfolk County Agricultural	Norfolk County Agricultural HS	Add/Reno	\$28,552,385	\$15,369,712	\$30,589,078	\$13,867,050	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Northborough	Lincoln Street ES	Add/Reno	\$25,530,553	\$10,407,408	\$25,530,553	\$10,407,408	The MSBA Board Approved Total Project Budget increased by \$60,400 from \$25,470,153 to \$25,530,553 due to the addition of an alternate, for a new ball field added at the District's request.
Oxford	Oxford MS	Add/Reno	\$6,128,870	\$3,483,589	\$7,340,000	\$3,359,171	The District received additional funding to cover additional construction costs including accessibility upgrades. District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Peabody	William A. Welch ES	Add/Reno	\$29,973,821	\$17,628,004	\$33,432,013	\$17,628,004	The District has appropriated additional funds to cover the costs associated with the construction bid overage.
Plymouth	South HS	New	\$107,800,000	\$46,867,514	\$111,063,271	\$46,328,160	The District appropriated \$3,263,371 of additional funding to fund change order work to incorporate scope previously identified in the construction bid documents as Alternate 4 (synthetic turf field) and a portion of Alternate 5 (electrical infrastructure to support future lights at synthetic turf field). Note that the increased Total Project Budget will not increase the Maximum Facilities Grant.
Quincy	Reay E Sterling MS	New	\$58,314,910	\$29,285,563	\$58,825,659	\$28,482,446	The District increased its Total Project Budget due to additional construction change orders for a turf field and for delay costs associated with a utility company work stoppage.
Revere	Staff Sergeant James J. Hill ES	New	\$45,402,396	\$29,551,048	\$45,402,396	\$29,551,048	At Project Scope and Budget, the Total Project Budget was approved at \$44,382,396. The City of Revere has increased the land acquisition budget. Therefore, the projected total project budget at PFA has increased to \$45,402,396. Note that the MSBA grant has not changed since the Project Scope and Budget Agreement.
Salem	Saltonstall ES	Repair	\$15,503,406	\$11,794,492	\$15,752,033	\$10,709,091	The District has executed a GMP that exceeds the Construction Budget of the PFA. The District has appropriated additional funds to cover the costs associated with increased construction costs and additional contingencies.
Somerville	East Somerville Community School	Add/Reno	\$33,185,258	\$15,237,996	\$38,006,621	\$15,237,996	At the March 28, 2012 Board Meeting, the Board approved an amendment to the PFA and a \$6.25M District loan.
Sutton	Sutton MS	Add/Reno	\$59,945,474	\$29,843,511	\$60,130,536	\$27,002,506	The District has executed a Tender Agreement and Completion Agreement Contract, increasing its Total Project Budget, following the termination of its original construction contract.
Tewksbury	Tewksbury HS	New	\$84,173,174	\$44,194,627	\$67,710,158	\$36,219,487	The District submitted final project costs that exceeded the total project budget established at bid. Final Costs did not exceed the original total project budget established at Project Funding Agreement.
Uxbridge	Uxbridge HS	New	\$43,000,000	\$22,362,328	\$44,986,479	\$22,362,328	The District has appropriated additional funds to cover the costs associated with the construction of athletic fields originally included in the PFA but which were not included in the bid as the District's construction contract would have exceeded the budget.
Weston	Field ES	New	\$31,504,146	\$8,310,510	\$32,654,146	\$8,105,549	District-approved Construction Change Orders exceeded available contingency amount.
Westwood	Paul R. Hanlon ES	New	\$87,820,386	\$18,235,725	\$89,856,899	\$18,087,808	The District has appropriated additional funds to cover the costs associated with the construction bid overage.
Winchester	Winchester HS	Add/Reno	\$129,923,146	\$44,493,270	\$131,513,741	\$43,100,458	The MSBA Board Approved Total Project Budget increased due to a construction change order for additional soil abatements at Skillings Field. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Winthrop	Winthrop MS/HS	New	\$81,818,740	\$42,582,841	\$81,432,986	\$41,249,005	The MSBA Board Approved Total Project Budget increased due to revised FEMA flood plain requirements which necessitated the elevation of the new building to be raised. Note that the increased Total Project Budget will not increase the Maximum Total Facilities Grant.
Woburn	Wyman-Hurld ES	New	\$33,705,396	\$14,387,427	\$39,647,723	\$14,387,427	The District had completed a project review with its Conservation Commission and an Order of Conditions was issued on June 12, 2015. A neighborhood group appealed this Order and was reviewed by The DEP. The District experienced delays in completing its City Council vote for its appropriation and incurred additional costs.
Worcester	Doherty HS	New	\$293,384,178	\$135,241,024	\$314,351,858	\$127,118,217	The District has appropriated additional funds to cover the costs associated with the construction bid overage.

Core Program – Additional Funding Update

Staff has received information provided by districts and their consultants reporting additional funding increases for the 14 projects below. Upon execution of an amendment to the Project Funding Agreement to incorporate the additional funding, a project will be removed from this table and reflected in the prior table. No shading appears where project information is new or updated since the previous Board meeting. In no event has the increase in a budget resulted in an increase to the Maximum Total Facilities Grant, as authorized by the Board. Since the last report, two districts (Tyngsborough and Watertown) have been added while two districts (Andover and Worcester) have been removed.

District	School	Scope	Project Funding Agreement		PFA Bid Amendment/ Final Audit		Reason for Increase to Total Project Budget
			Total Project Budget	Maximum Total Facilities Grant	Total Project Budget	Maximum Total Facilities Grant	
Boston	Josiah Quincy Upper School	New	\$193,591,467	\$54,075,966	-	-	The District has appropriated an additional \$30.30M to fund increased construction costs.
Boston	Carter School	New	\$91,966,532	\$61,290,298	-	-	The District has appropriated an additional \$19.61M to fund increased construction costs.
Fitchburg	Crocker ES	New	\$65,032,984	\$42,145,758			The District has appropriated an additional \$11.60M to fund increased construction costs.
Groton-Dunstable	Florence Roche School	New	\$78,650,734	\$26,503,001	-	-	The District has appropriated an additional \$10.50M to fund increased construction costs.
Lawrence	Oliver Partnership School	Add/ Reno	\$132,300,000	\$61,647,551	-	-	The District has appropriated an additional \$15.50M to fund increased construction costs.
Lawrence	Francis M Leahy ES	New	\$103,740,911	\$61,290,298	-	-	The District has appropriated an additional \$15.50M to fund increased construction costs.
Lowell	Lowell HS	Add/ Reno	\$343,399,220	\$215,992,406	-	-	The District has appropriated an additional \$38.50M to fund increased construction costs.
Nauset	Nauset Regional HS	Add/ Reno	\$131,825,665	\$36,676,476	-	-	The District has appropriated an additional \$38.10M to fund increased construction costs.
Randolph	Elizabeth G. Lyons ES	New	\$50,384,511	\$27,558,249	-	-	The District has appropriated an additional \$0.99M to fund increased construction costs.
Stoneham	Stoneham HS	New	\$189,593,594	\$48,968,062	-	-	The District has appropriated an additional \$24.99M to fund increased construction costs.
Swampscott	Hadley ES	New	\$98,316,523	\$32,572,001	-	-	The District has appropriated an additional \$2.91M to fund increased construction costs.
Tyngsborough	Tyngsborough MS	New	\$83,480,000	\$28,637,072	-	-	The District has appropriated an additional \$4.63M to fund increased construction costs.
Watertown	Watertown HS	New	\$201,461,673	\$45,309,315			The District has appropriated an additional \$17.27M to fund increased construction costs.
Wellesley	Ernest F. Upham ES	New	\$72,500,000	\$13,508,529	-	-	The District has appropriated an additional \$0.35M to fund increased construction costs.

APPENDIX A
PROJECT STATUS LIST

Date of Report: 11/14/2023

Total Projects: 289

SOI	MSBA ID	District	School	Project Phase	Project Type	Project Scope	Procurement Type	OPM	Designer	CM\GC	Commissioning Consultant
2016	201606000020	Acton-Boxborough	C.T. Douglas Elementary School	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Arrowstreet Inc.	Consigli Construction Company, Inc.	Colliers Project Leaders NE, LLC
2019	201900030025	Acushnet	Acushnet Elementary School	Building Complete	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Next Phase Studios, Inc.	Young Developers LLC	Gale Associates, Inc.
2020	202000050505	Agawam	Agawam High	Feasibility Study	Core Program			Leftfield, LLC	Flansburgh Associates, Inc.	-	-
2019	201900050405	Agawam	Agawam Junior High	Closeout	Accelerated Repair	Boiler	DBB	D.A. Sullivan & Sons, Inc.	Shekar & Associates, Inc.	Adams Plumbing and Heating, Inc.	BVH Integrated Services, P.C.
2015	201500070005	Amesbury	Amesbury Elementary	Building Complete	Core Program	New Construction	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	DiNisco Design, Inc.	CTA Construction Co., Inc.	BVH Integrated Services, P.C.
2019	201900080020	Amherst	Fort River Elementary	Design Development	Core Program	New Construction	DBB	Anser Advisory	DiNisco Design, Inc.	-	Van Zelm Heywood & Shadford, Inc.
2017	201700090025	Andover	West Elementary	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	Gilbane Building Company	Rist-Frost-Shumway Engineering, P.C.
2015	201500100505	Arlington	Arlington High	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.
2017	201700140015	Ashland	David Mindess	Building Complete	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Flansburgh Associates, Inc.	Shawmut Design and Construction	WSP USA
2014	201400160505	Attleboro	Attleboro High	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Consigli Construction Company, Inc.	Cadmus Group LLC
2020	202000240025	Belchertown	Jabish Middle School	Feasibility Study	Core Program			Skanska USA Building, Inc	Lamoureux Pagano Associates Architects, Inc.	-	-
2015	201500260505	Belmont	Belmont High	Building Complete	Core Program	Addition / Renovation	CM@R	CHA Consulting, Inc.	Perkins+Will	Skanska USA Building, Inc.	BVH Integrated Services, P.C.
2020	202000270010	Berkley	Berkley Community School	Schematic Design	Core Program	New Construction		PMA Consultants, LLC	Taylor & Burns, Inc.	-	-
2021	202106180505	Berkshire Hills	Monument Mt Regional High	Designer Selection	Core Program			Skanska USA Building, Inc	-	-	-
2022	202206220505	Blackstone-Millville	Blackstone Millville RHS	Eligibility Period	Core Program			-	-	-	-
2018	201806220010	Blackstone-Millville	Millville Elementary	Closeout	Accelerated Repair	Boiler	DBB	PCA 360	NV5	NB Kenney Company, Inc	Colliers Project Leaders NE, LLC
2013	201300350546	Boston	Boston Arts Academy	Building Complete	Core Program	New Construction	CM@R	PMA Consultants, LLC	Perkins Eastman/DPC	Lee Kennedy Co., Inc.	Symmes, Maini & McKee Associates
2021	202100350505	Boston	Boston Day and Evening Academy	Design Development	Accelerated Repair	Windows / Doors	DBB	Anser Advisory	Habeeb & Associates Architects, Inc.	-	Gale Associates, Inc.
2016	201600350560	Boston	Boston Latin	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	NB Kenney Company, Inc	Rist-Frost-Shumway Engineering, P.C.
2017	201700350036	Boston	Carter School	Construction	Core Program	New Construction	CM@R	Hill International Company	Perkins+Will	Bond Brothers, Inc.	NV5 (RDK) Symmes, Maini & McKee Associates
2017	201700350052	Boston	Charles Sumner	Closeout	Accelerated Repair	Boiler	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative Inc.	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2019	201900350020	Boston	Curley K-8 School	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	Raymond Design Associates, Inc.	Reliable Roofing and Sheet Metal, LLC	Building Enclosure Associates, LLC (VPC)
2022	202200350077	Boston	Dennis C Haley	Approved Project Vote Pending	Accelerated Repair	Boiler		NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	-
2018	201800350080	Boston	Donald Mckay	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzemeyer & Tocci Associates, Inc.
2022	202200350426	Boston	Dr. William Henderson Upper	Approved Project Vote Pending	Accelerated Repair	Roof		NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	-
2021	202100350426	Boston	Dr. William Henderson Upper	Design Development	Accelerated Repair	Boiler	DBB	Anser Advisory	Habeeb & Associates Architects, Inc.	-	Consulting Engineering Services, LLC
2017	201700350530	Boston	East Boston High	Closeout	Accelerated Repair	Boiler	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative Inc.	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2010	201000350074	Boston	Henry Dearborn Middle School	Closeout	Core Program	New Construction	CM@R	CHA Consulting, Inc.	Jonathan Levi Architects LLC	Gilbane Building Company	Symmes, Maini & McKee Associates
2017	201700350141	Boston	Hugh Roe O'Donnell	Closeout	Accelerated Repair	Boiler	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative Inc.	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.

2016	201600350146	Boston	James Condon Elementary	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	NB Kenney Company, Inc	Rist-Frost-Shumway Engineering, P.C.
2018	201800350156	Boston	James Otis	Closeout	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2022	202200350525	Boston	Jeremiah E Burke High	Approved Project Vote Pending	Accelerated Repair	Boiler		NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	-
2017	201700350178	Boston	John Marshall	Closeout	Accelerated Repair	Windows / Doors	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative	WCI Corp.	Simpson Gumpertz & Heger Inc.
2016	201600350179	Boston	John W McCormack	Closeout	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2018	201800350286	Boston	Josiah Quincy	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2018	201800350262	Boston	Lyndon	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2019	201900350655	Boston	Lyon Upper 9-12	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Raymond Design Associates, Inc.	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2017	201700350229	Boston	Maurice J Tobin	Closeout	Accelerated Repair	Boiler	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C.
2018	201800350575	Boston	O'Bryant School Math/Science	Closeout	Accelerated Repair	Windows / Doors	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	GVW, Inc.	Simpson Gumpertz & Heger Inc.
2016	201600350268	Boston	Paul A Dever	Closeout	Accelerated Repair	Roof	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2010	201000350565	Boston	Quincy Upper School	Construction	Core Program	New Construction	CM@R	Skanska USA Building, Inc	HMFH Architects, Inc.	Turner Construction Company	Rist-Frost-Shumway Engineering, P.C. Symmes, Maini & McKee Associates
2018	201800350691	Boston	Rafael Hernandez	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	Enterprise Equipment Co., Inc.	Fitzmeyer & Tocci Associates, Inc.
2021	202100350691	Boston	Rafael Hernandez	Design Development	Accelerated Repair	Windows / Doors	DBB	Anser Advisory	Habeeb & Associates Architects, Inc.	-	Gale Associates, Inc.
2022	202200350535	Boston	The English High	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		NV5 (fka Joslin, Lesser + Associates Inc.)	CSS Architects Incorporated	-	-
2017	201700350366	Boston	William E Russell	Closeout	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative	Reliable Roofing and Sheet Metal, LLC	Simpson Gumpertz & Heger Inc.
2021	202100350366	Boston	William E Russell	Design Development	Accelerated Repair	Boiler	DBB	Anser Advisory	Habeeb & Associates Architects, Inc.	-	Consulting Engineering Services, LLC
2016	201600350360	Boston	William Ellery Channing	Closeout	Accelerated Repair	Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	ICON architecture, inc.	NB Kenney Company, Inc	Rist-Frost-Shumway Engineering, P.C.
2019	201900350363	Boston	William McKinley	Closeout	Accelerated Repair	Roof	DBB	NETCO Construction Project Managers, Inc.	Raymond Design Associates, Inc.	Reliable Roofing and Sheet Metal, LLC	Building Enclosure Associates, LLC (VPC)
2013	201300400305	Braintree	East Middle School	Closeout	Core Program	Addition / Renovation	CM@R	Hill International Company	Miller Dyer Spears Inc.	Shawmut Design and Construction	Fitzmeyer & Tocci Associates, Inc.
2020	202000400015	Braintree	Highlands	Construction	Accelerated Repair	Roof	DBB	P3 Inc.	Johnson Roberts Associates, Inc.	Gibson Roofs, Inc.	Simpson Gumpertz & Heger Inc.
2021	202100400005	Braintree	Hollis	Construction	Accelerated Repair	Roof	DBB	PCA 360	BWA Architecture, Inc	Titan Roofing, Inc.	R.J. Kenney Associates, Inc.
2020	202000400025	Braintree	Liberty	Construction	Accelerated Repair	Roof	DBB	P3 Inc.	Johnson Roberts Associates, Inc.	Capeway Roofing Systems, Inc.	Simpson Gumpertz & Heger Inc.
2021	202100400020	Braintree	Mary E Flaherty School	Construction	Accelerated Repair	Roof	DBB	PCA 360	BWA Architecture, Inc	Young Developers LLC	R.J. Kenney Associates, Inc.
2016	201600400310	Braintree	South Middle School	Building Complete	Core Program	New Construction	DBB	Hill International Company	Miller Dyer Spears Inc.	Bacon Construction Co, Inc.	Rist-Frost-Shumway Engineering, P.C.
2016	201606250002	Bridgewater-Raynham	Mitchell Elementary School	Building Complete	Core Program	New Construction	DBB	CHA Consulting, Inc.	Raymond Design Associates, Inc.	Bacon Construction Co, Inc.	Consulting Engineering Services, LLC
2014	201409100705	Bristol County Agricultural	Bristol County Agricultural High	Closeout	Core Program	Addition / Renovation	CM@R	Colliers Project Leaders NE, LLC	HMFH Architects, Inc.	Gilbane Building Company	NV5 (RDK)
2017	201708100605	Bristol-Plymouth Regional Voc Tech	Bristol-Plymouth Vocational Technical	Construction	Core Program	New Construction	DBB	PMA Consultants, LLC	HMFH Architects, Inc.	Consigli Construction Company, Inc.	BVH Integrated Services, P.C.
2014	201400440421	Brockton	Ashfield Middle School	Closeout	Accelerated Repair	Roof, Boiler	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
2022	202200440505	Brockton	Brockton High	Eligibility Period	Core Program			-	-	-	-

2014	201400440010	Brockton	Brookfield	Closeout	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Enterprise Equipment Co., Inc.	Simpson Gumpertz & Heger Inc.
2014	201400440035	Brockton	Gilmore	Closeout	Accelerated Repair	Roof, Boiler	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Enterprise Equipment Co., Inc.	Rist-Frost-Shumway Engineering, P.C. Simpson Gumpertz & Heger Inc.
2018	201800460040	Brookline	Pierce	Design Development	Core Program	Addition / Renovation	CM@R	Leftfield, LLC	Miller Dyer Spears Inc.	Consigli Construction Company, Inc.	-
2020	202000480007	Burlington	Fox Hill	Feasibility Study	Core Program			Dore & Whittier Management Partners, Inc.	DiNisco Design, Inc.	-	-
2022	202200490006	Cambridge	Amigos School	Approved Project Vote Pending	Accelerated Repair	Roof		Hill International Company	CIVITECTS PC	-	R.J. Kenney Associates, Inc.
2020	202000490007	Cambridge	Cambridgeport	Construction	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Kaestle Boos Associates, Inc.	Lizotte Glass	Simpson Gumpertz & Heger Inc.
2016	201600490090	Cambridge	Fletcher/Maynard Academy	Closeout	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	Atane Engineers, P.C.	John F. Shea Company, Inc.	Gale Associates, Inc.
2021	202100500305	Canton	Wm H Galvin Middle	Feasibility Study	Core Program			Leftfield, LLC	Ai3 Architects LLC	-	-
2014	201408150605	Cape Cod Regional Voc Tech	Cape Cod Region Vocational Technical	Closeout	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Drummey Rosane Anderson, Inc.	Brait Builders Corp.	NV5 (RDK)
2015	201506350505	Central Berkshire	Wahconah Regional High	Closeout	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Drummey Rosane Anderson, Inc.	Barr & Barr Inc.	Horizon Engineering Associates, LLP
2022	202200610003	Chicopee	Barry	Eligibility Period	Core Program			-	-	-	-
2009	200900610021	Chicopee	Dupont Middle	Closeout	Core Program	Renovation	DBB	Arcadis U.S., Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Symmec, Maini & McKee Associates
2020	202000640305	Clinton	Clinton Middle School	Schematic Design	Core Program	New Construction		Dore & Whittier Management Partners, Inc.	Lamoureux Pagano Associates Architects, Inc.	-	-
2015	201500710032	Danvers	Ivan G Smith	Closeout	Core Program	New Construction	CM@R	PMA Consultants, LLC	Tappe Architects, Inc.	W. T. Rich Company Inc.	Colliers Project Leaders NE, LLC
2020	202000730030	Dedham	Oakdale	Schematic Design	Core Program	New Construction		Compass Project Management, Inc.	Jonathan Levi Architects LLC	-	-
2015	201506450305	Dennis-Yarmouth	Mattacheese Middle School	Building Complete	Core Program	New Construction	DBB	PMA Consultants, LLC	Perkins Eastman/DPC	Commodore Builders Corporation	Consulting Engineering Services, LLC
2019	201900790035	Dracut	Brookside Elementary	Building Complete	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	CIVITECTS PC	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
2019	201900790045	Dracut	George H. Englesby Elementary School	Building Complete	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	CIVITECTS PC	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
2021	202100790020	Dracut	Joseph A Campbell Elementary	OPM Selection	Core Program			-	-	-	-
2022	202200830005	East Bridgewater	Central	Eligibility Period	Core Program			-	-	-	-
2019	201900870505	East Longmeadow	East Longmeadow High	Approved Project Vote Pending	Core Program	New Construction		Skanska USA Building, Inc	Jones Whitsett Architects, Inc.	-	-
2014	201400860010	Easthampton	Maple	Building Complete	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2016	201600880003	Easton	Center School	Building Complete	Core Program	New Construction	DBB	PMA Consultants, LLC	Perkins Eastman/DPC	Brait Builders Corp.	Symmec, Maini & McKee Associates
2021	202100930015	Everett	Webster School	Design Development	Accelerated Repair	Roof	DBB	Anser Advisory	Gorman Richardson Architects, Inc.	-	Building Enclosure Associates, LLC (VPC)
2014	201400950505	Fall River	B M C Durfee High	Closeout	Core Program	Addition / Renovation	CM@R	Leftfield, LLC	Ai3 Architects LLC	Suffolk Construction Company	Jacobs Engineering Group Inc.
2017	201700950140	Fall River	James Tansey	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	exPERTcon, Inc.	Tighe & Bond, Inc.	Collins Construction Co., Inc.	Fitzmeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.
2018	201800950325	Fall River	Resiliency Preparatory Academy	Closeout	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	Greenwood Industries, Inc.	Symmec, Maini & McKee Associates
2022	202200950325	Fall River	Resiliency Preparatory Academy	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		STV DPM (fka STV Inc.)	The S/L/A/M Collaborative	-	R.J. Kenney Associates, Inc.
2017	201700950145	Fall River	Samuel Watson	Building Complete	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	exPERTcon, Inc.	Tighe & Bond, Inc.	J.J. Cardosi, Inc.	Fitzmeyer & Tocci Associates, Inc. Thompson & Lichtner Co., Inc.

2018	201800950150	Fall River	Westall	Closeout	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	NB Kenney Company, Inc	Symmes, Maini & McKee Associates
2020	202000960015	Falmouth	Teaticket	Construction	Accelerated Repair	Roof	DBB	Leftfield, LLC	The S/L/A/M Collaborative	Capeway Roofing Systems, Inc.	Russo Barr Associates, Inc.
2021	202100970315	Fitchburg	Arthur M Longsjö Middle School	Construction	Accelerated Repair	Windows / Doors	DBB	NV5	Mount Vernon Group Architects, Inc.	-	3IVE LLC
2022	202200970315	Fitchburg	Arthur M Longsjö Middle School	Approved Project Vote Pending	Accelerated Repair	Boiler		P3 Inc.	IMEG Consultant Corp.	-	WSP USA
2016	201600970016	Fitchburg	Crocker Elementary	Construction	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	saam architecture	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2019	201900970060	Fitchburg	South Street Elementary	Building Complete	Accelerated Repair	Roof, Boiler	DBB	P3 Inc.	edm Services, Inc.	Greenwood Industries, Inc.	Colliers Project Leaders NE, LLC
2020	202000980005	Florida	Abbott Memorial	Construction	Accelerated Repair	Windows / Doors	DBB	Hill International Company	Gale Associates, Inc.	R&R Window Contractors, Inc.	R.J. Kenney Associates, Inc.
2015	201500990015	Foxborough	Mabelle M Burrell	Building Complete	Core Program	Addition / Renovation	DBB	Colliers Project Leaders NE, LLC	Kaestle Boos Associates, Inc.	CTA Construction Co., Inc.	Cadmus Group LLC
2015	201501000305	Framingham	Fuller Middle	Closeout	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Jonathan Levi Architects LLC	Consigli Construction Company, Inc.	Jacobs Engineering Group Inc.
2022	202208180605	Franklin County Regional Voc Tech	Franklin County Technical	Eligibility Period	Core Program			-	-	-	-
2021	202106650002	Freetown-Lakeville	Assawompset Elementary School	Construction	Accelerated Repair	Windows / Doors	DBB	Watermark Environmental, Inc.	The S/L/A/M Collaborative	NENA Construction, Inc.	Building Enclosure Associates, LLC (VPC)
2016	201601030020	Gardner	Waterford Street	Building Complete	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Jones Whitsett Architects, Inc.	Bacon Construction Co, Inc.	Fitzemeyer & Tocci Associates, Inc.
2016	201601070020	Gloucester	East Gloucester Elementary	Building Complete	Core Program	New Construction	CM@R	Turner & Townsend Heery	Dore & Whittier Architects, Inc.	W. T. Rich Company Inc.	NV5 (RDK)
2021	202101070305	Gloucester	Ralph B O'Maley Middle	Construction	Accelerated Repair	Windows / Doors	DBB	Leftfield, LLC	CIVITECTS PC	Lambrian Construction Corp.	Socotec AE Consulting, LLC fka. CBI Consulting LLC
2017	201708210605	Greater Fall River Regional Voc Tech	Diman Regional Vocational Technical High	Construction	Core Program	New Construction	CM@R	Colliers Project Leaders NE, LLC	Kaestle Boos Associates, Inc.	Suffolk Construction Company	WSP USA
2017	201706730010	Groton-Dunstable	Florence Roche School	Construction	Core Program	New Construction	CM@R	Leftfield, LLC	Studio G. Architects, Inc.	Gilbane Building Company	NV5 (RDK)
2021	202106750010	Hamilton-Wenham	Cutler School	Feasibility Study	Core Program			PMA Consultants, LLC	JCJ Architecture, PC	-	-
2015	201501250005	Harvard	Hildreth Elementary School	Closeout	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Arrowstreet Inc.	Shawmut Design and Construction	Bard, Rao + Athanas Consulting Engineers, LLC
2018	201801280100	Haverhill	Consentino Middle School	Design Development	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Dore & Whittier Architects, Inc.	-	Fitzemeyer & Tocci Associates, Inc.
2021	202101280045	Haverhill	Moody	Building Complete	Accelerated Repair	Roof	DBB	P3 Inc.	CSS Architects Incorporated	Capeway Roofing Systems, Inc.	3IVE LLC
2022	202201280045	Haverhill	Moody	Schematic Design	Accelerated Repair	Boiler		Vertex (Eng.) Construction Services	NV5	-	-
2022	202201280067	Haverhill	Silver Hill Elementary School	Approved Project Vote Pending	Accelerated Repair	Boiler		Vertex (Eng.) Construction Services	NV5	-	-
2020	202001310019	Hingham	Plymouth River	Construction	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Homer Contracting	R.J. Kenney Associates, Inc.
2019	201901310010	Hingham	Wm L Foster Elementary	Construction	Core Program	New Construction	DBB	PMA Consultants, LLC	Raymond Design Associates, Inc.	Bacon Construction Co, Inc.	Jacobs Engineering Group Inc.
2020	202001370045	Holyoke	E N White Elementary	Construction	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	ICON architecture, inc.	W.J. Mountford Company	Building Enclosure Associates, LLC (VPC)
2022	202201370070	Holyoke	H.B. Lawrence School	Design Development	Accelerated Repair	Windows / Doors		Leftfield, LLC	Habeeb & Associates Architects, Inc.	-	Building Enclosure Associates, LLC (VPC)
2020	202001370055	Holyoke	Lt Clayre Sullivan Elementary	Construction	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	ICON architecture, inc.	W.J. Mountford Company	Building Enclosure Associates, LLC (VPC)
2022	202201370015	Holyoke	Lt Elmer J McMahon Elementary	Design Development	Accelerated Repair	Windows / Doors		Leftfield, LLC	Habeeb & Associates Architects, Inc.	-	Building Enclosure Associates, LLC (VPC)
2020	202001370060	Holyoke	Maurice A Donahue Elementary	Construction	Accelerated Repair	Roof	DBB	JACOBS Project Management Co.	ICON architecture, inc.	W.J. Mountford Company	Building Enclosure Associates, LLC (VPC)
2022	202201370060	Holyoke	Maurice A Donahue Elementary	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Leftfield, LLC	Habeeb & Associates Architects, Inc.	-	Building Enclosure Associates, LLC (VPC)
2020	202001370030	Holyoke	William R. Peck School	Design Development	Core Program	New Construction - Model School	DBB	Anser Advisory	Mount Vernon Group Architects, Inc.	American Environmental, Inc.	Van Zelm Heywood & Shadford, Inc.
2022	202201370605	Holyoke	Wm J Dean Vocational Technical High	Approved Project Vote Pending	Accelerated Repair	Boiler		Leftfield, LLC	Habeeb & Associates Architects, Inc.	-	Van Zelm Heywood & Shadford, Inc.

2020	202001390010	Hopkinton	Elmwood	Approved Project Vote Pending	Core Program	New Construction		Compass Project Management, Inc.	Perkins Eastman/DPC	-	-	
2019	201901450005	Kingston	Kingston Elementary	Final Audit Approved	Accelerated Repair	Boiler	DBB	exPERTcon, Inc.	Architectural Engineers, Inc.	Veterans Development Corporation, Inc.	Jacobs Engineering Group Inc.	
2017	201701490040	Lawrence	Francis M Leahy	Construction	Core Program	New Construction	DBB	Atlantic Construction and Management, Inc.	Mount Vernon Group Architects, Inc.	J & J Contractors, Inc.	Jacobs Engineering Group Inc.	
2016	201601490050	Lawrence	Henry K Oliver	Construction	Core Program	Addition / Renovation	CM@R	Anser Advisory	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	Rist-Frost-Shumway Engineering, P.C.	
2021	202101530007	Leominster	Fall Brook	Feasibility Study	Core Program			Leftfield, LLC	-	-	-	
2021	202101550505	Lexington	Lexington High	Feasibility Study	Core Program			Dore & Whittier Management Partners, LLC	-	-	-	
2015	201501550035	Lexington	Maria Hastings	Closeout	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	DiNisco Design, Inc.	Walsh Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC	
2021	202101580005	Littleton	Shaker Lane Elementary	OPM Selection	Core Program			-	-	-	-	
2021	202101590017	Longmeadow	Glenbrook Middle	Designer Selection	Core Program			Colliers Project Leaders NE, LLC	-	-	-	
2022	202201600310	Lowell	B.F. Butler Middle School	Schematic Design	Accelerated Repair	Boiler		Watermark Environmental, Inc.	edm Services, Inc.	-	-	
2022	202201600090	Lowell	Bartlett Community Partnership	Schematic Design	Accelerated Repair	Boiler		Watermark Environmental, Inc.	edm Services, Inc.	-	-	
2021	202101600345	Lowell	Dr An Wang School	Design Development	Accelerated Repair	Roof, Boiler	DBB	Arcadis U.S., Inc.	edm Services, Inc.	-	WSP USA	
2019	201901600002	Lowell	Dr Gertrude Bailey	Closeout	Accelerated Repair	Roof, Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	Ambient Temperature Corporation	Symmes, Maini & McKee Associates	
2019	201901600015	Lowell	Greenhalge	Closeout	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	Ambient Temperature Corporation	Symmes, Maini & McKee Associates	
2021	202101600330	Lowell	Henry J Robinson Middle	Design Development	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Arcadis U.S., Inc.	edm Services, Inc.	-	WSP USA	
2022	202201600330	Lowell	Henry J Robinson Middle	Schematic Design	Accelerated Repair	Boiler	DBB	Watermark Environmental, Inc.	edm Services, Inc.	-	-	
2019	201901600315	Lowell	James S Daley Middle School	Closeout	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	Ambient Temperature Corporation	Symmes, Maini & McKee Associates	
2019	201901600340	Lowell	James Sullivan Middle School	Closeout	Accelerated Repair	Roof, Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	Ambient Temperature Corporation	Symmes, Maini & McKee Associates	
2021	202101600050	Lowell	John J Shaughnessy	Design Development	Accelerated Repair	Boiler	DBB	Arcadis U.S., Inc.	edm Services, Inc.	-	Fitzmeyer & Tocci Associates, Inc.	
2022	202201600050	Lowell	John J Shaughnessy	Schematic Design	Accelerated Repair	Roof	DBB	Watermark Environmental, Inc.	edm Services, Inc.	-	-	
2022	202201600010	Lowell	Joseph McAvinnue	Schematic Design	Accelerated Repair	Boiler		Watermark Environmental, Inc.	edm Services, Inc.	-	-	
2014	201401600505	Lowell	Lowell High	Construction	Core Program	Addition / Renovation	CM@R	Skanska USA Building, Inc	Perkins Eastman/DPC	Suffolk Construction Company	Bard, Rao + Athanas Consulting Engineers, LLC	
2019	201901600005	Lowell	Rogers STEM Academy	Closeout	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	Ambient Temperature Corporation	Symmes, Maini & McKee Associates	
2019	201901600075	Lowell	S Christa McAuliffe Elementary	Closeout	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	Ambient Temperature Corporation	Symmes, Maini & McKee Associates	
2021	202101600075	Lowell	S Christa McAuliffe Elementary	Design Development	Accelerated Repair	Roof	DBB	Arcadis U.S., Inc.	edm Services, Inc.	-	Building Enclosure Associates, LLC (VPC)	
2015	201501610020	Ludlow	Chapin Street Elementary School	Closeout	Core Program	New Construction	DBB	STV DPM (fka STV Inc.)	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP	
2022	202201630016	Lynn	A Drewicz Elementary	Approved Project Vote Pending	Accelerated Repair	Windows / Doors		Colliers Project Leaders NE, LLC	Gorman Richardson Architects, Inc.	-	Socotec AE Consulting, LLC fka. CBI Consulting LLC	
2021	202101630090	Lynn	Capt William G Shoemaker	Construction	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	TSKP Studio, LLC	Capeway Roofing Systems, Inc.	Gale Associates, Inc.	
2018	201801630605	Lynn	Lynn Vocational Technical Institute	Closeout	Accelerated Repair	Roof	DBB	Hill International Company	Russo Barr Associates, Inc.	Stanley Roofing Company, Inc.	Socotec AE Consulting, LLC fka. CBI Consulting LLC	
2020	202001630605	Lynn	Lynn Vocational Technical Institute	Construction	Accelerated Repair	Windows / Doors	DBB	PMA Consultants, LLC	CIVITECTS PC	GVW, Inc.	Socotec AE Consulting, LLC fka. CBI Consulting LLC	

2020	202001630420	Lynn	Pickering Middle	Schematic Design	Core Program	New Construction		Leftfield, LLC	Raymond Design Associates, Inc.	Consigli Construction Company, Inc.	-	
2015	201506980010	Manchester Essex Regional	Manchester Memorial Elementary	Building Complete	Core Program	New Construction	CM@R	Dore & Whittier Management Partners, Inc.	JCJ Architecture, PC	W. T. Rich Company Inc.		Symmes, Maini & McKee Associates
2022	202201670035	Mansfield	Harold L Qualters Middle	Approved Project Vote Pending	Accelerated Repair	Boiler		Architectural Consulting Group, LLC	Shekar & Associates, Inc.	-		WSP USA
2021	202101670505	Mansfield	Mansfield High	Construction	Accelerated Repair	Boiler	DBB	Hill International Company	BLW Engineers, Inc.	-		Bard, Rao + Athanas Consulting Engineers, LLC
2015	201501680015	Marblehead	Elbridge Gerry	Closeout	Core Program	New Construction	CM@R	Leftfield, LLC	Raymond Design Associates, Inc.	Gilbane Building Company		NV5 (RDK)
2015	201501700025	Marlborough	Richer	Closeout	Core Program	New Construction - Model School	DBB	CHA Consulting, Inc.	Mount Vernon Group Architects, Inc.	Fontaine Brothers, Inc.		WSP USA
2022	202201700025	Marlborough	Richer	Eligibility Period	Core Program			-	-	-		-
2021	202107000505	Martha's Vineyard	Martha's Vineyard Regional High	OPM Selection	Core Program			-	-	-		-
2019	201901740010	Maynard	Green Meadow	Approved Project Vote Pending	Core Program	New Construction	DBB	Colliers Project Leaders NE, LLC	Mount Vernon Group Architects, Inc.	-		-
2021	202101780017	Melrose	Herbert Clark Hoover	Construction	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	Tighe & Bond, Inc.	-		Russo Barr Associates, Inc.
2021	202101780025	Melrose	Horace Mann	Construction	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	Tighe & Bond, Inc.	-		Russo Barr Associates, Inc.
2014	201401820505	Middleborough	Middleborough High	Building Complete	Core Program	New Construction	DBB	Compass Project Management, Inc.	Drummey Rosane Anderson, Inc.	Fontaine Brothers, Inc.		Colliers Project Leaders NE, LLC
2016	201601860025	Millbury	Raymond E. Shaw Elementary	Building Complete	Core Program	New Construction	DBB	Hill International Company	Turowski2 Architecture, Inc.	Fontaine Brothers, Inc.		Consulting Engineering Services, LLC
2014	201401870005	Millis	Clyde F Brown	Closeout	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Tappe Architects, Inc.	Bacon-Agostini Construction Joint Venture		Colliers Project Leaders NE, LLC
2021	202101870505	Millis	Millis High School	Designer Selection	Core Program			-	-	-		-
2009	200908300605	Minuteman Voc Tech	Minuteman Regional High	Closeout	Core Program	New Construction	CM@R	Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	Gilbane Building Company		Bard, Rao + Athanas Consulting Engineers, LLC
2019	201901910025	Monson	Quarry Hill Community School	Building Complete	Accelerated Repair	Roof	DBB	P3 Inc.	Simpson Gumpertz & Heger Inc.	J.D. Rivet & Co., Inc.		Colliers Project Leaders NE, LLC
2019	201907250505	Nashoba	Nashoba Regional	Approved Project Vote Pending	Core Program	New Construction		Skanska USA Building, Inc	Kaestle Boos Associates, Inc.	-		-
2015	201501980305	Natick	J F Kennedy Middle School	Building Complete	Core Program	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	Brait Builders Corp.		Rist-Frost-Shumway Engineering, P.C.
2016	201606600505	Nauset	Nauset Regional High	Construction	Core Program	Addition / Renovation	DBB	CHA Consulting, Inc.	Flansburgh Associates, Inc.	Brait Builders Corp.		Consulting Engineering Services, LLC
2017	201702010015	New Bedford	Elizabeth Carter Brooks	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	Johnson Roberts Associates, Inc.	J.J. Cardosi, Inc.		WSP USA
2022	202202010015	New Bedford	Elizabeth Carter Brooks	Design Development	Accelerated Repair	Roof	DBB	PCA 360	CGKV Architects, Inc.	-		Simpson Gumpertz & Heger Inc.
2022	202202010075	New Bedford	Ellen R Hathaway	Design Development	Accelerated Repair	Windows / Doors	DBB	PCA 360	CGKV Architects, Inc.	-		Simpson Gumpertz & Heger Inc.
2020	202002010020	New Bedford	Elwyn G Campbell	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	NV5	CSS Architects Incorporated	J.J. Cardosi, Inc.		WSP USA
2018	201802010115	New Bedford	John Avery Parker	Closeout	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	Habeeb & Associates Architects, Inc.	Capeway Roofing Systems, Inc.		Thompson & Lichtner Co., Inc.
2020	202002010050	New Bedford	John B Devalles	Schematic Design	Core Program	New Construction		P3 in collaboration w/ Atlantic Construction & Mgt Inc.	Turowski2 Architecture, Inc.	-		-
2018	201802010510	New Bedford	Trinity Day Academy	Closeout	Accelerated Repair	Boiler	DBB	Vertex (Eng.) Construction Services	Habeeb & Associates Architects, Inc.	Araujo Brothers Plumbing & Heating		WSP USA
2020	202002070040	Newton	Countryside	Schematic Design	Core Program	New Construction		Dore & Whittier Management Partners, Inc.	DiNisco Design, Inc.	-		-
2018	201809150705	Norfolk County Agricultural	Norfolk County Agricultural	Building Complete	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	Raymond Design Associates, Inc.	Homer Contracting		Gale Associates, Inc.
2019	201902090015	North Adams	Greylock	Feasibility Study	Core Program			Colliers Project Leaders NE, LLC	TSKP Studio, LLC	-		-

2021	202102110015	North Andover	Kittredge	Designer Selection	Core Program				Colliers Project Leaders NE, LLC	-	-	-
2021	202102120505	North Attleborough	North Attleboro High	Designer Selection	Core Program				The Vertex Companies, LLC	-	-	-
2016	201607350030	North Middlesex	Hawthorne Brook	Closeout	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	Gale Associates, Inc.	
2011	201107350505	North Middlesex	North Middlesex Regional	Closeout	Core Program	New Construction	DBB	Turner & Townsend Heery	Symmes Maini & McKee Associates, Inc.	CTA Construction Co., Inc.	Horizon Engineering Associates, LLP	
2016	201607350020	North Middlesex	Squannacook	Closeout	Accelerated Repair	Roof	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	Vanguard Construction Company, Inc.	Gale Associates, Inc.	
2016	201607350035	North Middlesex	Varnum Brook	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Habeeb & Associates Architects, Inc.	E. Amanti & Sons, Inc.	Gale Associates, Inc.	
2010	201002170505	North Reading	North Reading High	Closeout	Core Program	Addition / Renovation	CM@R	PMA Consultants, LLC	Dore & Whittier Architects, Inc.	Gilbane Building Company	Cannon Design	
2019	201902140305	Northbridge	Northbridge Middle	Closeout	Accelerated Repair	Boiler	DBB	Architectural Consulting Group, LLC	Habeeb & Associates Architects, Inc.	NB Kenney Company, Inc	NV5 (RDK)	
2015	201502140001	Northbridge	W Edward Balmer	Closeout	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Dore & Whittier Architects, Inc.	Fontaine Brothers, Inc.	Fitzmeyer & Tocci Associates, Inc.	
2017	201708530605	Northeast Metropolitan Regional Voc Tech	Northeast Metro Regional Vocational	Construction	Core Program	New Construction	CM@R	PMA Consultants, LLC	Drummey Rosane Anderson, Inc.	Gilbane Building Company	Consulting Engineering Services, LLC Symmes, Maini & McKee Associates	
2017	201702180060	Norton	Henri A. Yelle	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.	
2017	201702180015	Norton	J C Solmonese	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.	
2017	201702180010	Norton	L G Nourse Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Architectural Consulting Group, LLC	Turowski2 Architecture, Inc.	Lockheed Window Corporations	Simpson Gumpertz & Heger Inc.	
2018	201802200305	Norwood	Dr. Philip O. Coakley Middle School	Construction	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Ai3 Architects LLC	W. T. Rich Company Inc.	Horizon Engineering Associates, LLP	
2021	202108550605	Old Colony Reg Voc Tech	Old Colony Regional Vocational Technical	OPM Selection	Core Program							
2016	201602230010	Orange	Dexter Park	Construction	Core Program	Addition / Renovation	DBB	Hill International Company	Raymond Design Associates, Inc.	J & J Contractors, Inc.	WSP USA	
2018	201802290027	Peabody	William A Welch Sr	Construction	Core Program	Addition / Renovation	CM@R	Dore & Whittier Management Partners, Inc.	DiNisco Design, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC	
2015	201507450505	Pentucket	Pentucket Regional Sr High	Building Complete	Core Program	New Construction	CM@R	Vertex (Eng.) Construction Services	Dore & Whittier Architects, Inc.	Rich-KBE Pentucket School Joint Venture	Jacobs Engineering Group Inc.	
2020	202002390011	Plymouth	Federal Furnace School	Construction	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	TSKP Studio, LLC	Greenwood Industries, Inc.	Gale Associates, Inc.	
2020	202002390012	Plymouth	Indian Brook	Construction	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	TSKP Studio, LLC	Greenwood Industries, Inc.	Gale Associates, Inc.	
2020	202002390047	Plymouth	West Elementary	Construction	Accelerated Repair	Roof	DBB	Colliers Project Leaders NE, LLC	TSKP Studio, LLC	Greenwood Industries, Inc.	Gale Associates, Inc.	
2019	201907530010	Quabbin	Hubbardston Center	Building Complete	Accelerated Repair	Roof	DBB	Anser Advisory	CSS Architects Incorporated	Capeway Roofing Systems, Inc.	Thompson & Lichtner Co., Inc.	
2015	201502430020	Quincy	Beechwood Knoll Elementary	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	Atlantic Construction and Management, Inc.	Baker/Wohl Architects, Inc.	Alpha Contracting Associates, Inc.	Socotec AE Consulting, LLC fka. CBI Consulting LLC	
2022	202202430075	Quincy	Francis W Parker	Design Development	Accelerated Repair	Boiler		Anser Advisory	TSKP Studio, LLC	-	-	
2022	202202430065	Quincy	Montclair	Design Development	Accelerated Repair	Roof		Anser Advisory	TSKP Studio, LLC	-	-	
2017	201702430510	Quincy	North Quincy High	Closeout	Accelerated Repair	Roof	DBB	STV DPM (fka STV Inc.)	Socotec AE Consulting, LLC fka. CBI Consulting LLC	Greenwood Industries, Inc.	Gale Associates, Inc.	
2013	201302430320	Quincy	Reay E. Sterling Middle School	Closeout	Core Program	New Construction	CM@R	PCA 360	Ai3 Architects LLC	Bond Brothers, Inc.	Symmes, Maini & McKee Associates	
2020	202002430095	Quincy	Squantum	Feasibility Study	Core Program			PCA 360	Arrowstreet Inc.	-	-	
2022	202202430110	Quincy	Wollaston School	Design Development	Accelerated Repair	Roof		Anser Advisory	TSKP Studio, LLC	-	-	
2017	201702440020	Randolph	Elizabeth G Lyons Elementary	Construction	Core Program	New Construction	DBB	CHA Consulting, Inc.	TSKP Studio, LLC	Agostini Construction Co., Inc.	Jacobs Engineering Group Inc.	
2017	201702440015	Randolph	Margaret L Donovan	Closeout	Accelerated Repair	Windows / Doors, Boiler	DBB	Atlantic Construction and Management, Inc.	TSKP Studio, LLC	A&A Window Products, Inc.	Consulting Engineering Services, LLC Gale Associates, Inc.	

2017	201702440040	Randolph	Martin E Young Elementary	Closeout	Accelerated Repair	Windows / Doors	DBB	Atlantic Construction and Management, Inc.	TSKP Studio, LLC	Modern Glass & Aluminum, Inc.	Gale Associates, Inc.
2021	202102460017	Reading	J Warren Killam	Designer Selection	Core Program			-	-	-	-
2020	202002480025	Revere	Abraham Lincoln	Construction	Accelerated Repair	Windows / Doors	DBB	PMA Consultants, LLC	CGKV Architects, Inc.	GVW, Inc.	R.J. Kenney Associates, Inc.
2020	202002480013	Revere	Beachmont Veterans Memorial School	Construction	Accelerated Repair	Boiler	DBB	PMA Consultants, LLC	CGKV Architects, Inc.	NB Kenney Company, Inc	Bard, Rao + Athanas Consulting Engineers, LLC
2018	201802480505	Revere	Revere High	Feasibility Study	Core Program	New Construction		Leftfield, LLC	Perkins Eastman/DPC	Consigli Construction Company, Inc.	-
2016	201602510060	Rockland	Jefferson Elementary School	Building Complete	Core Program	New Construction	DBB	PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	Brait Builders Corp.	NV5 (RDK)
2019	201902580005	Salem	Bentley	Closeout	Accelerated Repair	Boiler	DBB	NETCO Construction Project Managers, Inc.	Johnson Roberts Associates, Inc.	Ambient Temperature Corporation	Fitzemeyer & Tocci Associates, Inc.
2022	202202580505	Salem	Salem High	Eligibility Period	Core Program			-	-	-	-
2014	201402620505	Saugus	Saugus High	Closeout	Core Program	New Construction	CM@R	PMA Consultants, LLC	HMFH Architects, Inc.	Suffolk Construction Company	Consulting Engineering Services, LLC
2012	201202640305	Scituate	Gates Intermediate School	Closeout	Core Program	New Construction	DBB	CHA Consulting, Inc.	Dore & Whittier Architects, Inc.	Bacon-Agostini Construction Joint Venture	WSP USA
2020	202002640010	Scituate	Hatherly Elementary	Schematic Design	Core Program	New Construction		Vertex (Eng.) Construction Services	Dore & Whittier Architects, Inc.	-	-
2016	201602660505	Sharon	Sharon High	Building Complete	Core Program	New Construction	CM@R	PMA Consultants, LLC	Tappe Architects, Inc.	Consigli Construction Company, Inc.	Fitzemeyer & Tocci Associates, Inc.
2015	201502710005	Shrewsbury	Beal School	Final Audit Approved	Core Program	New Construction	CM@R	PMA Consultants, LLC	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2021	202102710030	Shrewsbury	Oak Middle School	Design Development	Accelerated Repair	Windows / Doors	DBB	Vertex (Eng.) Construction Services	Mount Vernon Group Architects, Inc.	-	Simpson Gumpertz & Heger Inc.
2017	201702730305	Somerset	Somerset Middle School	Construction	Core Program	New Construction	CM@R	CGA Project Management	Ai3 Architects LLC	Brait Builders Corp.	Bard, Rao + Athanas Consulting Engineers, LLC
2013	201302740505	Somerville	Somerville High	Building Complete	Core Program	Addition / Renovation	CM@R	PMA Consultants, LLC	Symmes Maini & McKee Associates, Inc.	Suffolk Construction Company	WSP USA
2021	202108730605	South Shore Regional Voc Tech	So Shore Vocational Technical High	Feasibility Study	Core Program			Leftfield, LLC	Drummey Rosane Anderson, Inc.	-	-
2021	202102760020	Southborough	Margaret A Neary	Designer Selection	Core Program			Skanska USA Building, Inc	-	-	-
2018	201807670505	Spencer-E Brookfield	David Prouty High	Construction	Core Program	Addition / Renovation	CM@R	Colliers Project Leaders NE, LLC	Jones Whitsett Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2015	201502810025	Springfield	Brightwood	Closeout	Core Program	New Construction	CM@R	Skanska USA Building, Inc	DiNisco Design, Inc.	Daniel O'Connell's Sons, Inc.	WSP USA
2019	201902810080	Springfield	Frederick Harris	Final Audit Approved	Accelerated Repair	Boiler	DBB	PCA 360	Raymond Design Associates, Inc.	Adams Plumbing and Heating, Inc.	Horizon Engineering Associates, LLP
2021	202102810068	Springfield	Glickman Elementary	Construction	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	Johnson Roberts Associates, Inc.	W.J. Mountford Company	Simpson Gumpertz & Heger Inc.
2020	202002810530	Springfield	High School/Science-Tech	Closeout	Accelerated Repair	Windows / Doors	DBB	Arcadis U.S., Inc.	Simpson Gumpertz & Heger Inc.	NENA Construction, Inc.	Russo Barr Associates, Inc.
2019	201902810100	Springfield	Indian Orchard Elementary	Final Audit Approved	Accelerated Repair	Boiler	DBB	PCA 360	Raymond Design Associates, Inc.	TJ Conway Company	Horizon Engineering Associates, LLP
2022	202202810023	Springfield	Milton Bradley School	Approved Project Vote Pending	Accelerated Repair	Boiler		Arcadis U.S., Inc.	NV5	-	Van Zelm Heywood & Shadford, Inc.
2022	202202810055	Springfield	Rebecca M Johnson	Approved Project Vote Pending	Accelerated Repair	Boiler		Arcadis U.S., Inc.	NV5	-	Van Zelm Heywood & Shadford, Inc.
2021	202102810500	Springfield	Springfield Central High	Construction	Accelerated Repair	Boiler	DBB	Colliers Project Leaders NE, LLC	Johnson Roberts Associates, Inc.	-	Van Zelm Heywood & Shadford, Inc.
2019	201902810160	Springfield	Sumner Avenue	Final Audit Approved	Accelerated Repair	Boiler	DBB	PCA 360	Raymond Design Associates, Inc.	Adams Plumbing and Heating, Inc.	Horizon Engineering Associates, LLP
2021	202102810015	Springfield	Thomas M Balliet	Construction	Accelerated Repair	Windows / Doors	DBB	Colliers Project Leaders NE, LLC	Johnson Roberts Associates, Inc.	D.A. Sullivan & Sons, Inc.	Simpson Gumpertz & Heger Inc.
2016	201602810045	Springfield	William N. DeBerry	Building Complete	Core Program	New Construction	CM@R	Skanska USA Building, Inc	DiNisco Design, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2018	201802840505	Stoneham	Stoneham High	Construction	Core Program	New Construction	CM@R	Symmes Maini & McKee Associates, Inc.	Perkins+Will	Consigli Construction Company, Inc.	NV5 (RDK)
2020	202002850015	Stoughton	South Elementary	Schematic Design	Core Program	New Construction		Compass Project Management, Inc.	Drummey Rosane Anderson, Inc.	-	-

2013	201302850505	Stoughton	Stoughton High	Closeout	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Drummey Rosane Anderson, Inc.	Consigli Construction Company, Inc.	Fitzmeyer & Tocci Associates, Inc.
2017	201702910010	Swampscott	Hadley	Construction	Core Program	New Construction	DBB	Hill International Company	LaVallee Brensinger Architects	CTA Construction Co., Inc.	WSP USA
2022	202202920305	Swansea	Joseph Case Jr High	Eligibility Period	Core Program			-	-	-	-
2020	202002930057	Taunton	H H Galligan	Construction	Accelerated Repair	Windows / Doors, Boiler	DBB	Hill International Company	Tighe & Bond, Inc.	Lambrian Construction Corp.	WSP USA
2014	201402930015	Taunton	Mulcahey Elementary School	Closeout	Core Program	New Construction	DBB	CGA Project Management	Dore & Whittier Architects, Inc.	Agostini Construction Co., Inc.	Consulting Engineering Services, LLC
2018	201802930525	Taunton	Taunton Alternative High School	Closeout	Accelerated Repair	Roof, Windows / Doors	DBB	NETCO Construction Project Managers, Inc.	Simpson Gumpertz & Heger Inc.	J.J. Cardosi, Inc.	Building Enclosure Associates, LLC (VPC)
2015	201502950025	Tewksbury	Louise Davy Trahan	Building Complete	Core Program	New Construction	CM@R	Turner & Townsend Heery	Flansburgh Associates, Inc.	Consigli Construction Company, Inc.	Consulting Engineering Services, LLC
2019	201908780605	Tri County	Tri-County Regional Vocational Technical	Approved Project Vote Pending	Core Program	New Construction		Dore & Whittier Management Partners, Inc.	Drummey Rosane Anderson, Inc.	-	-
2018	201803010305	Tyngsborough	Tyngsborough Middle	Construction	Core Program	New Construction	CM@R	Leftfield, LLC	JCJ Architecture, PC	Fontaine Brothers, Inc.	NV5 (RDK)
2019	201903050505	Wakefield	Wakefield Memorial High	Design Development	Core Program	New Construction	CM@R	Leftfield, LLC	Symmes Maini & McKee Associates, Inc.	Bond Building Construction, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2018	201803070305	Walpole	Bird Middle	Construction	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Tappe Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2014	201403080505	Waltham	Waltham Sr High	Construction	Core Program	New Construction	CM@R	Leftfield, LLC	Symmes Maini & McKee Associates, Inc.	Consigli Construction Company, Inc.	Fitzmeyer & Tocci Associates, Inc.
2015	201503100003	Wareham	John William Decas	Final Audit Approved	Accelerated Repair	Roof, Boiler	DBB	Colliers Project Leaders NE, LLC	ICON architecture, inc.	Nadeau Corporation	Bard, Rao + Athanas Consulting Engineers, LLC Gale Associates, Inc.
2015	201503100017	Wareham	Minot Forest	Building Complete	Core Program	New Construction	DBB	PMA Consultants, LLC	Mount Vernon Group Architects, Inc.	Bacon Construction Co, Inc.	Symmes, Maini & McKee Associates
2021	202103100305	Wareham	Wareham Middle	Construction	Accelerated Repair	Roof	DBB	Leftfield, LLC	CGKV Architects, Inc.	Capeway Roofing Systems, Inc.	Socotec AE Consulting, LLC fka. CBI Consulting LLC
2021	202103100505	Wareham	Wareham Senior High	Construction	Accelerated Repair	Boiler	DBB	Leftfield, LLC	CGKV Architects, Inc.	D.D.S. Industries, Inc.	Bard, Rao + Athanas Consulting Engineers, LLC
2017	201703140505	Watertown	Watertown High	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Ai3 Architects LLC	-	Fitzmeyer & Tocci Associates, Inc.
2019	201903150020	Wayland	Loker School	Closeout	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Tighe & Bond, Inc.	Tower Construction Corporation	Gale Associates, Inc.
2018	201803160505	Webster	Bartlett Jr Sr High Sch	Design Development	Core Program	Addition / Renovation	DBB	Colliers Project Leaders NE, LLC	Flansburgh Associates, Inc.	-	Van Zelm Heywood & Shadford, Inc.
2017	201703170050	Wellesley	Ernest F Upham	Construction	Core Program	New Construction	CM@R	Compass Project Management, Inc.	Symmes Maini & McKee Associates, Inc.	Shawmut Design and Construction	Fitzmeyer & Tocci Associates, Inc.
2022	202203230003	West Bridgewater	Rose L Macdonald	Eligibility Period	Core Program			-	-	-	-
2015	201503320007	West Springfield	Philip G Coburn	Building Complete	Core Program	New Construction	DBB	NV5 (fka Joslin, Lesser + Associates Inc.)	TSKP Studio, LLC	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2016	201603210010	Westborough	Annie E Fales	Building Complete	Core Program	New Construction	CM@R	Vertex (Eng.) Construction Services	HMFH Architects, Inc.	Gilbane Building Company	Fitzmeyer & Tocci Associates, Inc.
2018	201803250015	Westfield	Franklin Ave	Construction	Core Program	New Construction	DBB	P3 Inc.	Caolo & Bieniek Associates, Inc.	Fontaine Brothers, Inc.	Van Zelm Heywood & Shadford, Inc.
2021	202103260310	Westford	Blanchard Middle	Design Development	Accelerated Repair	Roof	DBB	P3 Inc.	CIVITECTS PC	-	3IVE LLC
2020	202003300505	Weston	Weston High	Construction	Accelerated Repair	Roof	DBB	P3 Inc.	BWA Architecture, Inc	-	Socotec AE Consulting, LLC fka. CBI Consulting LLC
2019	201903310030	Westport	Westport Elementary	Building Complete	Accelerated Repair	Roof	DBB	Vertex (Eng.) Construction Services	The S/L/A/M Collaborative	Capeway Roofing Systems, Inc.	Simpson Gumpertz & Heger Inc.
2014	201403310305	Westport	Westport Junior/Senior High School	Building Complete	Core Program	New Construction	CM@R	CHA Consulting, Inc.	Jonathan Levi Architects LLC	Agostini Construction Co., Inc.	BVH Integrated Services, P.C.
2017	201703350015	Westwood	Paul Hanlon	Construction	Core Program	New Construction	DBB	Compass Project Management, Inc.	Dore & Whittier Architects, Inc.	Brait Builders Corp.	Jacobs Engineering Group Inc.
2015	201503360020	Weymouth	Maria Weston Chapman Middle School	Building Complete	Core Program	Addition / Renovation	CM@R	Hill International Company	HMFH Architects, Inc.	Bond Brothers, Inc.	WSP USA

2019	201903360085	Weymouth	Ralph Talbot	Closeout	Accelerated Repair	Boiler	DBB	Colliers Project Leaders NE, LLC	Shekar & Associates, Inc.	Ambient Temperature Corporation	WSP USA
2019	201907800310	Whitman-Hanson	Whitman Middle	Approved Project Vote Pending	Core Program	New Construction		Colliers Project Leaders NE, LLC	Ai3 Architects LLC	-	-
2019	201908850605	Whittier Voc	Whittier Regional Vocational	Schematic Design	Core Program	New Construction		Leftfield, LLC	JCJ Architecture, PC	Consigli Construction Company, Inc.	-
2020	202003420015	Wilmington	Wildwood	Feasibility Study	Core Program			Symmes Maini & McKee Associates, Inc.	Dore & Whittier Architects, Inc.	-	-
2009	200903420505	Wilmington	Wilmington High	Final Audit Approved	Core Program	New Construction	CM@R	NV5 (fka Joslin, Lesser + Associates Inc.)	Dore & Whittier Architects, Inc.	Gilbane Building Company	Symmes, Maini & McKee Associates
2019	201903440020	Winchester	Lynch Elementary	Design Development	Core Program	New Construction	DBB	Hill International Company	Tappe Architects, Inc.	-	Jacobs Engineering Group Inc.
2019	201903480035	Worcester	Burncoat Street	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
2018	201803481008	Worcester	Challenge and Reach Academy	Closeout	Accelerated Repair	Roof, Windows / Doors, Boiler	DBB	Arcadis U.S., Inc.	Johnson Roberts Associates, Inc.	D.A. Sullivan & Sons, Inc.	Colliers Project Leaders NE, LLC
2016	201603480512	Worcester	Doherty Memorial High	Construction	Core Program	New Construction	CM@R	Tishman Construction Corporation of MA	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	BVH Integrated Services, P.C.
2019	201903480160	Worcester	Lincoln Street	Closeout	Accelerated Repair	Boiler	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Rist-Frost-Shumway Engineering, P.C.
2014	201403480520	Worcester	South High Community	Closeout	Core Program	New Construction	CM@R	Turner & Townsend Heery	Lamoureux Pagano Associates Architects, Inc.	Fontaine Brothers, Inc.	Horizon Engineering Associates, LLP
2019	201903480230	Worcester	Tatnuck	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
2019	201903480280	Worcester	Vernon Hill School	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
2020	202003480225	Worcester	Worcester Arts Magnet School	Construction	Accelerated Repair	Roof	DBB	Architectural Consulting Group, LLC	Russo Barr Associates, Inc.	J.D. Rivet & Co., Inc.	3IVE LLC
2019	201903480420	Worcester	Worcester East Middle	Closeout	Accelerated Repair	Roof	DBB	exPERTcon, Inc.	Habeeb & Associates Architects, Inc.	Greenwood Industries, Inc.	Russo Barr Associates, Inc.
2022	202203500010	Wrentham	Charles E Roderick	Eligibility Period	Core Program			-	-	-	-

APPENDIX B
2023-26 ESTIMATED BID DATES

2023 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 17, 2023

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Oct '22	Nov '22	Dec '22	Jan '23	Feb '23	Mar '23	Apr '23	May '23	Jun '23	Jul '23	Aug '23	Sep '23	Oct '23	Nov '23	Dec '23	Jan '24	Feb '24	Mar '24
Fitchburg	ES	845	New	\$ 65.0	Wed 11/9/22	Tue 2/14/23	\$ 49.8	NTP approved: February 2023...	<p>Fitchburg - Crocker Elementary School 11/9 — 2/14 1/31</p>																	
Wellesley	ES	365	New	\$ 72.5	Tue 11/15/22	Thu 4/13/23	\$ 56.4	GMP approved: April 2023...	<p>Wellesley - Ernest F. Upham Elementary School 11/15 — 4/13 3/3</p>																	
Groton Dunstable	ES	645	New	\$ 78.7	Fri 11/18/22	Thu 6/29/23	\$ 61.7	GMP approved: June 2023...	<p>Groton Dunstable - Florence Roche School 11/18 — 6/29 1/13</p>																	
Randolph	ES	315	New	\$ 50.4	Wed 12/7/22	Wed 1/25/23	\$ 41.6	NTP approved: January 2023...	<p>Randolph - Elizabeth G. Lyons Elementary School 12/7 — 1/25 1/11</p>																	
Walpole	MS	905	New	\$ 115.8	Fri 12/16/22	Tue 2/14/23	\$ 92.9	GMP approved: February 2023...	<p>Walpole - Bird Middle School 12/16 — 2/14 1/13</p>																	
Westfield	ES	395	New	\$ 62.2	Fri 1/20/23	Tue 3/21/23	\$ 50.4	NTP approved: March 2023...	<p>Westfield - Franklin Avenue Elementary School 1/20 — 3/21 3/7</p>																	
Somerset	MS	590	New	\$ 85.0	Wed 1/25/23	Mon 3/6/23	\$ 70.0	GMP approved: March 2023...	<p>Somerset Middle School 1/25 — 3/6 2/28</p>																	
Boston	PK-12	60	New	\$ 92.0	Wed 2/15/23	Fri 11/17/23	\$ 69.4	GMP targeted: November 2023...	<p>Boston - William E. Carter School 2/15 — 11/17 3/31</p>																	
Hingham	ES	605	New	\$ 113.3	Wed 3/1/23	Tue 5/16/23	\$ 88.1	NTP approved: May 2023...	<p>Hingham - William L. Foster Elementary School 3/1 — 5/16 4/25</p>																	
Norwood	MS	1070	New	\$ 150.0	Wed 3/8/23	Mon 6/12/23	\$ 114.4	GMP approved: June 2023	<p>Norwood - Coakley Middle School 3/8 — 6/12 4/18</p>																	
Watertown	HS	720	New	\$ 201.5	Wed 3/22/23	Wed 5/10/23	\$ 138.7	NTP approved: May 2023...	<p>Watertown High School 3/22 — 5/10 5/3</p>																	
Lawrence	K-8	1000	New	\$ 103.7	Wed 4/5/23	Wed 5/24/23	\$ 81.8	NTP approved: May 2023...	<p>Lawrence - Francis M. Leahy Elementary School 4/5 — 5/24 5/10</p>																	

Construction Manager at Risk Project CMR Project Pending Local Approval Filed Sub Bids
 Design Bid Build Project DBB Project Pending Local Approval GC Bids/GMP Execution

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.

Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

2023 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 17, 2023

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Oct '22	Nov '22	Dec '22	Jan '23	Feb '23	Mar '23	Apr '23	May '23	Jun '23	Jul '23	Aug '23	Sep '23	Oct '23	Nov '23	Dec '23	Jan '24	Feb '24	Mar '24					
Tyngsborough	MS	480	New	\$ 83.5	Fri 5/19/23	Wed 12/13/23	\$ 66.0	GMP targeted: December 2023...								5/19															
Bristol - Plymouth	V&A- HS	1434	New	\$ 305.6	Thu 6/29/23	Thu 8/31/23	\$ 240.9	NTP targeted: August 2023...																							
Northeast Metro	V&A- HS	1600	New	\$ 317.4	Wed 8/30/23	Fri 2/16/24	\$ 244.0	GMP targeted: February 2024...													8/30										
Spencer- East Brookfield	HS	305	Add/ Reno	\$ 111.6	Wed 9/13/23	Thu 11/30/23	\$ 91.4	GMP targeted: November 2023...													9/13										
Winchester	ES	520	New	\$ 94.5	Thu 10/5/23	Thu 11/30/23	\$ 67.7	NTP targeted: November 2023...													10/5										
Holyoke	MS	550	New	\$ 85.5	Thu 11/30/23	Thu 1/11/24	\$ 70.6	GMP targeted: January 2024...													11/30										
Total		12,404		\$ 2,188.1			\$ 1,695.8																								

Construction Manager at Risk Project		CMR Project Pending Local Approval		Filed Sub Bids	
Design Bid Build Project		DBB Project Pending Local Approval		GC Bids/GMP Execution	

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.










Projects represented by a single black diamond have not completed a Schematic Design Submission.




Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval.
Note: Budget values are in millions.




2024 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 17, 2023

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Nov '23	Dec '23	Jan '24	Feb '24	Mar '24	Apr '24	May '24	Jun '24	Jul '24	Aug '24	Sep '24	Oct '24	Nov '24	Dec '24	Jan '25	Feb '25								
Webster	C-HS	445	Add/Reno	\$ 101.4	Wed 11/29/23	Wed 1/17/24	\$ 78.2	NTP targeted: January 2024	Webster - Bartlett Junior Senior High School 11/29  1/17																							
Greater Fall River	V&A - HS	1500	New	\$ 293.5	Thu 12/14/23	Thu 3/21/24	\$ 244.4	NTP targeted: March 2024	Greater Fall River - Diman Regional VTHS 12/14  3/21																							
Haverhill	MS	1,080	New	\$ 159.9	Wed 1/10/24	Fri 3/8/24	\$ 125.1	NTP targeted: March 2024	Haverhill - Dr. Albert B. Consentino Middle School 1/10  3/8																							
Wakefield	HS	1,000	New	\$ 275.3	Mon 4/29/24	Fri 6/28/24	\$ 224.2	GMP targeted: June 2024	Wakefield - Wakefield memorial High School 4/29  6/28																							
Amherst	ES	575	New	\$ 99.2	Wed 5/1/24	Wed 6/26/24	\$ 81.3	NTP targeted: June 2024	Amherst - Fort River Elementary School 5/1  6/26																							
Brookline	K-8	725	Add/Reno	\$ 211.9	Wed 9/18/24	Fri 12/13/24	\$ 168.3	GMP targeted: December 2024	Brookline - John R. Pierce School 9/18  12/13																							
Maynard	ES	395	New	\$ 83.6	Wed 10/2/24	Wed 11/6/24	\$ 66.9	NTP targeted: November 2024	Maynard - Green Meadow Elementary School 10/2  11/6																							
Lynn	MS	1100	New		Tue 10/15/24	Wed 12/11/24		GMP targeted: December 2024	Lynn - Pickering Middle School 10/15  12/11																							
East Longmeadow	HS	800	New	\$ 177.5	Mon 12/2/24	Mon 1/13/25	\$ 147.8	GMP targeted: January 2025	East Longmeadow - East Longmeadow High School 12/2  1/13																							
Total		6,670		\$ 1,402.3			\$ 1,136.2																									

Construction Manager at Risk Project  CMR Project Pending Local Approval  Filed Sub Bids 

Design Bid Build Project  DBB Project Pending Local Approval  GC Bids/GMP Execution 

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.

Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

2025 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 17, 2023

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Nov '24	Dec '24	Jan '25	Feb '25	Mar '25	Apr '25	May '25	Jun '25	Jul '25	Aug '25	Sep '25	Oct '25	Nov '25	Dec '25	Jan '26	Feb '26	Mar '26
Whitman-Hanson	MS	675	New	\$ 135.3	Fri 12/13/24	Fri 2/28/25	\$ 106.7	NTP targeted: February 2025																	
									Whitman-Hanson - Whitman Middle School 12/13 2/28 2/1																
Newton	ES	465	New		Fri 1/3/25	Fri 2/28/25		NTP targeted: February 2025																	
									Newton - Countryside Elementary School 1/3 2/28 2/14																
New Bedford	ES	760	New		Wed 1/8/25	Wed 2/12/25		NTP targeted: February 2025																	
									New Bedford - John B. DeValles Elementary School 1/8 2/12 1/29																
Nashoba	HS	925	New	\$ 241.7	Mon 2/3/25	Thu 10/9/25	\$ 199.6	GMP targeted: October 2025																	
									Nashoba Regional High School 2/3 10/9 3/7																
Tri County	HS	1000	New	\$ 286.0	Tue 2/4/25	Mon 4/28/25	\$ 233.7	GMP targeted: April 2025																	
									Tri County Regional Vocational Technical High School 2/4 4/28 3/4																
Hopkinton	ES	1195	New	\$ 158.4	Tue 3/11/25	Tue 4/22/25	\$ 125.0	NTP targeted: April 2025																	
									Hopkinton - Elmwood Elementary School 3/11 4/22 4/8																
Dedham	ES	550	New		Tue 5/6/25	Tue 5/6/25		NTP targeted: May 2025																	
									Dedham - Oakdale Elementary School 5/6																
Stoughton	ES	515	New		Fri 6/13/25	Fri 6/13/25		NTP targeted: June 2025																	
									Stoughton - South Elementary School 6/13																
Whittier Voc Tech	HS	1280	New		Wed 7/23/25	Wed 12/31/25		GMP targeted: December 2025																	
									Whittier Regional Vocational Technical High School 7/23 12/31 10/14																
Clinton	MS	700	New		Wed 8/6/25	Wed 8/6/25		NTP targeted: August 2025																	
									Clinton Middle School 8/6																
Scituate	ES	460	New		Thu 8/7/25	Thu 8/7/25		NTP targeted: August 2025																	
									Scituate - Hatherly Elementary School 8/7																
Total		9,625		\$ 821.4			\$ 665.0																		

Construction Manager at Risk Project CMR Project Pending Local Approval Filed Sub Bids

Design Bid Build Project DBB Project Pending Local Approval GC Bids/GMP Execution

The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.







Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

2026 ESTIMATED BID DATES

Note bid dates are Estimates ONLY. Please contact Districts for exact information.

November 17, 2023

District	School Type	Enrollment	Project Type	Project Budget	Start	Finish	Construction Budget	Notes	Dec '25	Jan '26	Feb '26	Mar '26	Apr '26	May '26	Jun '26	Jul '26	Aug '26	Sep '26	Oct '26	Nov '26	Dec '26
Berkley	ES	385	New		Thu 1/22/26	Thu 1/22/26		NTP targeted: January 2026		Berkley Community School											
										◆											
Total		385																			

Construction Manager at Risk Project  CMR Project Pending Local Approval  Filed Sub Bids 
 Design Bid Build Project  DBB Project Pending Local Approval  GC Bids/GMP Execution 


The project start date represents the Filed-Sub bid solicitation date, the gray diamond Filed-Sub bid date, and the black diamond GC Bids / GMP Execution.

Projects represented by a single black diamond have not completed a Schematic Design Submission.

Project Budget denotes total District costs, not the basis of the MSBA Total Facilities Grant. Projects without budget information have not received Project Scope and Budget approval. Note: Budget values are in millions.

APPENDIX C
SCHOOL CONSTRUCTION COSTS COMPARED
TO COMMON ECONOMIC INDICATORS

New Construction Costs Compared to Common Economic Indicators | November 17, 2023

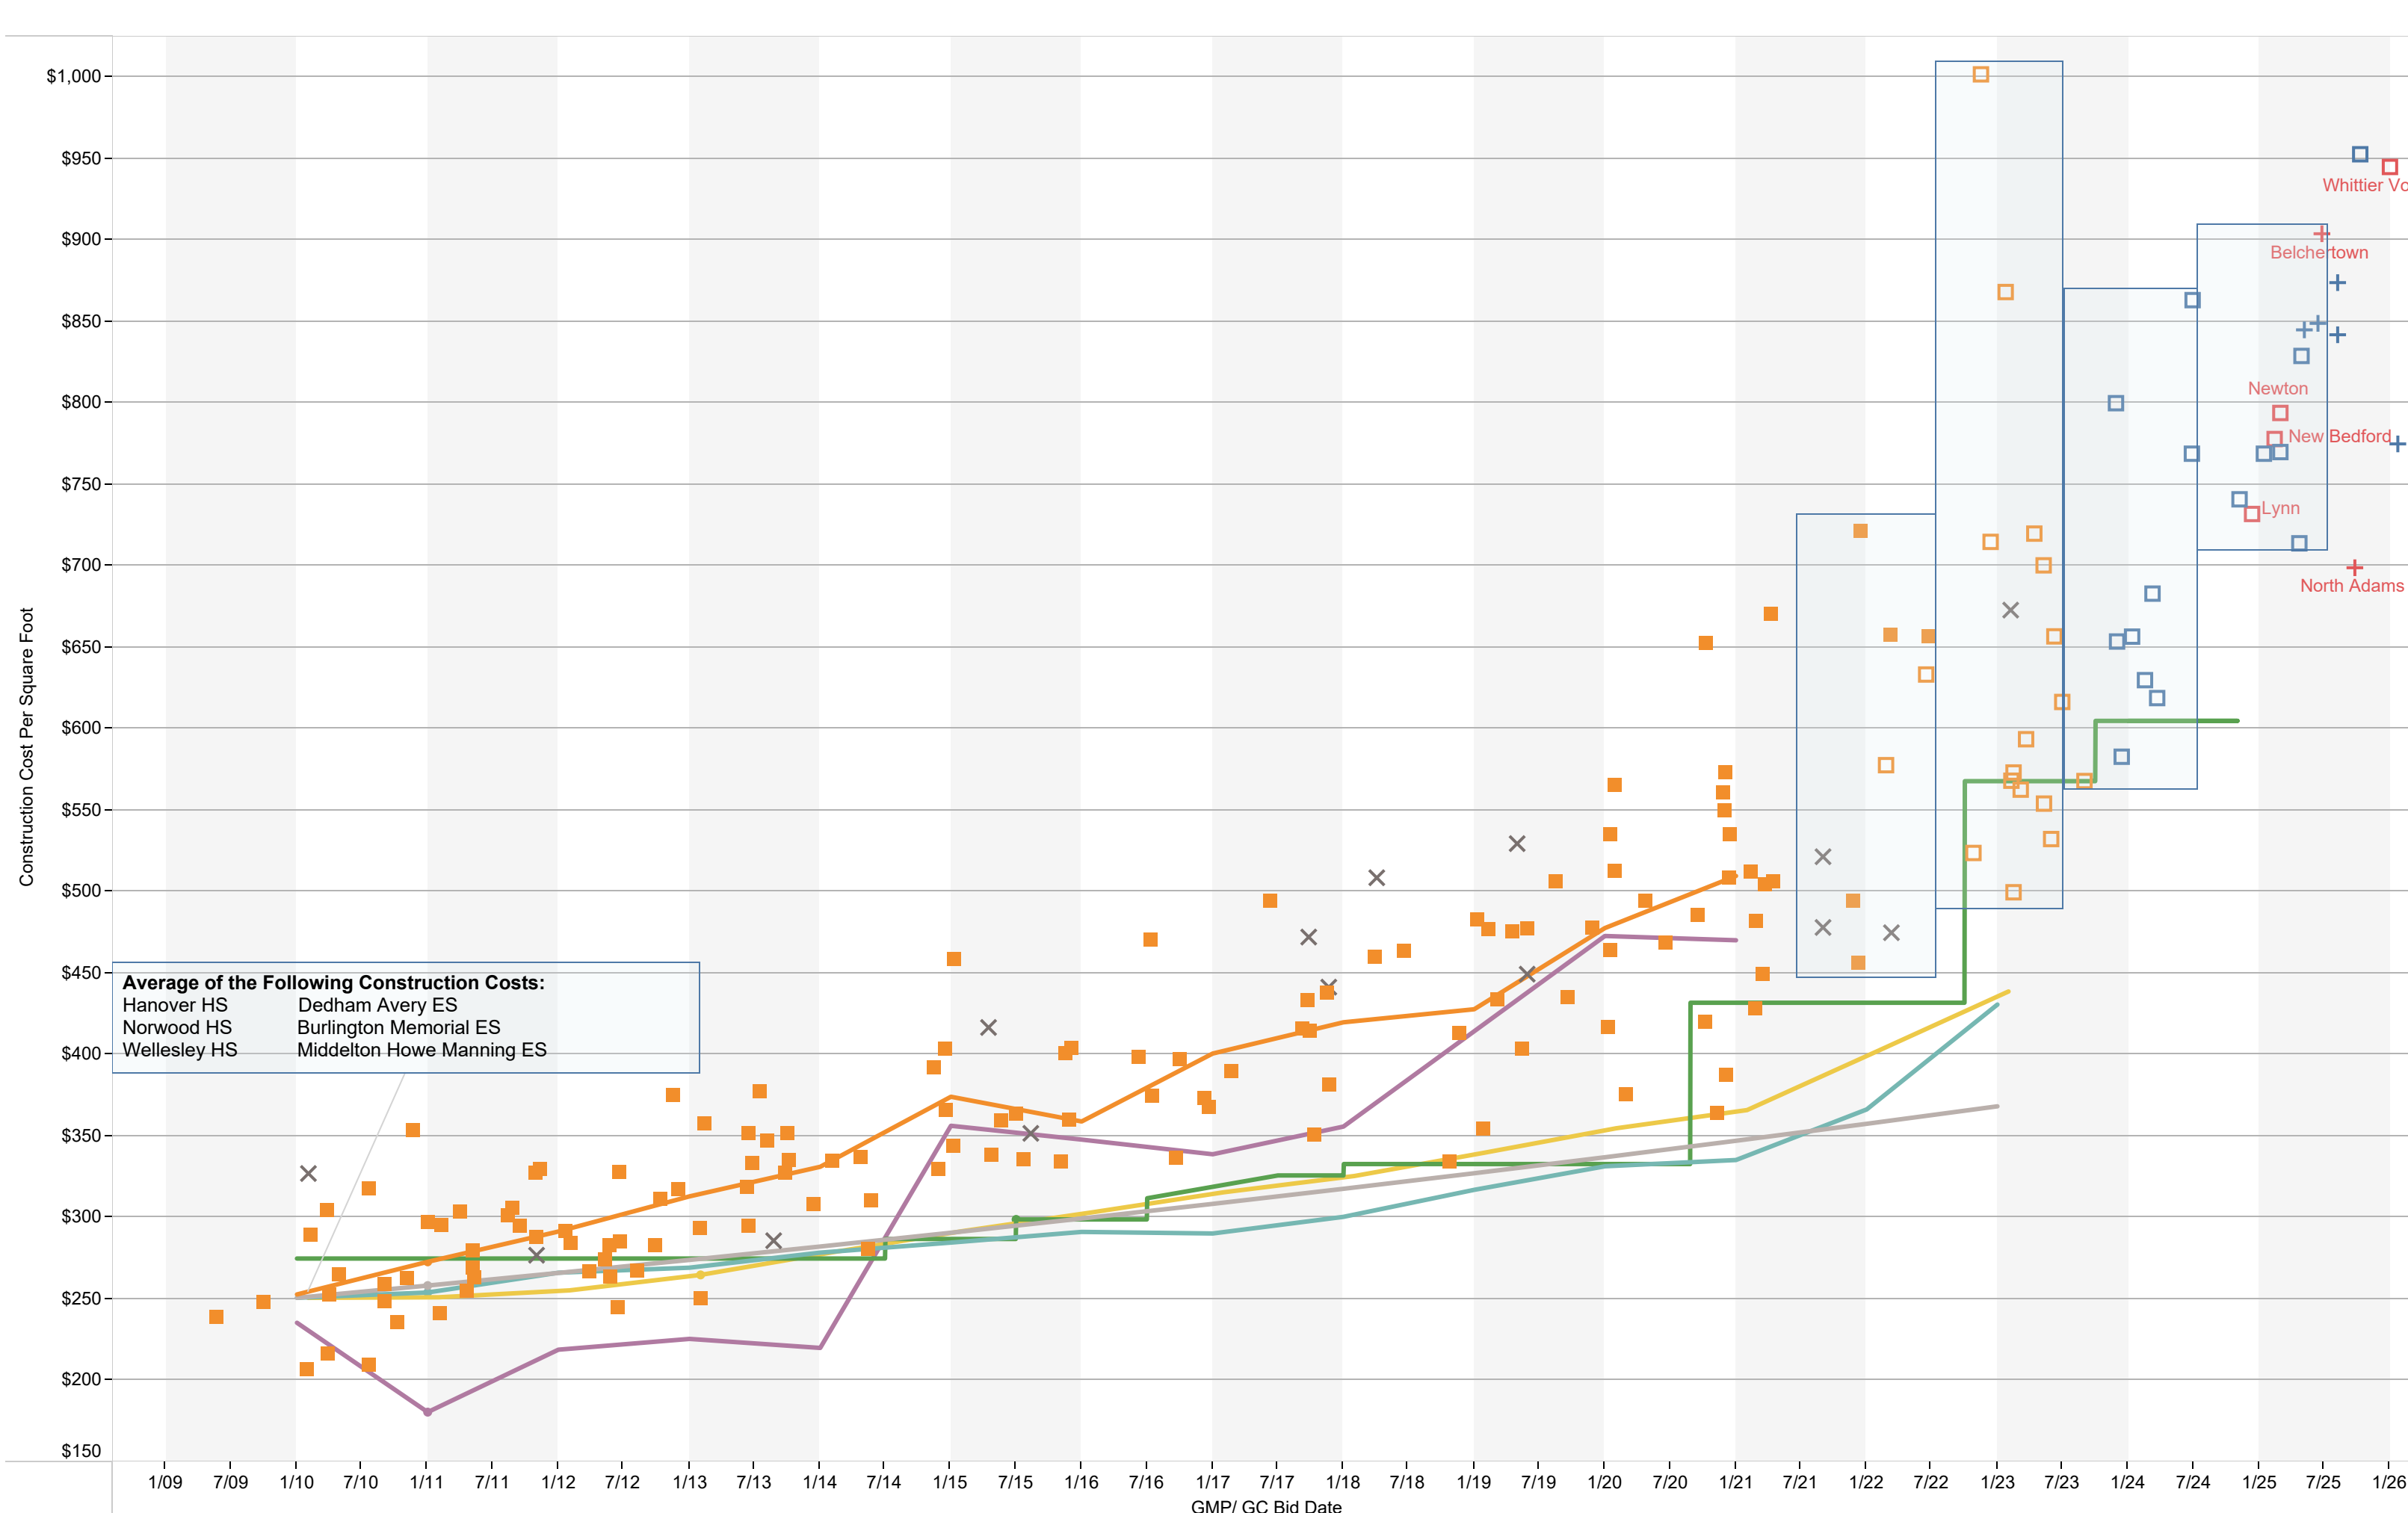

- Legend**
- New Construction PSR +
 - New Construction PSR - Board Vote +
 - New Construction SD
 - New Construction SD Board Vote
 - New Construction Vote Failed ×
 - New Construction Bid
 - New Construction PFA Amended
 - 3% Escalation
 - Average- New Construction Projects
 - BLS PPI- New School Construction
 - MSBA Construction Funding Limit
 - RLB Comparative Cost- Boston
 - Average \$/SF for Add/Reno


Average of the Following Construction Costs:
 Hanover HS Dedham Avery ES
 Norwood HS Burlington Memorial ES
 Wellesley HS Middleton Howe Manning ES

The information and data contained in this chart is based on the MSBA's review of construction cost estimates, contracts and other documentation provided by cities, towns, and regional school districts.

This information and data is intended for informational purposes only. The data may have changed based on actual construction bids or contract amendments, for example, and the MSBA shall have no responsibility or duty to update any of the information.

Please contact the Districts for the most current information. The MSBA hereby disclaims any and all liability and responsibility that may arise in connection with the information contained in this chart. (Updated November 2023)

Addition/Renovation Costs Compared to Common Economic Indicators | November 17, 2023

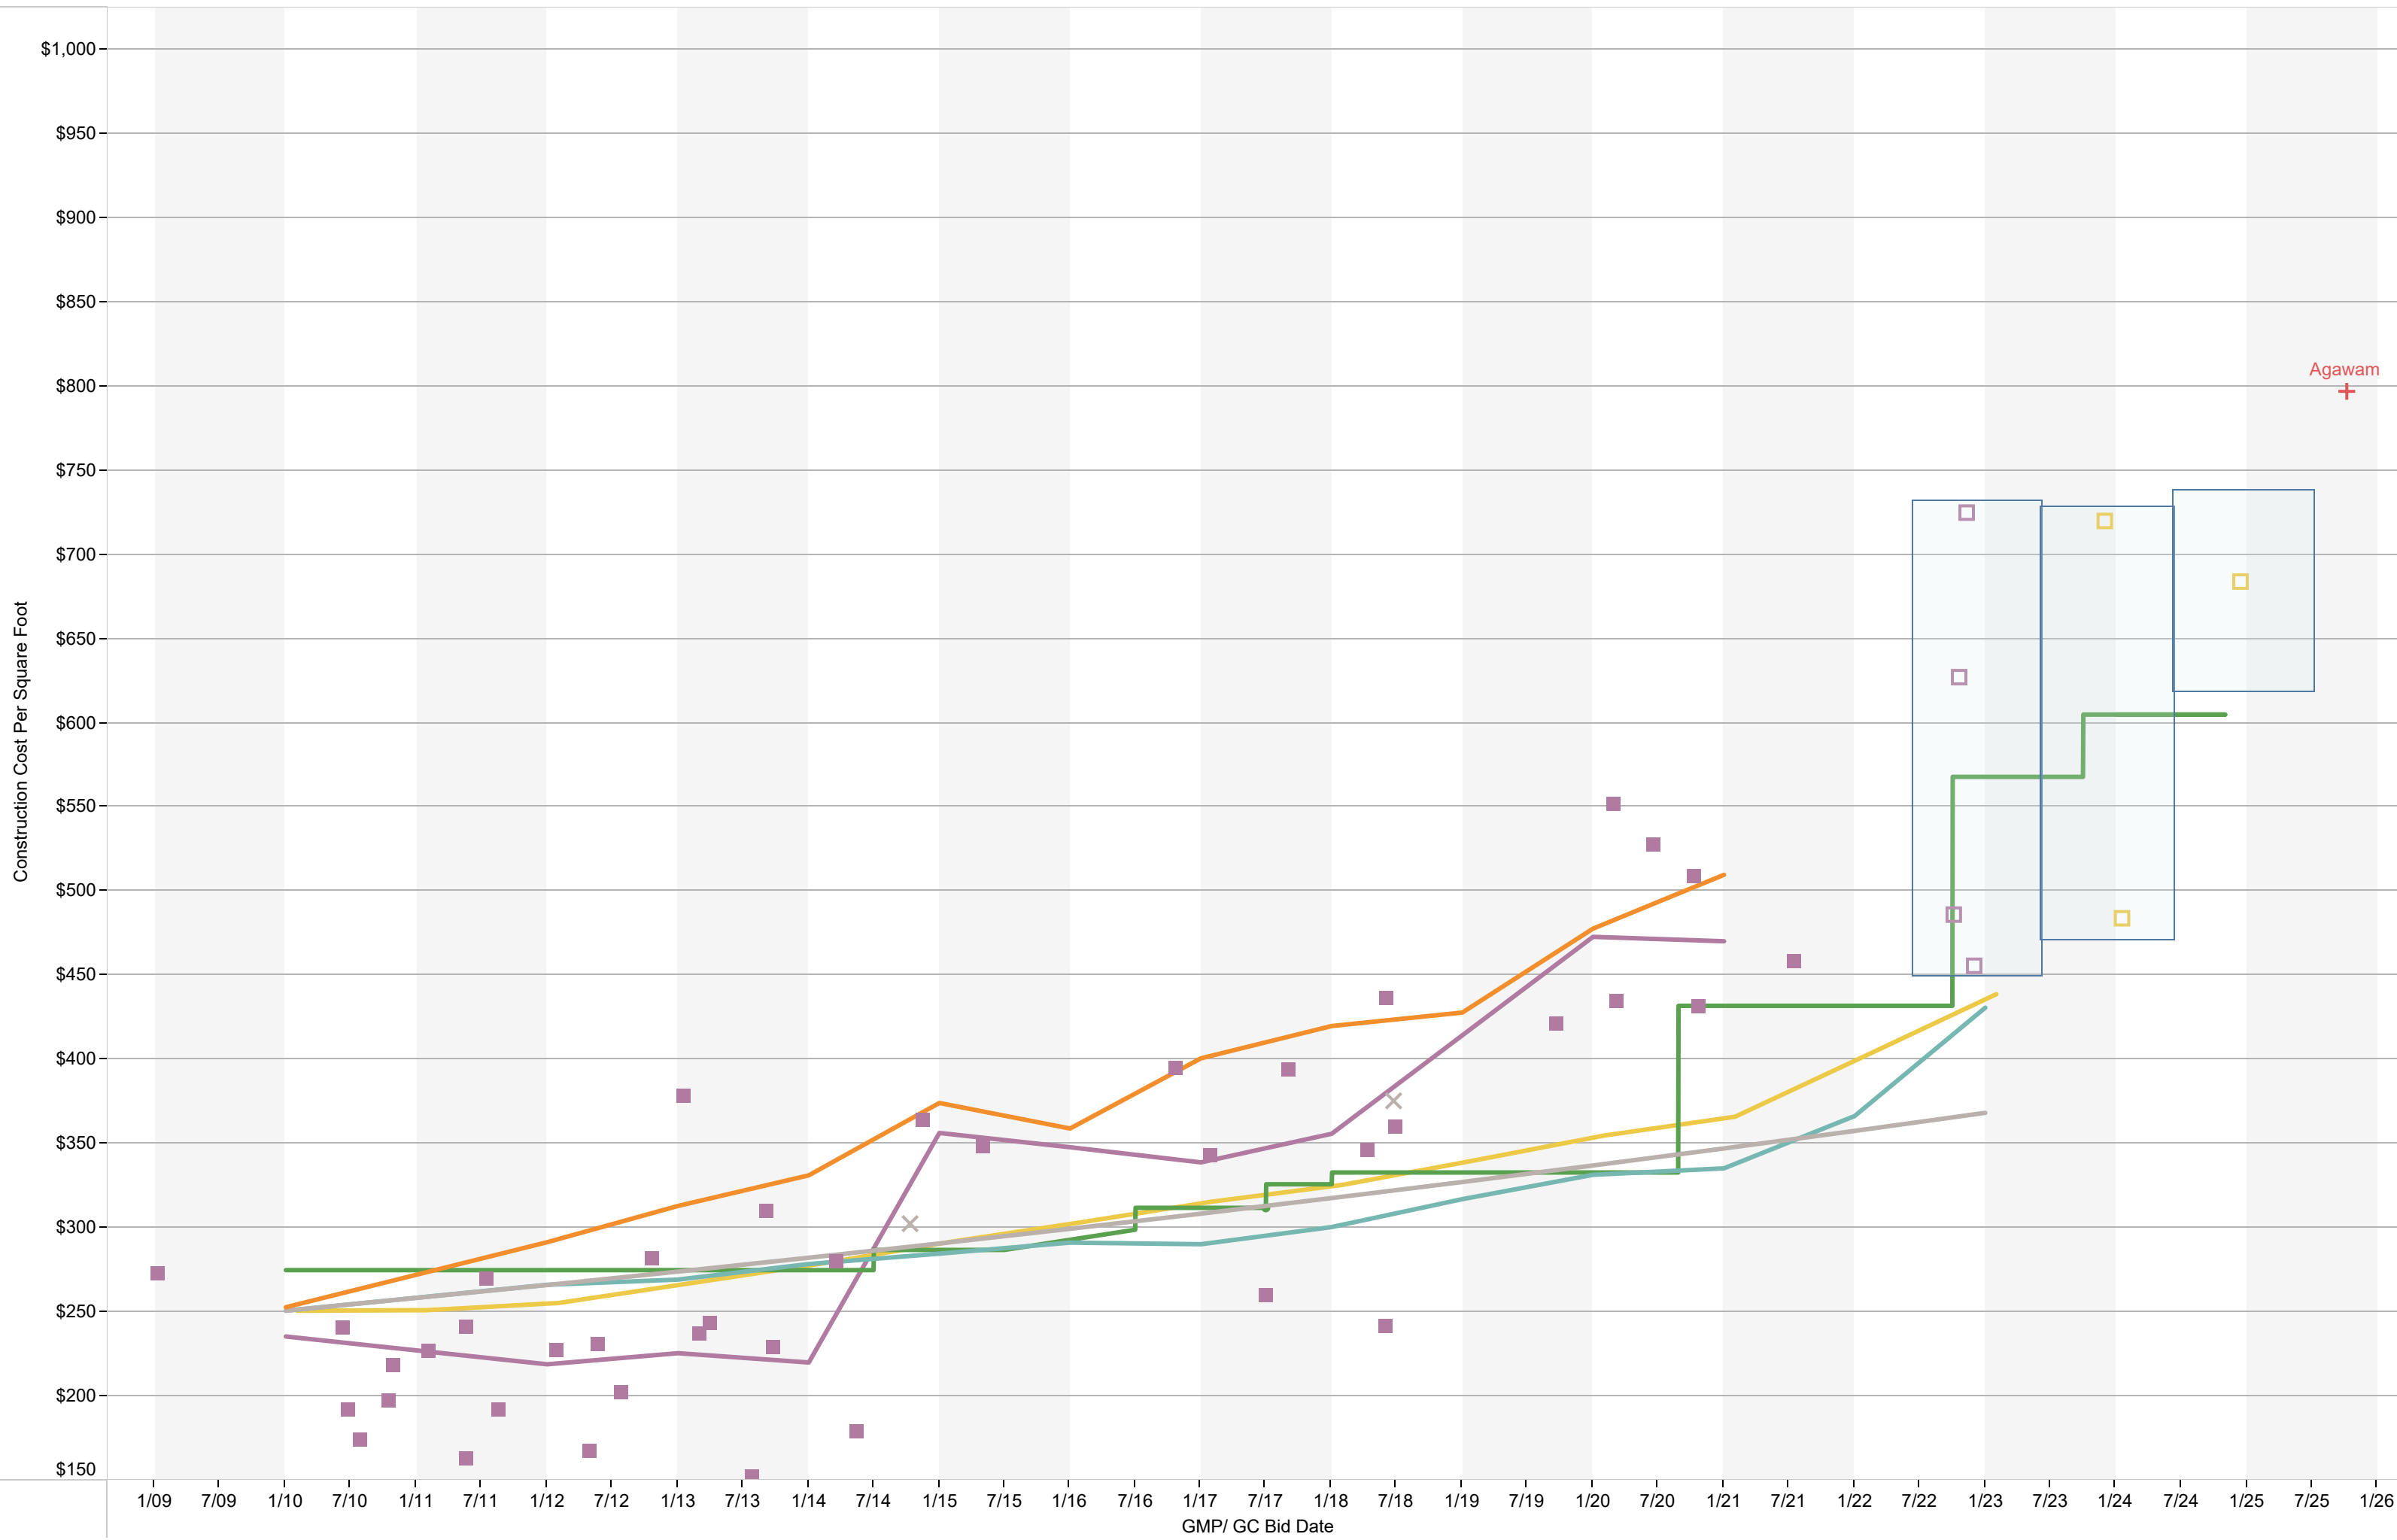

Legend


- Addition / Renovation SD □
- Addition / Renovation Bid □
- Addition / Renovation PFA Amended ■
- Addition / Renovation Vote Failed ×
- Addition / Renovation PSR Board Vote +
- 3% Escalation —
- Average- New Construction Projects —
- BLS PPI- New School Construction —
- MSBA Construction Funding Limit —
- RLB Comparative Cost- Boston —
- Average \$/SF for Add/Reno —

The information and data contained in this chart is based on the MSBA's review of construction cost estimates, contracts and other documentation provided by cities, towns, and regional school districts.

This information and data is intended for informational purposes only. The data may have changed based on actual construction bids or contract amendments, for example, and the MSBA shall have no responsibility or duty to update any of the information.

Please contact the Districts for the most current information. The MSBA hereby disclaims any and all liability and responsibility that may arise in connection with the information contained in this chart. (Updated November 2023)

Projects Below \$150/ SF

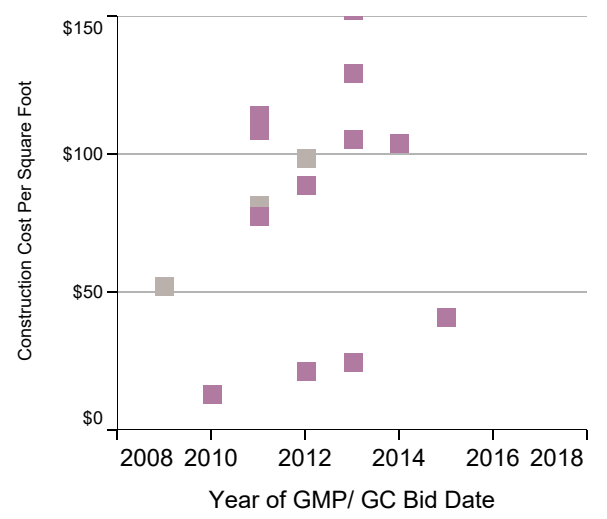

APPENDIX D
CONSTRUCTION STATUS REPORT

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of November 14, 2023**

Core Program and Waitlist Totals			\$6,264,645,890															*Includes Alternates	\$3,020,642,386
Project	Grade	Contractor	Total Construction Cost*	Projected Enrollment	PFA or Bid Data	SD Gross Sq.Ft.	Construction Cost/Sq.Ft.	Building Cost	Building Cost/Sq.Ft.	Procurement Type	Construction Start Date	Substantial Completion Date *	Building Construction Complete **	Schedule Variance (days) ***	Physical Progress	Change Orders	Change Orders %	Construction Status	Est Max Total Facilities Grant
CAPITAL PIPELINE PROJECTS IN CONSTRUCTION																			
Core Program Totals			\$6,264,645,890																\$3,020,642,386
Amesbury Amesbury Elementary	Elementary School	CTA Construction Co., Inc.	\$48,976,932	425	Bid	98,195	\$499	\$31,212,190	\$318	Design/Bid/Build	17-May-21	17-Feb-23	02-Aug-23	166 behind	98%	\$563,006	1.150%	Site work activities include punch list work. Building interior activities include mechanical control wiring and systems balancing, formal commissioning, installation of the sliding glass door system at the reception desk, and punch list work.	\$24,150,576
Braintree South Middle School	Middle School	Bacon Construction Co, Inc.	\$69,181,416	800	Bid	145,846	\$474	\$47,780,677	\$328	Design/Bid/Build	10-Jan-22	30-Jun-23	1-Sep-23	63 behind	99%	\$952,255	1.377%	Building interior and exterior activities include ongoing efforts to complete punch list items.	\$30,967,468
Bridgewater-Raynham Mitchell Elementary School	Elementary School	Bacon Construction Co, Inc.	\$51,185,151	740	Bid	132,045	\$388	\$38,763,609	\$294	Design/Bid/Build	01-Feb-21	15-Aug-22		0	99%	\$1,260,635	2.463%	Work on punch list items, warranty items, system testing, trainings, and corrective items continues.	\$32,319,411
Bristol-Plymouth Regional Voc Tech	Vocational/Technical	Consigli Construction Company, Inc.	\$240,885,538	1,434	PFA	419,765	\$574	\$152,567,448	\$363	Design/Bid/Build	1-Jun-22	26-May-26		0	2%	\$0	0.000%	Sitework activities include surveying and site fencing installation.	\$123,320,490
Dennis-Yarmouth Mattacheese Middle	Middle School	Commodore Builders Corporation	\$83,843,640	940	Bid	186,500	\$451	\$69,813,633	\$376	Design/Bid/Build	02-Apr-21	14-Oct-22	16-Feb-23	125 behind	99%	\$8,283,775	9.880%	Building exterior and interior activities include punch list work.	\$44,383,043
Easthampton Maple	Elementary School	Fontaine Brothers, Inc.	\$84,831,000	1,010	Bid	177,370	\$478	\$66,350,569	\$374	Design/Bid/Build	04-Dec-19	01-Mar-22	15-Apr-22	45 behind	99%	\$3,413,592	4.207%	Construction activity includes punch list work and verification of commissioning item completion.	\$48,274,725
Easton Center School	Elementary School	Brait Builders Corp.	\$74,886,581	760	Bid	148,422	\$505	\$48,090,933	\$324	Design/Bid/Build	11-Mar-21	14-Oct-22	20-Dec-22	67 behind	99%	\$2,151,065	2.872%	Site work activities include installation of pavement markings, maintenance of landscaping, and punch list work. Building interior activities included work on punch list items.	\$34,212,027
Fitchburg Crocker Elementary	Elementary School	Fontaine Brothers, Inc.	\$49,774,500	845	PFA	115,788	\$430	\$34,626,300	\$299	Design/Bid/Build	23-Mar-23	01-Feb-25		0	12%	\$216,170	0.434%	Building activities include concrete building foundation excavation and installation, underground plumbing piping installation, and structural steel erection.	\$42,248,583
Foxborough Mabelle M Burrell	Elementary School	CTA Construction Co., Inc.	\$25,900,000	270	Bid	61,455	\$421	\$19,880,255	\$323	Design/Bid/Build	14-Nov-19	15-Aug-21	26-Aug-21	11 behind	99%	\$819,747	3.165%	Building interior and exterior activities include punch list work and corrective work.	\$14,656,301
Gardner Waterford Street	Elementary School	Bacon Construction Co, Inc.	\$61,556,403	925	Bid	147,120	\$418	\$45,982,650	\$313	Design/Bid/Build	15-Oct-20	12-Sep-22	12-Sep-22	0	99%	\$3,524,566	5.726%	Sitework activities include parking lot improvements and preparation for final playground surfacing. Building exterior and interior activities include punch list and change order work.	\$49,199,470
Hingham Wm L Foster Elementary	Elementary School	Bacon Construction Co, Inc.	\$88,114,851	605	PFA	126,385	\$697	\$51,009,185	\$404	Design/Bid/Build	22-Nov-22	16-May-25		0	10%	\$76,530	0.087%	Building activities included completion of concrete foundations and ongoing structural steel progress.	\$24,582,732
Lawrence Francis M Leahy	Elementary School	J&J Contractors, Inc.	\$81,846,297	1,000	PFA	173,520	\$472	\$58,039,366	\$334	Design/Bid/Build	18-Sep-23	25-Nov-24		0	1%	\$0	0.00%	Early site work includes installation of underground utilities, and concrete foundation placements.	\$60,308,143
Middleborough Middleborough High	High School	Fontaine Brothers, Inc.	\$79,515,000	720	Bid	166,650	\$477	\$60,188,611	\$361	Design/Bid/Build	19-Feb-19	05-Feb-21	16-Apr-21	70 behind	99%	\$2,278,165	2.888%	Construction activities include completion of all remaining punch list items.	\$41,968,750
Millbury Raymond E. Shaw Elementary	Elementary School	Fontaine Brothers, Inc.	\$44,482,548	550	Bid	90,266	\$493	\$32,607,259	\$361	Design/Bid/Build	24-Feb-21	29-Jul-22	29-Jul-22	0	99%	\$2,572,535	5.783%	Building exterior and interior activities include progress on punch list items.	\$23,937,157
Natick J F Kennedy Middle	Middle School	Brait Builders Corp.	\$79,110,300	1,000	Bid	182,195	\$434	\$64,167,247	\$352	Design/Bid/Build	19-Mar-19	11-Dec-20	11-Dec-20	0	99%	\$2,675,827	3.382%	Building interior and exterior activities include progress on punch list items.	\$36,501,996
Nauset Nauset Regional High	High School	Brait Builders Corp.	\$104,708,165	905	PFA	214,250	\$489	\$68,244,805	\$319	Design/Bid/Build	13-Jan-23	28-Feb-26		0	32%	\$3,448,290	3.293%	Site work activities include site lighting and drain installation, retaining walls, and paving the parking lot. Building exterior work include installation of wall sheathing and air/vapor barrier. Building interior include mechanical/electrical/plumbing installations, concrete slab on grade, and wall framing.	\$35,572,564
Orange Dexter Park	Elementary School	J & J Contractors, Inc.	\$45,730,728	520	Bid	97,115	\$471	\$25,795,276	\$266	Design/Bid/Build	21-Jul-21	25-Aug-23		0	95%	\$2,112,786	4.620%	Site work includes road and sidewalk paving. Building exterior includes abatement and demolition of the existing building. Building interior activities includes millwork and other finishes installation, stage and gymnasium flooring, and final cleaning.	\$33,110,916
Randolph Elizabeth G Lyons Elementary	Elementary School	Agostini Construction Co., Inc.	\$41,576,611	315	PFA	74,720	\$556	\$25,567,307	\$342	Design/Bid/Build	01-Mar-23	28-Jul-24		0	38%	\$626,207	1.506%	Site work activities include perimeter road paving and retaining wall installation. Building exterior activities include sheathing and roof screen installation. Building interior activities include mechanical, electrical and plumbing and fire protection rough-ins and framing, slab on grade concrete placements.	\$27,059,330
Rockland Jefferson Elementary School	Elementary School	Brait Builders Corp.	\$68,549,754	760	Bid	120,672	\$568	\$39,624,932	\$328	Design/Bid/Build	31-Mar-21	22-Dec-22	22-Dec-22	0	97%	\$1,104,501	1.611%	Site work activities consist of preparation for demolition of the existing building. Building exterior and interior work include punch item completions.	\$34,200,179
Swampscott Hadley	Elementary School	CTA Construction Co., Inc.	\$77,937,159	900	PFA	153,855	\$507	\$50,931,200	\$331	Design/Bid/Build	21-Nov-22	01-Jul-24		0	47%	\$1,531,486	1.965%	Site work activities include installation of permanent transformers. Building exterior activities include installation of roofing, and exterior wall framing and sheathing. Building interior work include heating/ventilation/air conditioning and plumbing installations throughout the building.	\$33,818,941
Wareham Minot Forest	Elementary School	Bacon Construction Co, Inc.	\$60,117,573	1,020	Bid	159,989	\$376	\$46,317,213	\$290	Design/Bid/Build	01-Mar-20	15-Oct-21	05-Nov-21	21 behind	99%	\$1,874,786	3.119%	Minor warranty work being performed.	\$50,328,204
Watertown Watertown High	High School	Brait Builders Corp.	\$138,651,235	720	PFA	258,914	\$536	\$94,057,895	\$363	Design/Bid/Build	25-Sep-23	02-Mar-26		0	1%	\$0	0.000%	Site work activities include contractor mobilization and site preparation. Building construction activities include building abatement.	\$44,283,365
West Springfield Philip G Coburn	Elementary School	Fontaine Brothers, Inc.	\$43,537,700	585	Bid	119,800	\$363	\$36,372,700	\$304	Design/Bid/Build	19-Nov-20	22-Jul-22	30-Aug-22	39 behind	99%	\$1,351,264	3.104%	Building exterior and interior activities include work on punch list items.	\$38,446,369
Westfield Franklin Ave	Elementary School	Fontaine Brothers, Inc.	\$50,430,464	395	PFA	88,495	\$570	\$38,496,029	\$435	Design/Bid/Build	10-Apr-23	27-May-25		0	39%	\$110,524	0.219%	Building exterior activities include roof installation and exterior wall framing. Building interior work include HVAC ductwork and roof drain piping, fireproofing installation, and masonry wall construction.	\$30,562,787
Westwood Paul Hanlon	Elementary School	Brait Builders Corp.	\$70,380,680	560	Bid	113,141	\$622	\$43,765,081	\$387	Design/Bid/Build	20-Jul-22	03-Jan-24		0	86%	\$706,026	1.003%	Site work includes paving installation, landscaping, and playground installation. Building exterior work includes roof edge installation. Building interior work includes mechanical/electrical/plumbing installations, and finish work including flooring installations, millwork, and casework. Installation of the emergency generator is ongoing.	\$17,609,759
Acton-Boxborough C.T. Douglas Elementary	Elementary School	Consigli Construction Company, Inc.	\$88,737,490	990	Bid	174,759	\$508	\$55,519,573	\$318	CM-at-Risk	24-Jun-20	01-Jul-22	26-Aug-22	56 behind	99%	\$5,705,953	6.430%	Site work and building exterior and interior activities consist of ongoing efforts to complete punch list items.	\$36,764,631
Andover West Elementary	Elementary School	Gilbane Building Company	\$119,178,907	925	Bid	191,028	\$624	\$72,338,002	\$379	CM-at-Risk	02-Jun-22	20-Aug-24		0	39%	\$345,058	0.290%	Building exterior activities include masonry wall installation, roofing insulation, and exterior wall and sheathing. Building interior activities include mechanical/electrical/plumbing rough-ins, wall framing and drywall installation.	\$37,022,178
Arlington Arlington High	High School	Consigli Construction Company, Inc.	\$234,287,346	1,755	Bid	408,590	\$573	\$161,482,636	\$395	CM-at-Risk	09-Apr-19	05-May-25		0	76%	\$2,088,540	0.891%	Building exterior activities include wall framing and veneer installation. Building interior activities include elevator installation, kitchen equipment, and finish installation including flooring, lockers, millwork, painting, tile work, and lighting fixtures.	\$82,637,254
Ashland David Mindess	Elementary School	Shawmut Design and Construction	\$67,725,296	635	Bid	104,885	\$646	\$37,389,325	\$356	CM-at-Risk	29-Nov-21	17-Jul-23	07-Aug-23	21 behind	95%	\$1,792,880	2.647%	Sitework activities include work on drainage and ball fields, landscaping, bus drop off loop, and playground installation.	\$25,666,380
Attleboro Attleboro High	High School	Consigli Construction Company, Inc.	\$223,088,312	1,725	Bid	476,425	\$468	\$147,727,880	\$310	CM-at-Risk	13-May-19	15-Aug-22	15-Aug-22	0	98%	\$1,073,309	0.481%	Site work activities include development of athletic fields, preparation of sod installation, preparation of tennis courts for final surfacing, irrigation, hydroseeding, and final pavement marking. Building interior and exterior activities include punch list work.	\$122,638,496
Belmont Belmont High	High School	Skanska USA Building, Inc.	\$239,790,693	2,215	Bid	445,100	\$539	\$160,111,108	\$360	CM-at-Risk	10-Jun-19	21-Jul-23	15-Aug-23	25 behind	99%	\$16,619,471	6.931%	Site work activities include final landscaping. Building interior activities include mechanical, electrical, plumbing system balancing and startup, testing, commissioning of mechanical work and punch list work.	\$76,864,025
Boston Boston Arts Academy	High School	Lee Kennedy Co., Inc.	\$102,921,915	500	Bid	153,476	\$671	\$71,742,646	\$467	CM-at-Risk	17-Dec-18	04-Apr-22	29-Aug-22	147 behind	98%	\$13,980,557	13.584%	Building interior activities include punch list work.	\$46,971,048
Boston Carter Developmental Center	Middle/High School	Bond Brothers, Inc.	\$68,888,383	60	PFA	86,130	\$800	\$44,248,438	\$514	CM-at-Risk	8-Sep-22	07-Mar-25		0	14%	\$0	0.000%	Site work activities include excavating, preparing sub-grade and backfilling. Building exterior activities include building formwork, placing concrete, installing damp proofing, installing lightning protection, underground electrical conduit, installing underground plumbing and associated through wall pipe, and installing underground pool piping.	\$25,606,126
Boston Quincy Upper School	Middle/High School	Turner Construction Company	\$146,812,305	650	PFA	178,024	\$825	\$101,359,804	\$569	CM-at-Risk	17-Jan-22	18-Jun-24		0	58%	\$0	0.000%	Building exterior activities include scaffolding, window framing and glazing. Building interior activities include electrical and telecom raceways and cabling, mechanical piping, ductwork, interior wall framing, wallboard installation and taping, and switchgear installation.	\$52,139,805
Gloucester East Gloucester Elementary	Elementary School	W. T. Rich Company Inc.	\$51,925,531	440	PFA	90,461	\$574	\$0	\$0	CM-at-Risk	02-Aug-21	28-Aug-23	28-Aug-23	0	98%	\$570,732	1.099%	Site work activities include final landscaping. Building interior activities include mechanical, electrical, plumbing system balancing and startup, testing, commissioning of mechanical work and punch list work.	\$25,496,634
Greater Fall River Regional Diman Regional Voc Tech High	Vocational/Technical	Suffolk Construction Company	\$242,300,294	1,500	PFA	394,650	\$614	\$151,180,200	\$383	CM-at-Risk	30-Oct-23	1-Jul-26		0	1%	\$0	0.000%	Site work activities include mobilization of the project site.	\$148,671,938
Groton-Dunstable Florence Roche	Elementary School	Gilbane Building Company	\$61,541,339	645	PFA	109,855	\$560	\$36,686,920	\$334	CM-at-Risk	19-Aug-22	15-Apr-24		0	55%	\$961,552	1.562%	Site work activities include erosion control. Building exterior activities include ongoing window and roofing installation. Interior building activities include installation of door frames, inwall and above ceiling mechanical, electrical, plumbing and fire protection work, and drywall and taping installation on the 1st and 2nd floors.	\$25,835,473

**Projects in Construction
MSBA Grant Basis and Maximum Grant Amount
Data Reported as of November 14, 2023**

Lawrence Henry K Oliver	K-8	Consigli Construction Company, Inc.	\$104,899,839	1,000	PFA	162,000	\$648	\$69,122,675	\$427	CM-at-Risk	12-Jan-22	30-Oct-24		0	28%	\$798,668	0.761%	Building exterior activities include underground plumbing installation, Air Vapor Barrier, window installation, steel erection, and slab placement is ongoing. Building interior activities include spray fireproofing.	\$58,290,756
Lowell Lowell High	High School	Suffolk Construction Company	\$270,444,856	3,520	PFA	622,777	\$434	\$174,614,719	\$280	CM-at-Risk	02-Mar-21	04-May-26		0	44%	\$3,528,734	1.305%	Site work activities include drainage and utilities. Building exterior activities include curtainwall installation, roofing, and masonry. Building interior activities include elevator installation, framing, fireproofing, rough mechanical, electrical, and plumbing, drywall, painting and tile.	\$210,023,036
Manchester Essex Regional Manchester Memorial Elementary	Elementary School	W. T. Rich Company Inc.	\$41,142,103	335	Bid	77,102	\$534	\$27,710,731	\$359	CM-at-Risk	29-Jul-19	06-Aug-21	13-Aug-21	7 behind	99%	\$1,656,010	4.025%	Site work activities include landscaping, plantings, main playground installation and punch list. Building interior and exterior activities include completing the punch list.	\$12,312,861
Northeast Metropolitan Regional Voc Tech Northeast Metro Reg Voc	Vocational/Technical	Gilbane Building Company	\$243,591,092	1,600	PFA	386,630	\$630	\$135,512,106	\$350	CM-at-Risk	25-Oct-23	07-May-26		0	2%	\$0	0.000%	Site work activities include ledge blasting and clearing.	\$138,044,288
Norwood Dr. Philip O. Coakley Middle School	Middle School	W. T. Rich Company Inc.	\$119,499,563	1,070	PFA	187,840	\$636	\$71,676,813	\$382	CM-at-Risk	08-Jun-23	13-Jun-25		0	11%	\$682,758	0.600%	Building exterior activities include foundation footings, walls, piers, steel preparation, under slab mechanical, electrical and plumbing work is ongoing.	\$45,331,282
Peabody William A Welch Sr	Elementary School	Consigli Construction Company, Inc.	\$23,348,836	390	PFA	59,025	\$396	\$14,265,517	\$242	CM-at-Risk	17-May-22	31-Oct-23		0	86%	\$480,192	2.057%	Site work activities include hard packing the basketball court and walkways. Building interior activities include completing punch list work.	\$17,184,400
Pentucket Regional Sr High	High School	Rich-KBE Pentucket School Joint Venture	\$118,540,836	965	Bid	211,700	\$560	\$72,676,646	\$343	CM-at-Risk	22-Apr-20	31-Jul-22	31-Jul-22	0	91%	\$3,505,251	2.957%	Site work activities include final landscaping. Building interior activities include mechanical system balancing as well as startup, testing, and commissioning of mechanical work, and punch list work.	\$52,092,194
Sharon Sharon High	High School	Consigli Construction Company, Inc.	\$125,792,153	1,250	Bid	240,204	\$524	\$79,741,218	\$332	CM-at-Risk	14-Aug-20	25-Aug-22	25-Aug-22	0	98%	\$2,852,017	2.267%	Site work activities include final landscaping. Building interior activities include mechanical, electrical, plumbing system balancing and startup, testing, commissioning of mechanical work, and punch list work.	\$49,628,362
Somerset Somerset Middle School	Middle School	Brait Builders Corp.	\$69,956,365	590	PFA	124,200	\$563	\$44,955,581	\$362	CM-at-Risk	22-Dec-22	31-May-24		0	54%	\$404,222	0.586%	Site work activities include pavement preparation and binder installation, and installation of the gas service. Building exterior activities include siding, exterior masonry, cement board and storefront installation. Building interior activities include mechanical, electrical, and plumbing rough-ins, drywall installation, fire protection, acoustical ceiling grid and painting.	\$30,759,152
Somerville Somerville High	High School	Suffolk Construction Company	\$203,912,277	1,590	Bid	369,496	\$552	\$142,493,522	\$386	CM-at-Risk	12-Jun-17	15-Mar-20	22-Feb-21	252 behind	99%	\$40,307,389	19.767%	Site work activities include contaminated soil export off the site, placement of concrete driveways, sidewalks, and plaza areas, water, sewer, and drain utility installations continued, perimeter drain installation at the field. Building interior and exterior activities include punch list and corrective work.	\$118,275,833
Spencer-E Brookfield David Prouty High	High School	Fontaine Brothers, Inc.	\$91,217,674	305	PFA	126,823	\$719	\$49,027,362	\$387	CM-at-Risk	26-Jun-23	14-Aug-26		0	20%	\$0	0.000%	Site work activities include site drainage installation, site utility work, and access road installation to upper athletic fields. Building exterior activities include excavation and forming of building perimeter footings.	\$44,790,070
Springfield William N Deberry	Elementary School	Fontaine Brothers, Inc.	\$76,956,270	800	Bid	155,990	\$493	\$58,294,282	\$374	CM-at-Risk	01-Jun-21	30-Jun-23		0	94%	\$590,541	0.767%	Site work activities include punch list items. Building interior and exterior activities include commissioning, training and punch list work.	\$52,770,493
Stoneham Stoneham High	High School	Consigli Construction Company, Inc.	\$153,418,660	695	PFA	207,077	\$741	\$79,549,347	\$384	CM-at-Risk	13-Oct-22	20-Dec-24		0	28%	\$1,312,449	0.856%	Site work activities include power and exterior duct work for temporary heaters. Building exterior activities include masonry, roof coping, Air Vapor Barrier installation. Building interior activities include overhead Heating, Ventilation and Air Conditioning, acoustic insulation, fireproofing, mechanical, electrical, and plumbing rough-ins, door frame installation, wall blocking, radiant and concrete flooring.	\$47,700,057
Tewksbury Louise Davy Trahan	Elementary School	Consigli Construction Company, Inc.	\$77,450,806	790	Bid	139,457	\$555	\$39,783,068	\$285	CM-at-Risk	29-Apr-20	28-Oct-22	28-Oct-22	0	99%	\$2,142,125	2.766%	Building interior and exterior activities include miscellaneous punch list work through out the building and miscellaneous warranty work.	\$31,190,956
Tyngsborough Tyngsborough Middle	Middle School	Fontaine Brothers, Inc.	\$65,755,571	480	PFA	112,784	\$583	\$40,881,533	\$362	CM-at-Risk	06-Jan-23	07-Aug-26		0	19%	\$0	0.000%	Building exterior activities include foundation installation and backfilling, Concrete Masonry Unit installation and concrete slab placement.	\$28,058,982
Walpole Bird Middle	Middle School	Fontaine Brothers, Inc.	\$92,599,826	905	PFA	162,193	\$571	\$56,765,213	\$350	CM-at-Risk	26-Oct-22	01-Jul-24		0	47%	\$497,402	0.537%	Building exterior activities include window and curtainwall installation. Building interior activities include spray acoustic insulation and interior painting.	\$37,248,947
Waltham Waltham Sr High	High School	Consigli Construction Company, Inc.	\$298,923,790	1,830	Bid	414,854	\$721	\$192,973,827	\$465	CM-at-Risk	03-Jun-21	24-May-24		0	77%	\$1,879,536	0.629%	Site work activities include sidewalks, courtyard landscaping, asphalt installation at exit road, installation of site lighting and utilities at the garage. Building exterior activities include finishing metal panel installation and canopy facade work. Building interior activities include ceiling installation, tile and miscellaneous flooring installation, drywall installation at lower floors, painting is ongoing, acoustic panels in the Gym, and millwork installation.	\$118,207,106
Wellesley Ernest F Upham	Elementary School	Shawmut Design and Construction	\$55,569,898	365	PFA	80,039	\$694	\$30,661,753	\$383	CM-at-Risk	13-Apr-23	31-Jul-24		0	27%	\$0	0.000%	Site work activities include construction of new Route 9 access road. Building exterior activities include installation of underground plumbing and electrical, exterior wall framing, sheathing, Air Vapor Barrier, window blocking, curtainwall frame installation, roof blocking, parapet construction and roof membrane installation. Building interior activities include interior wall layout, framing, mechanical, electrical and plumbing rough-ins.	\$13,217,621
Westborough Annie E Fales	Elementary School	Gilbane Building Company	\$45,627,177	400	Bid	70,242	\$650	\$27,197,754	\$387	CM-at-Risk	17-Feb-20	14-Oct-21	14-Oct-21	0	98%	\$1,818,304	3.985%	Site work activities include landscape punch list. Building interior and exterior activities include commissioning.	\$15,469,934
Westport Westport Westport Junior/Senior High School	Middle/High School	Agostini Construction Co., Inc.	\$77,976,264	860	Bid	187,100	\$417	\$53,720,577	\$287	CM-at-Risk	15-Oct-18	02-Aug-21	02-Sep-21	31 behind	99%	\$3,109,140	3.987%	Building interior and exterior activities include punch list work and the completion of remaining commissioning items.	\$37,546,233
Weymouth Maria Weston Chapman Middle School	Middle School	Bond Brothers, Inc.	\$128,105,641	1,470	Bid	252,170	\$508	\$81,003,946	\$321	CM-at-Risk	30-May-20	01-Jul-22	22-Aug-22	52 behind	99%	\$2,309,423	1.803%	Sitework, building interior and exterior activities include completing commissioning and punch list work.	\$56,529,724
Worcester Doherty Memorial High	High School	Fontaine Brothers, Inc.	\$267,008,356	1,670	Bid	424,600	\$629	\$196,452,213	\$463	CM-at-Risk	27-Aug-21	06-Jun-24		0	67%	\$606,436	0.254%	Site work activities include installation of electrical equipment, switch pad and west side duct banks, courtyard stage, ramp and walls. Building interior activities include mechanical, electrical, plumbing, and fire protection rough-in, drywall installation and finishes.	\$123,632,825

Substantial Completion Date *
* Contract Substantial Completion Date. Field will remain blank until a contract/GMP has been executed.

Building Construction Complete **
** Field represents actual Substantial Completion date (date of Certificate of Completion).

Variance***
*** Variance is the difference between "Building Construction Completion" date and "Substantial Completion" Date. The number zero (0) will appear in this column until actual certificate of Substantial Completion is achieved.
